Community Based Sustainable Management of Tanguar Haor Project – Phase III (Consolidation)

Mid Term Review

Final Report

May 17, 2014

CONTENTS

		Page no
Contents		1
Abbreviations and Acronyms		2
Executive Summary		3
1	Background and Terms of Reference	4
2	The Tanguar Haor Ecosystem (THE)	6
3	Summary of the MTR Findings	9
4	Conclusions and Recommendations	13
5	Relevance of CBSMTHP to SDC Cooperation Strategy: Recommendations	29
6	Consolidation of Recommendations and Suggested Roles	37
Annexes		
A	Terms of Reference	42
B	Persons Met	48
C	Dhaka Meeting Schedules	50
D	Field Trip Schedule	52
E	References	54

Abbreviations and Acronyms

BCCSAP	Bangladesh Climate Change Strategy and Action Plan
CBOs	Community Based Organizations
CCC	Central Co-management Committee
CBSMTHP	Community Based Sustainable Management of Tanguar Haor Project
CNRS	Center for Natural Resources Studies
CREL	Climate Resilient Ecosystems and Livelihood
DFR	Draft Final Report
DP	Development Partners
GIZ	Deutsche Gesellschaft fur Internationale Zusammerarbeit
GOB	Government of Bangladesh
IPAC	Integrated Protected Area Co-management
IUCN	International Union for the Conservation of Nature
LGED	Local Government Engineering Department
MACH	Management of Aquatic Ecosystems through Community Husbandry
MOEF	Ministry of Environment and Forests
MOL	Ministry of Land
MTR	Mid-Term Review
NWN	National Wetland Network
NGOs	Non-Government Organizations
NSB	National Scientific Body
PSC	

- The incentives for the communities should be revisited during the preparation of the exit strategy (see Section 5 below).

The MTR Consultant concludes that the CBSMTHP performance in helping mobilize the AIGA and other economic opportunity enhancing efforts, secure communities' access rights to resources and modest attempts to understand the market challenges are reasonably good. Sustainability of these systems is going to be a serious issue and it should be a major focus for the remaining period.

The MTR Consultant recommends that:

- The wholesale idea of transferring the operation of the revolving fund to an existing MFI

FI

Restoration ecology is a complex technical area. The project has used the natural history of the area, supplemented by the baseline survey and one-off consultants' reports on fishery, forestry and reeds to make a judgment on the restoration process. This is perfectly alright. The concern that the Consultant has is the late start of the restoration process, which means that the project will end with no opportunity to monitor the establishment and success.

The project has demarcated, broadly, the water bodies into two divisions: (a) the core zone and (b) the buffer zone taking into account the ecosystem protection, habitat restoration and biodiversity conservation requirements. This demarcation is working well for identifying appropriate habitat restoration and sustainable resource harvesting interventions that the project is deploying. However, there is a clear dispute over the demarcation when it comes to identifying the THE boundary under official land tenure systems. Absence of a proper and officially approved boundary marking puts the entire resource management system at complete jeopardy.

The THE still does not have a comprehensive biodiversity assessment. IUCN Bangladesh Country Office has worked to leverage the Arannayk Foundation (Bangladesh Tropical Forest Conservation Foundation) to conduct an assessment. Once completed, the information will be valuable input to the CNSMTHP exit strategy.

The project has established a hydrological monitoring system and trained some community monitors to regularly monitor the water level. This is an essential aspect of understanding the seasonal changes and their impact on the ecosystem.

The Consultant concludes that ensuring the ecological sustainability of the project interventions are of most critical in nature and the project should spend considerable energy to devise an appropriate exit strategy. Some recommendations follow:

- The project should intensify the supervision of the community M&E process to make sure it works and continue to help the monitors refresh the training that they received.
- The project should make every effort to link the future SCM management to resource M&E.
- The CBSMTHP should look for other initiatives (such as USAID's CREL project) that have some presence in habitat restoration now. The community M&E may be linked with those initiatives in a formal manner.
- The boundary marking must be completed and approved not only to safeguard the beels from leasing, but also to help maintain the ecosystem's ecological integrity and productivity.
- Ecological restoration is a long-term process and monitoring plays a critical role. A time series of real time data will be essential to determine the improvement of the ecosystem. A long-term monitoring protocol should be established no matter whether the project will be extended beyond the planned period of June 2015. The community M&E may be a permanent agenda for the National Scientific Body. The other option will be to link them with a university or research institute.
- The hydrological monitoring system deserves a very serious attention. The monitoring protocol should be linked to an academic or research organization. The results shown in Figure 4 indicates a clear trend that historical water flow in a major river that traverses through the THE is decreasing steadily. This is alarming. If this trend continues, no external intervention will prove good enough to maintain the vitality of the ecosystem.

  This visible trend in decreased water flow into the THE indicates another broader aspect. Control of the water flow into the THE exists outside the geographical boundary of Bangladesh. This is; therefore, a transboundary issue and this cannot be dealt with within the current scope of the project or the current knowledge that exists on the THE. The CBSMTHP coordinating partner IUCN should flag this issue and

start discussing with its India and Regional Offices to find a way to initiate a dialogue with the Government of Meghalaya to commission, at the very least, a transboundary study. This is perhaps well beyond the scope of the project, but IUCN/Bangladesh should make the long-term monitoring of the THE a priority agenda under its core program, fund the study from its own resources and approach other DPs (including SDC) for support.

The CBSMTHP has planned a series of actions to ensure that it leaves behind a system, and a more aware, skilled and organized community with better economic and livelihoods opportunities to sustain the ecological integrity and productivity of the THE. A National Scientific Body (NSB), approved through a gazette notification, comprising of 8 members started working and they are providing scientific inputs for achieving project objectives. The planned National Wetland Network (NWN) was established and the network has already organized a national level meeting. The CBSMTHP has established a TH Information Center (THIC) at Sunamganj. Construction of a new dynamic and interactive web portal for knowledge management on the THE is under process to improve the existing knowledge portal.

The plan to establish the Tanguar Haor Management Authority (THMA) under an Act of the Parliament is a brilliant idea. The institutional nature of the proposed THMA will determine the flexibility and effectiveness of the institution. The CBSMTHP is currently working to develop a long-term management plan framework for the THE. The Consultant holds, but only in theory, a positive impression about the CBSMTHP's long-term institutional sustainability approach.

The MTR Consultant would offer the following recommendations that the project should consider seriously in the remainder of the Consolidation Phase:

x

The CBSMTHP objectives match very well with those of the SDC Cooperation Strategy. The CBSMTHP has been a long-term commitment for SDC. The Consultant commends the SDC for the way they have been incrementally supporting the development of a collaborative management, with the poor as central to the approach, of a significant ecosystem that has its influence on the ecology of a much larger area and the wellbeing of a large section of the ultra-poor. The Consultant strongly recommends that SDC considers keeping its engagements with the THE improvement as well as supporting the poor communities for another project cycle. This is too good to drop at this stage.

The Consolidation Phase is crucial since it is expected that the CBSMTHP will take into serious cognizance the MTR recommendations. Implementing the recommendations will require SDC's focused attention, particularly from the Project Manager and, intermittently, from the Head of Cooperation. The MTR Consultant recommends that:

- The SDC proactively convenes a meeting involving the Country Representative of IUCN Bangladesh Country Office and the Steering Committee to discuss the MTR recommendations and strategize priority actions.
- The SDC convenes a meeting involving like-minded DPs, preferably at the Heads of Agencies level, and have the CBSMTHP team present the project highlighting the importance of the THE, achievements thus far of the CBSMTHP and importance of continuing the process.
- The SDC Project Manager holds more frequent consultations with the CBSMTHP team to oversee the implementation of the priority actions.

The SDC has an advantageous role and a responsibility. Even if continuation of its involvement to improve the management of the THE for another project cycle does not meet SDC's new strategic priorities, the Consultant recommends that, at a minimum, the following be considered:

- Adding a supplementary fund to CBSMTHP to develop a THSAP.
    - Alternately, jointly with IUCN Bangladesh Country Office, approaching the Ramsar Secretariat to fund the process.
- Keeping a thematic focus based on the CBSMTHP achievements on the THE communities and the co-management organizations through other projects in the region.
- Leveraging support from other DPs (e.g., USAID through its CREL project and German Technical Cooperation who is facilitating a broader process to improve wetland management policies) to co-finance some priority areas identifi

1 Background and Terms of Reference (TOR)

1.1 The Report

The Swiss Agency for Development and Cooperation (SDC) deployed one independent Consultant[2] for the Mid Term Review (MTR) of the Consolidation Phase of an important project they have been funding since 2006, "Community Based Sustainable Management of Tanguar Haor Project" (CBSMTHP). The project is being implemented by the International Union for the Conservation of Nature (IUCN) Bangladesh Country Office

- A final report containing the presentation of findings and recommendations focusing on:
    - Adjustment of interventions to improve performance within the consolidation phase.
    - Providing SDC with the rationale for making a decision on the future of the project.

Among other analytical work done under the CBSMTHP and beyond (e.g., Eleanor Ostrom), the MTR Consultant used a conceptual framework to understand and analyze the impact of the co-management approach from the perspectives of "Nature, Wealth and Power" (USAID, 2013). The MTR Consultant was provided with a large volume of documentation by the SDC and IUCN Bangladesh Country Office. The Consultant also collected a large number of documents from various sources and used them, directly or indirectly, to understand and analyze the achievements of CBSMTHP. The Consultant held extensive meetings with a wide range of stakeholders in Dhaka, Sunamgonj, Tahirpur and the communities living around the haor (see Annex C for the list of meetings). In addition, the Consultant reviewed many relevant websites. A list of all persons met is provided in Annex B to this report. A selection of the main websites and reports reviewed are provided in Annex E.

A field visit was carried out from March 21-26, 2014 at Sunamgonj and the TH. The field visit included a stakeholders' workshop. Annex D provides the details of the field schedule.

2 The Tanguar Haor Ecosystem (THE)

2.1 The Resource

Legally protected under national and international systems[3], the Tanguar Haor Ecosystem (THE), covering about 9,727 hectares, located in the district of Sunamganj in the north-eastern part of Bangladesh, is an ecologically and economically unique wetland ecosystem. It supports the livelihoods to about 60,000 people living in 88 villages. The THE functions as an important breeding ground for fresh water fishery. Because of its critical ecological importance, the Ministry of Environment and Forests (MOEF) took its management responsibility from the Ministry of Land (MOL) in 2001.

The MOEF, under the National Conservation Strategy (NCS) Implementation project, sponsored a number of studies to determine the potential in natural resources of the THE and to identify the causes of observed resource depletion. These studies identified lack of income and employment opportunities for the people of the basin (who live isolated on islands during the entire rainy season) alongside excessive exploitation under the leasehold system, as a major cause of resource depletion. The swamp forests have diminished as local people harvest wood for use as fuel, reed beds have depleted due to unsustainable harvesting practices and the fish stocks had been seriously diminished due to over-exploitation by leaseholders. The lack of any system for recognizing customary rights of use and related management schemes has alienated the haor residents and precluded the emergence of management schemes that could ensure that exploitation levels are sustainable.

Figure 1. The THE

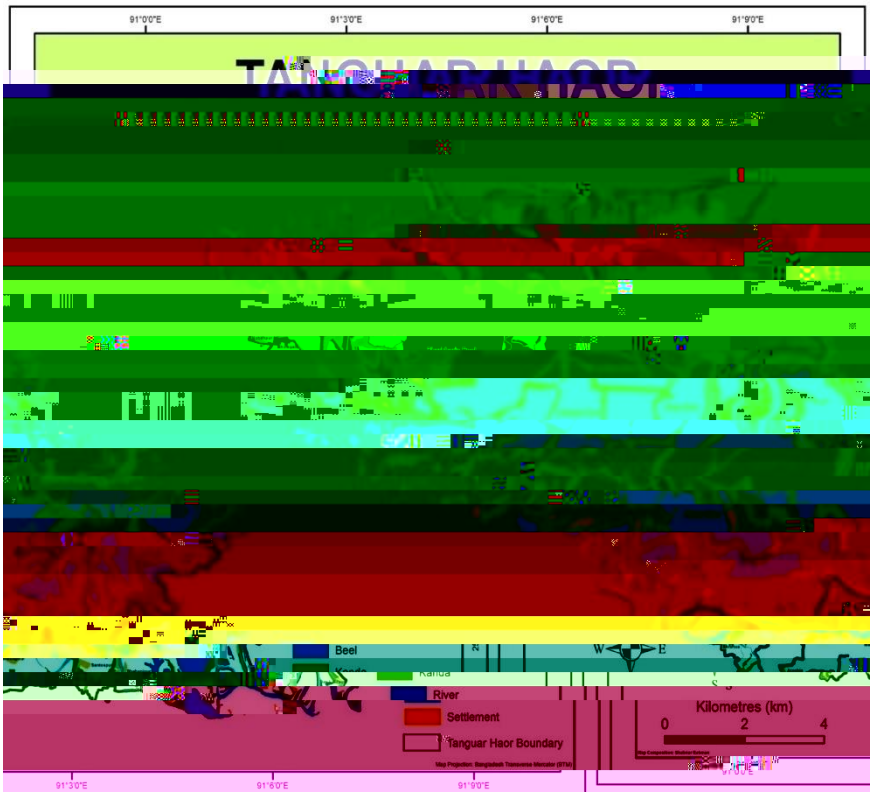

[3] The TH is a Ramsar Site since 1999. The MOEF declared TH as an Ecologically Critical Area (ECA) in 2000.

2.2 Conservation of the THE: Major GOB Initiatives

To conserve the resources of the THE, the GOB took three important steps:

1. Terminated the allocation of fishing rights to the highest bidding leaseholder, and suspended all fishing except for small-scale fishing in the immediate vicinity of haor villages for subsistence purposes. This suspension continued until 2008.
2. Prepared, in 2000, a comprehensive management plan for THE, introducing the concept of "wise-use" of wetland resources based on the wise-use principles of the RAMSAR convention.
3. Put in place in 2003 through the MOEF with its own resources and under the direction of the Deputy Commissioner, Sunamganj, a protection force consisting of Magistrates, ANSAR (unarmed law-enforcers of the government), Police and Border Guard Bangladesh (BGB) officers, to enforce a moratorium on the exploitation.

2.3 The CBSMTHP

The MOEF in tandem with IUCN Bangladesh Country Office received SDC support for the CBSMTHP project. Following a brief Preparatory Phase, a three-year (2009-2012) Development Phase was completed to establish a co-management system that would ensure both the preservation of key ecosystem functions and values as well as provide substantial livelihood improvements for rural communities. The current phase is termed as the Consolidation Phase (2013-2015).

The goal of the CBSMTHP is to introduce and institutionalize a co-management system for the TH Ramsar site that will conserve ecosystem values and services and provide a basis for the improvement of livelihoods for rural communities. Based on the experiences of the previous phases, the consolidation phase was set to achieve the goal through the following specific outcomes:

1. The co-management system in TH is consolidated and effective
2. The communities of the TH have improved livelihoods and increased incomes
3.

- Commitment of the local administrations including Upazilla and local government to establish a co-management mechanism involving the communities.
- Analyze the status of the institutional capacity to empower communities, particularly the poor and the women and also to provide a comparative analysis of the new institutional mechanism with the existing local system.
- Analyze the effectiveness of alternative income generation (AIG) and other economic activities for the poor including women to examine whether they have helped improve livelihood options to the extent that they would take the pressure off the resources of TH.
- Analyze the progress in managing local power relations and conflicts in implementing the proposed co-management system with particular reference to conflict management.
- Evaluate the role of the GOB in the project management as a major stakeholder. How far GoB policy decisions, practices and/or steps on Haor/water bodies, Ramsar helping or affecting? Does the GOB have special strategy on the project, particularly on co-management?
- Identify and analyze the factors that may influence sustainability of co-management in the medium and long term.
- To recommend the next course of role/

3 Summary of the MTR Findings Overall Performance of the CBSMTHP Challenge Phase

3.1 The CBSMTHP Governance

The CBSMTHP co-management governance apparently is well thought-out with a foundation at the grassroots resource user level and linking up to the GOB's highest, policymaking level. The Village Co-management Committee (VCC) is at the bottom of the governance structure. As its name suggests, VCCs were formed at the village level. The CBSMTHP has so far facilitated the formation of 73 VCCs covering 76 out of 88 villages around the THE and brought 6,616 members from 4,774 out of 10,205 households into the co-management process. The VCCs are the bases for establishing four Union Co-management Committees (UCCs). The Central Co-management Committee (CCC) is the apex body at the ecosystem level that serves as the voice for the THE community. The Tanguar Haor Management Committee (THMC) is located at the Sunamganj District Headquarters and chaired by the Deputy Commissioner (DC) of the district.[4] While THMC is the authority to set the TOR for the implementation of all the operations of the project, the CCC plays a central role in managing the SCM. The Project Steering Committee (PSC) located at MOEF is chaired by the Secretary MOEF. The Joint Secretary (Development) of MOEF is the CBSMTHP Project Director.

Figure 1 Schematic of the CBSMTHP Co-management Governance Structure

Nine General Body members of the VCC, five professional secretaries and four other office bearers; President, General Secretary, Office Secretary and Treasurer, are elected to the VCC for two years and form the VCC Executive Committee (EC).

The VCC-EC members are aggregated at the concerned UCC as UCC General Body (GB) members, and they vote for formation of UCC-EC members. The UCC-EC members are aggregated into the CCC as CCC-GB members.

At VCC level each voter of GB has the right to choose four office bearers, and one professional secretary from his/her own professional group in the EC. At the UCC level each voter of the GB has the right to choose only one member for the EC from his/her own group. On the other hand, at the CCC level each voter of the GB has the right to choose all members of the CCC-EC body. That means that the VCC is practicing five votes, UCC a single one and CCC nine.

Three representatives from the CCC represent the THE community at the THMC.

Portfolio based election system is introdu 1 30 EMC nt CCCodym

3.2 Legal Authority

restoration process. Training programs on biodiversity conservation with gender- and ethnic-balanced participants are ongoing to educate the communities on the importance and methods of ecological restoration are ongoing.

3.3.2 Outcome 2The Communities of the TH have Improved Livelihoods and Increased Incomes

3.3.2.1 Economic Empowerment

Aiming at helping the communities to achieve economic empowerment, the project has been assisting alternate income generating activities (AIGA). The Project is facilitating the use of the money through co-management committees.

The total of 700 HHs is facilitated to develop their 3 years LIP, and out of these, 463 HHs have already been supported. The communities accumulated BDT 18,681,112 and the Project has been utilizing this fund for livelihood improvement of the community. Total 2822 community members have been trained on AIGA (35% women); they are using this fund to increase their household level income. Financial assistance from the revolving Social Capital Management (SCM) increased up to BDT 57,990,000 as of February 2014. Involvement of women in economic activities increased by 70% compared to the previous reporting period. The Livelihood Improvement Plan (LIP) has already supported 463 (out of 700 planned) households.

3.3.2.2

3.3.3.2 Financial Sustainability

The co-management organizations have accumulated BDT 2,191,545 from commercial and non-commercial fish harvesting as of March 2014. The CCC also received BDT 1,500,000 as Organizational Development (OD) fund. The cumulative fund of the CCC has been raised to BDT 7,158,544 since inception of the project. All these efforts are expected to bring the sustainability target into fruition. The project is in the process of developing a long-term financial sustainability plan.

As an exit strategy, the project is also weighing options to transfer the management of the credit operation to an established micro-finance institute (MFI) since the communities, lacking education and skill, have a way to go to efficiently manage the operation themselves.

The community indeed needs further support for management of their huge fund due to their limitation particularly in case of providing the operational cost and capacity to manage the SCM operation . Other options; therefore, need to be discussed with the communities as communities are the owner of their savings.

In preparation for exit, the project is carrying out value chain analyses for four major economic sectors: fish, agriculture, livestock and handicrafts. The fish and vegetables value chain analysis has been completed already. Project will do livestock value chain and leave handicrafts value chain as this is not promising through value chain selection lens.

Modest attempts are being made to popularize ecotourism in the THE aiming at benefitting the participating communities. An ecotourism plan will be prepared.

4 Conclusions and Recommendations

Arya (2011) concluded that the strategy to organize people around saving and credit has largely been successful inasmuch as it mobilized a majority of poor population, including women; gave them voice; strengthened empowering processes through transparency of records; and built representational tiers above successively. While the first part of the conclusion is valid to a great extent, the last part seems seriously questionable. The MTR Consultant concludes that the CBSMTHP co-management governance system has a major flaw.

Co-management by definition is "a pluralist approach to managing NRs, incorporating a variety of partners in a variety of roles, generally to the end goals of environmental conservation, sustainable use of NRs and the equitable sharing of resource-related benefits and responsibilities" and "a political and cultural process par excellence

o

- Re-defining the co-

The Deputy Commissioner did not speak very highly of the achievements of the CBSMTHP. This is alarming. However, the saving grace is that the Deputy Commissioner said as an anecdote that the TH will never be leased out to any commercial interest ever again. As the THMC Chair, he of course emphasize on the necessity to continue the project for at least two more

The MTR Consultant concludes that the CBSMTHP performance in helping mobilize the AIGA and other economic opportunity enhancing efforts, secure communities' access rights to resources and modest attempts to understand the market challenges are reasonably good. Sustainability of these systems is going to be a serious issue and it should be a major focus for the remaining period.

The MTR Consultant recommends that:

- The wholesale idea of transferring the operation of the revolving fund to an existing MFI is re-assessed.[13] Hiring an MFI may be expensive. The transaction cost may be too high for the community in absence of the other supports they are now receiving from the project. Protection of the fund (currently about BDT 6,240,287) is crucial. Other cost effective means, of course with sound fiduciary safeguards, should be explored. For example, the MACH project came up with an effective measure. The CBSMTHP partner CNRS should advise the team to find a solution to this issue.
- The tendering system for commercial fish marketing must stop now. The CBSMTHP is an exceptional project that aims at empowering a vulnerable community. The THMC should be able to negotiate with the policymakers to make an exceptional mechanism to conserve a national heritage and a public good in public interest. Some suggestions follow:
    - First and foremost, focus on value protection. Even though the area is still out of the national electricity grid, helping establish diesel operated ice factories may be a good option.
    - Proactively reach out to the fish processors that are operating in the area. The organized VCCs may be attractive as suppliers to the processors. They may come up with some upfront investment as well.
    - Examine the possibility of creating a branding for the THE fish to access a special clientele.

4.7 Conflicts and Conflict Management

The potential of future conflict among the local elite, local government and co-management organizations over power and control of resources has been discussed in Section 3. The communities do not reserve any ethnic barrier, which is a positive point for co-management. Unfortunately, there are other sources of conflict.

4.7.1 Guarding the THE for Protection of Resources

An ongoing conflict between the CGs and the GOB law enforcers (Ansar and police) is facing the CBSMTHP implementation. The previous patrolling system that was introduced by the project – joint patrolling by the CGs and the law enforcers – is working no more. The CGs refused to go with the law enforcers complaining that the law enforcers ally with the illegal poachers that may put the CGs into danger. The project is closely working to resolve the issue. One significant effort the project is making is to mainstreaming the CG patrolling system under the GOB's fiscal system. Once approved, the number of regular CGs will increase in one hand and, on the other; the morale of the community to join the CG will heighten to a great extent.

4.7.2 Conflict within the Communities

SCM opportunities than the poorest of the poor. The CCC is aware of it and is trying to mitigate the situation.

4.7.3 Potential Conflict with Development Planning of Other GOB Entities

Coordinating development planning and implementation is a common issue. The Bangladesh Haor Development Board (BHDB) has recently developed a Master Plan for the development of the haors. The BHDB representative that attended the Consultant's meeting with the THMC also mentioned that the THE will also be given priority during the implementation of the Master Plan, which, however, may not happen anytime soon.

alarming. If this trend continues, no external intervention will prove good enough to maintain the vitality of the ecosystem.

This visible trend in decreased water flow into the THE indicates another broader aspect. Control of the water flow into the THE exists outside the geographical boundary of Bangladesh. This is; therefore, a transboundary issue and this cannot be dealt with within the current scope of the project or the current knowledge that exists on the THE. The CBSMTHP coordinating partner IUCN Bangladesh Country Office should flag this issue and start discussing with its India and Regional Offices to find a way to initiate a dialogue with the Government of Meghalaya to commission, at the very least, a transboundary study. This is perhaps well beyond the scope of the project, but IUCN Bangladesh Country Office should make the long-term monitoring of the THE a priority agenda under its core program, fund the study from its own resources and approach other DPs (including SDC) for support.

Figure 4 . Time Series Plot of Mean Daily Water Level at Jadukata River

4.9 Approaches to Long-Term Sustainability

The CBSMTHP has planned a series of actions to ensure that it leaves behind a system and a more aware, skilled and organized community with better economic and livelihoods opportunities to sustain the ecological integrity and productivity of the THE.

4.9.1 National Scientific Body (NSB)

A NSB, approved through a gazette notification, comprising of 8 members started working and they are providing scientific inputs for achieving project objectives. The NSB will advise and provide

taken in the first NSB meeting. It did not appear that the NSB has organized well yet even though the individual members have notable capacity in their respective areas of expertise.

4.9.2 National Wetland Network (NWN)

The planned NWN was established and the network has already organized a national level meeting. Participation at the meeting came from the GOB, NGOs, and natural resources stakeholders from all over the country. The participating stakeholders shared lessons they learnt from being involved in co-managing other wetlands. The main theme was sustainable wetlands management following the Ramsar "Wise Use" Principle. The participants exchanged information, knowledge and experiences with the THMC.

4.9.3 TH Information Center (THIC)

The CBSMTHP has established a THIC at Sunamganj. The THIC has already started attracting students and academicians interested in the THE. Construction of a new dynamic and interactive web portal for knowledge management on the THE is under process to improve the existing knowledge portal. A high speed internet service has been established in the project office to support the new web portal.

4.9.4 Proposed Tanguar Haor Management Authority (THMA)

The plan to establish the THMA under an Act of the Parliament is a brilliant idea. The project has started drafting the Act and associated Rules and has had held a consultative meeting at the national level following field level consultations. The institutional nature of the proposed THMA will determine the flexibility and effectiveness of the institution. Reading the draft Act gives an impression that it will be heavily government controlled. The proposed steering committee is consisting of top level of bureaucracy. The project has recently conducted a study tour to Lake Cilika[14] – also a Ramsar site located in Orissa, India. The Chilika Lake is managed by the Cilika Development Authority (CDA).[15] If the project and, for that matter, the MOEF conceives the CDA as a model for the proposed THMA, that may be fatal. The THE does not match the expanse, both in terms of areal coverage and conservation challenges, of Lake Cilika. Also, the CDA is alleged to be a top-heavy bureaucratic authority and the management of resources is done through a "command and Control" approach. The legal basis for setting up the institutional framework; its technical mandate, organogram and personnel compensation plan must be very clearly thought out with a pragmatic vision.

4.9.5 Approaches to Eco-tourism Development

Road communications to and from the THE are difficult during the dry season. The wet season offers easy transportation even though the system becomes turbulent. The project, however, is planning to develop an eco-tourism plan despite a budget constraint. It is also considering negotiating with a tour operator to take the lead in developing eco-tourism packages to attract tourists to the THE. The Consultant is not comfortable with this 'checking the box' approach.

[14] Lake Chilika is a brackish water lagoon, spread over the Puri, Khurda and Ganjam districts of Odisha state on the east coast of India, at the mouth of the Daya River, flowing into the Bay of Bengal, covering an area of over 1,100 km².

[15] In 1992, the Government of Orissa, concerned by the degradation of the lake's ecosystem and cognizant of significant numbers of people who were dependent upon the lake's resources, set up the CDA as a parastatal body for restoration and overall development of the lake.

improved management will make the ecosystem more resilient and improved livelihood will make the communities more adaptive. The THE, however, needs to give a special attention to climate change

4. (Crosscutting) Climate Change Adaptation[16]

Broadly speaking, the CBSMTHP objectives match very well with those of the SDC Cooperation Strategy (Table 2).

The CBSMTHP has been a long-term commitment for SDC. The general area (Sunamganj) is still a focus geographical area under the strategy. The Consultant commends the SDC for the way they have been incrementally supporting the development of a collaborative management, with the poor as central to the approach, of a significant ecosystem that has its influence on the ecology of a much larger area and the wellbeing of a large section of the ultra-poor.

With the new strategy, SDC may decide to explore newer areas of interest for its engagement in the focus areas. The Consultant, however, strongly recommends that SDC considers keeping its engagements with the THE improvement as well as supporting the poor communities for another project cycle. Co-management is a temporally and fiscally challenging process. Empowerment of the poorest of the poor in a less favorable enabling environment is not easy to come by. The CBSMTHP has been an ambitious project with a low budget. The current MTR has identified a number of issues related to the achievements of the project. Nonetheless, the CBSMTHP's accomplishments are convincing, given that the scope of the work was quite wide and the project budget low. But, there is a long way to go. The Consultant hopes that the CBSMTHP Exit Strategy will set the stage for a renewed interest from the SDC and other DPs in advancing the process. This is too good to drop at this stage.

The Consolidation Phase is crucial since it is expected that the CBSMTHP will take into serious cognizance the MTR recommendations. Implementing the recommendations will require SDC's focused attention, particularly from the Project Manager and, intermittently, from the Head of Cooperation. The MTR Consultant recommends that:

- The SDC proactively convenes a meeting involving the Country Representative of IUCN Bangladesh Country Office and the Steering Committee to discuss the MTR recommendations and strategize priority actions.
- The SDC convenes a meeting involving like-minded DPs, preferably at the Heads of Agencies level, and

- Leveraging support from other DPs (e.g., USAID through its CREL project and German Technical Cooperation who is facilitating a broader process to improve wetland management policies) to co-finance some priority areas identified in the exit strategy.

Table 2 Synergy of the CBSMTHP Objectives with the SDC Country Cooperation Strategy (2013-2017)

CBSMTHP Outcome/Output	SDC CS Pillar
Outcome 1: The co-management system in TH is consolidated and effective	1, 2, 3, 4
Output 1.1 Institutional co-management structures are strengthened	3, 4
Output 1.2 A monitoring system for environmental and economic parameters is established and applied	2, 4

6 Consolidation of Recommendations with Suggested Roles and Responsibilities of Stakeholders

The following Table makes an attempt to suggest the appropriate roles and responsibilities of the relevant stakeholders in prioritizing the tasks, assigning a realistic timeframe and addressing resource requirement issues in implementing the recommendations made in the MTR Report. The CBSMTHP should make every effort to address all the issues within the Consolidation Phase to maximize the potential for sustainability of this long-term effort.

Table 3 Recommendations with Suggested Roles and Responsibilities of Stakeholders

Recommendation	Roles and Responsibilities		
	MOEF	IUCN Bangladesh Country Office and CBSMTHP Partners	SDC
Co-management Governance			
x The entire co-management governance structure be revisited. This will include at a minimum but not limited to: o Re-naming and re-organizing the VCCs, UCCs and the CCC under a user-group federation rubric. o Making every effort to include the local elite and the local government into the co-management structure. x			

		s.	
Stakeholder Coordination and Alliance Building			
x Alliance building efforts should be strengthened. x The incentives for the communities should be revisited during the preparation of the exit strategy.	MOEF should reach out to other similar GOB initiatives and other ministries, e.g., Ministry of Water Resources, Ministry of Local Government, Rural Development and Cooperatives, and Ministry of Land.	The CBSMTHP should strengthen the facilitation of alliance building among all stakeholders of the THE as well as other neighboring initiatives such as the "Community-based Fisheries Management Project" funded by IFAD and implemented jointly by the World Fish Center (WFC) and the Local Government Engineering Department (LGED) and the "Climate Resilient Ecosystems and Livelihoods (CREL) Project" funded by USAID and implemented by Winrock	

	results shown in Figure 4 indicates a clear trend that historical water flow in a major river that traverses through the THE is decreasing steadily. This is alarming. If this trend continues, no external intervention will prove good enough to maintain the vitality of the ecosystem. This visible trend in decreased water flow into the THE indicates another broader aspect. Control of the water flow into the THE exists outside the geographical boundary of Bangladesh. This is; therefore, a transboundary issue and this cannot be dealt with within the current scope of the project or the current knowledge that exists on the THE. The CBSMTHP coordinating partner IUCN Bangladesh Country Office should flag this issue and start discussing with its India and Regional Offices to find a way to initiate a dialogue with the Government of Meghalaya to commission, at the very least, a transboundary study. This is perhaps well beyond the scope of the project, but IUCN Bangladesh Country Office should make the long-term monitoring of the THE a priority agenda under its core program, fund the study from its own resources and approach other DPs (including SDC) for support.			
Lg -Ter Sa in aby				
	x While establishing the THMA, it should be kept in mind that the institution will have a unique mandate of managing complex governance processes, science and art of biodiversity conservation and natural resources			

	interventions, a number of legal protection measures are in place and, more importantly, the communities depending on the resources are now organized and, to a great extent, sensitized. This is the time to go into the future with a strategic framework.	
x	o The CBSMTHP has done a disaster risk reduction (DRR) analyses that recommended a number of actions. The project, however, did not include a long-term adaptation approach for the THE even though the improved management will make the ecosystem more resilient and improved livelihood will make the communities more adaptive. The THE, however, needs to give a special attention to climate change adaptation.	the SDC to provide a one-off funding for the THSAP developmen t. (2) Start a dialogue with the UNESCO World Heritage Site Secretariat to provide a small grant, (3) Approach the Ramsar Secretariat for a similar small grant. IUCN Bangladesh Country Office should take a coordinating lead in preparing a full-fledged climate change adaptation project proposal for continuing its involvement at the THE

proactive to establish a co-management mechanism/modality for the Tanguar Haor Ramsar site involving the communities around Tanguar Haor?

3. How inclusive are the local institutional mechanisms of the poor and vulnerable population groups for addressing a sustainable co-management (including voice raising and participation in decision making)? Do the mechanisms address the needs of the women, poor and vulnerable? How far does the Tanguar Haor institutional mechanism support or contradict existing local systems and mechanisms?
4. Are there available promising alternative income generation activities for the poor including women allowing them to maintain wise use of Tanguar Haor resources? How has the project enhanced the livelihood options of the community in the project area?
5. How to manage local power relations and conflicts in implementing a co-management system? Are conflict resolution instruments available? Are the traditional instruments if any, applicable? What changes are necessary? Is a training process built in for conflict resolution?
6. What role GoB plays in the project management as a major stakeholder? What kind of Government commitment and ownership is in place? Are the available means and approaches reinforcing local administrations including Upazilla, civil society networks, local elites, and local government in their capacity to support the concept of co-management of the Tanguar Haor involving the communities around it?
7. How far GoB policy decisions, practices and/or steps on Haor/water bodies, Ramsar helping or affecting? Does the GoB have special strategy on the project, particularly on co-management?
8. What could be the next course of action? What, in order for the local and central government, the district administration and representative of community will do after the consolidation phase?
9. What are the factors that may influence sustainability in the medium and long term? Is the co-management mechanism established will sustain beyond the project period?
10. How is the existing system of SCM and mobilization of fund for AIGs working? Is it sufficient for the livelihood support for the community beyond project? Who will take responsibility of the SCM after project is over?
11. Are the lessons learnt attracting enough attention of GoB and other development partners for investing in Tanguar haor and similar places? Is the project harmonised with other projects by other development partners and relevant ministries/departments of GoB.

Methodology

The methodology of the review work will include the following steps:

- Review of agreements among SDC-Government-IUCN, the project logical framework, project implementation plan, annual work plans, and project reports.
- Meetings with key government officials to develop understanding about the government views on the overall protected area management plan of the Government of Bangladesh in the context of the Ramsar site management and the respective role of Tanguar Haor project. This would include an assessment of the Government's commitment and the steps taken towards institutional arrangements at local, regional and central levels for supporting the Tanguar Haor Management beyond project intervention.
- Meetings with the project partners (IUCN, HSI , CNRS and local partners), relevant actors and developing a matrix of performance, understanding and capacity in the context of Ramsar site management, in general and wetland management co-management in particular, as well as capacity to support improving livelihood conditions for the TH community, especially very poor and vulnerable.
- Undertaking a reconnaissance visit to the Tanguar Haor area to understand the community perceptions on the issues in the area vis-à-vis biodiversity conservation and livelihoods.

- Facilitation of a workshop with stakeholders in Sunamganj and Dhaka to identify key issues and challenges of the ongoing project in view to orient the future joint endeavour.
- Critical appraisal of the current phase and validation of the strategies and approaches as a crucial input that shall enable SDC to make a decision to orient for the remaining project period and if recommended, fix a next phase.
- Elaboration of recommendations for facing future challenges based on the good practices and failures observed during the field visit and activities undertaken so far, partners mix and roles (mainly HSI, CNRS, ERA, BELA, IUCN and GoB), including policy issues, strategies and approaches, co-management set up, cost recovery system.
-

Budget

The consultant will be contracted to SDC and her/his fees will be defined as per SDC's procedures, norms and criteria.

Reference Documents

1. Project Document
2. Project Implementation Plan
3. Annual work plan of Year-1 and 2
4. Monitoring reports of the project
5. MoU between SDC and the Ministry of Environment & Forests
6. Credit Proposal
7. Baseline study Reports
8. Other study reports and documents produced.
9. Progress Reports
10. Govt policy documents on haor/wetland and related issues.

Ann-B

List of People Met (in person or via audio conference)

Government of Bangladesh

Ahmed Iftekhar, Superintend

Sommer, Dr. Verena, Advisor – Environment and Climate Change, GIZ

IUCN and Other Civil Society

Annex C

Appointment Schedule for Dr. Azharul Mazumder, Consultant, MTR, CBSMTH Project, Phase III

Name of the concerned person	Date and Time	Place	Remarks
1.National Scientific Body of Tagore Hall	3 March 2013 at 3:00 pm	IUCN country office, Dhaka	Accomplished
2.Mr M. Asaduzzaman Acting Executive Director CNRS Mr M. Mokles Rahman Vice-Chairperson, CNRS	4 March 2014 at 03:00 pm	Center for Natural Resource Studies (CNRS) House-13 (4th-6th Floor), Road-17, Block-D, Banani, Dhaka-1213, Bangladesh	Accomplished
3.Mr Greg Beyrouty, Economic Growth Office, USAID Bangladesh	5 March at 11:00 am	Economic Growth Office, USAID Bangladesh	Accomplished
4.Mr Asaduzzaman ARO,IUCN	05 March 2014 at 01:30pm	IUCNB Office	Accomplished
5.Mr Fokhruddin Bachani Country Director HELVETAS Bangladesh	05 March 2014 at 04:00pm	HELVETAS OFFICE, House # 13/A NE (K),Road # 83, Gulshan-2,Dhaka-1212	Zahid and Riadh
6.Ole Mertz Principal Advisor & Climate Change Coordinator Wetland and Forest Biodiversity Rehabilitation Projects Deutsche Gesellschaft für Internationale Zusammenarbeit (GIZ) GmbH	6 March 2014 at 8:00 am	Road 90, House 10/A, Gulshan 2,Dhaka 1212 / Bangladesh	
7.Mr Md. Shafiul Alam Patwari Secretary Ministry of Environment and Forests (MoEF), Government of the People's Republic of Bangladesh.	6 March 2014 at 10:30 am	Bangladesh Secretariat,Dhaka	Zahid
8.Mr Mazharul Additional Secretary Ministry of Land	6 March 2014 at 02:30 pm	Bangladesh Secretariat, Dhaka	01713115403 Zahid
9.Dr Mohammad Nasiruddin, Joint Secretary (Development), Ministry of			

Annex E References

Note : The MTR Consultant was provided with a substantial volume of background information by SDC and IUCN Bangladesh Country Office, including project agreement, previous evaluation reports, presentations, reports on project activities, and copies of GOB circulars, etc. This annex does not list all the documents seen, but includes key websites, major reports and all documents that are explicitly referred to in the text.

Websites:

IUCN: www.iucn.org/Bangladesh

Local Consultative Group on Climate Change and Environment: http://www.lcgbangladesh.org/cce.php?q=1&s=4

MOEF: www.moef.org.bd

Nishorgo: www.nishorgo.org

Reports and Documents

Borrini-Feyerabend et. al., 2004	Sharing Power. Learning by doing in co-management of natural resources throughout the world, IIED and IUCN/ CEESP/ CMWG, Cenesta, Tehran.
CBSMTHP, 2013	Year 1 Operational Report
CEGIS, 2012	Master Plan for Haor Area, Volume I-III
GOB, 2009	Bangladesh Climate Change Strategy and Action Plan 2009, Ministry of Environment and Forests, Government of the Peoples Republic of Bangladesh, 2009: http://www.scribd.com/doc/40048702/BCCSAP-2009
GOB, 2010	Outline Perspective Plan of Bangladesh 2010-2015, Making Vision 2021 A Reality, Planning Commission, Ministry of Planning, GOB, 2011
GOB, 2010a.	Perspective Plan of Bangladesh FY 2010-2015. Making Vision 2021 A Reality, General Economics Division, Bangladesh Planning Commission.
GOB, 2011	Bangladesh, Sixth Five Year Development Plan, Planning Commission, Ministry of Planning, GOB, 2011
GOB, 2012	Bangladesh Climate Expenditure and Institutional Review, General Economics Division, Planning Commission, Government of the People
