Terminal Evaluation of the UNEP/GEF Project
p%HZERGMRK XLI 2EKS]E 4VSXSGSP MR 'SY
6IKMSR (GEF ID 5774)

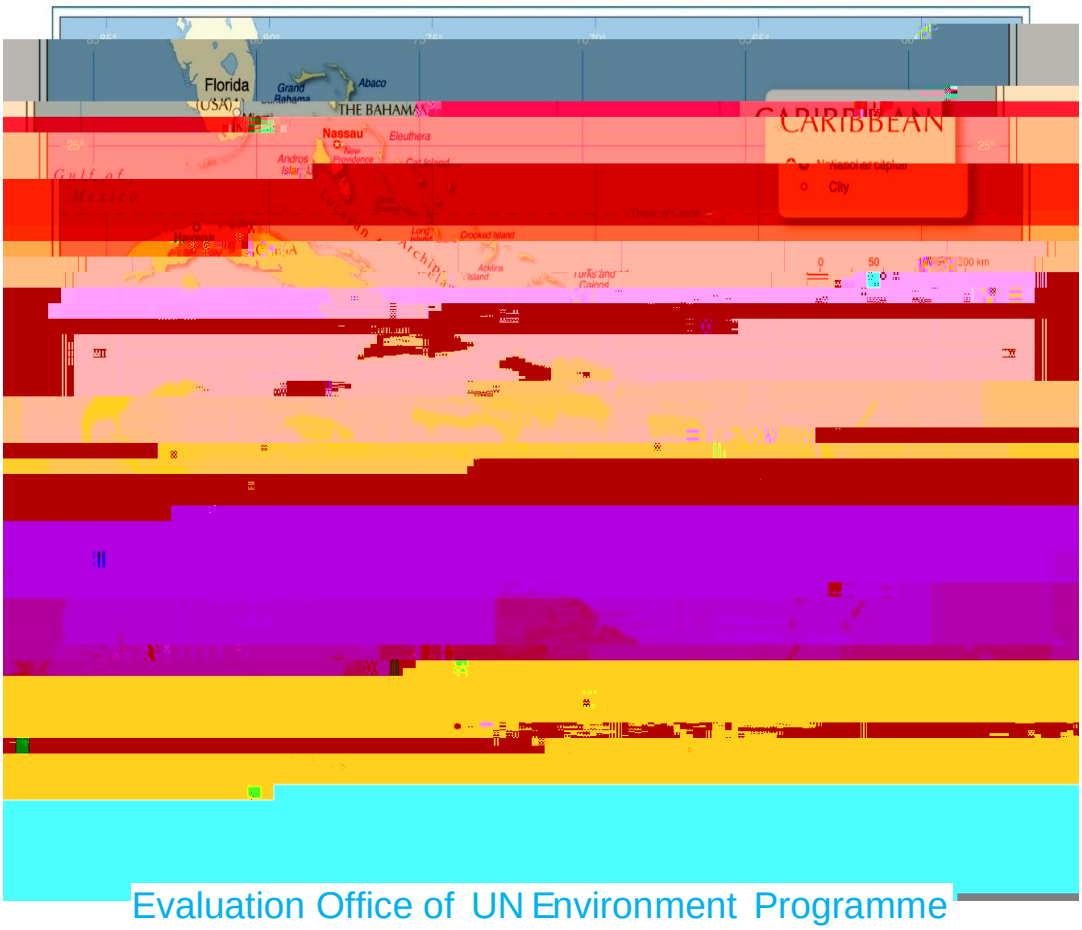

Evaluation Office of UN Environment Programme

April 2020

About the Evaluation

Joint Evaluation: No

Report Language(s): English

Evaluation Type: Terminal Project Evaluation

Brief Description: This report is the terminal evaluation of the UNEP-GEFproject ˹Bewbodjoh the Nagoya Protocol in Countries of the Caribbean Sfhjpo˺- implemented between July 2015 and May 2019.The project's overall development goal was to support countries of the Caribbean to facilitate access to their genetic resources and benefit sharing in a fair and equitable way, in line with

Project General Information

Table ES1: Project Identification Table

GEF Project ID:	5774	IMIS number:	GFL-5060-2711-4E67
Implementing Agency:	UNEP	Executing Agency:	International Union for the Conservation of Nature (IUCN)
Sub-programmes:	Ecosystems Management and Environmental Governance	Expected Accomplishment(s):	Ecosystem Management (expected accomplishment A), Environmental Governance (expected accomplishment B and C).
UNEP approval date:	September 2015	Programme of Work Output(s):	PoW biennia: 2016-2017; 2018 2019 Subprogramme 3: Healthy and productive ecosystems

5.8 Monitoring and Reporting 41
5.8.1 Monitoring design and budgeting 41
5.8.2 Monitoring of Project implementation 42
5.8.3 Project reporting 43
5.9 Sustainability 44
5.9.1 Socio-political Sustainability 44
5.9.2 Financial Sustainability 44
5.9.3 Institutional Sustainability (including issues of partnerships) 45
5.10 Factors and Processes Affecting Performance 46
5.10.1 Preparation and Readiness 46
5.10.2 Quality of Project Management and Supervision 47
5.10.3 Stakeholder Participation and Cooperation 47
5.10.4 Responsiveness to Human Rights and Gender Equality 48
5.10.5 Country Ownership and Drivenness 49
5.10.6 Communication and Public Awareness 49
6.0 Conclusions, Lessons Learned and Recommendations 52
6.1 Conclusions 52
6.2 Lessons Learned 57
6.3 Recommendations 59

Annexes

Annex 1. Response to stakeholder comments received but not (fully) accepted by the evaluator ..... 5.re..W*.n..BT../F3.11.04.Tf..1.0.0.1.82.824 327.7 Tm 0 g 0 G [(e)8(v)6(al)

.....

List of Acronyms and Abbreviations

ABS	Access and Benefit Sharing
CARICOM	Caribbean Community
CBD	Convention on Biological Diversity
GEF	Global Environmental Facility
GEF-OFP	GEF Operational Focal Points
GIZ	German Technical Cooperation (Deutsche Gesellschaft für Internationale Zusammenarbeit (GIZ) GmbH)
GR	Genetic Resources
ILCs	Indigenous and Local Communities
IUCN	International Union for the Conservation of Nature
IUCN-ORMACC	IUCN Regional Office for Mexico, Central America and the Caribbean
MAT	Mutually Agreed Terms
M&E	Monitoring and Evaluation
MTE	Mid-Term Evaluation
NBSAP	National Biodiversity and Action Plan
NC	National Coordinator
NP	Nagoya Protocol
OECS	Organization of Eastern Caribbean States
PC	Project Coordinator
PIC	Prior Informed Consent
PIR	Project Implementation Review
PMT	Project Management Team

Executive Summary

1. In July 2015 the UNEPreceived approval from the Global Environmental Facility for the Medium-Tj{ fe!Qspkfdu!TBewbodjoh!uif!Obhpzb!Qspupdpm!jo!dpvousjft!pg!uif!Dbsjccfbo!Sfhjpo!! (GFL-5060-2711-4E67) for three years. The project commenced in February 2016 and was completed in March 2019. This is the final report of the Terminal Evaluation that took place between June and November 2019 and included field visits to three of the eight participating countries, Costa Rica, and Panama, the regional headquarters for the UNEPwhere the Task

Context:	The project, both in the design and implementation phases, had a heavy bias towards the public sector. While this is understandable, given the need to develop requisite policies, legislation and ABS implementation tools and templates, there was little if any provisions made for engagement with private sector entities whose commercial interests could have acted as a powerful driver of change.
Lesson #3a:	Bioprospecting has great relevance and importance to both the overall economy and Indigenous Local Communities and can be a powerful driver of conservation and sustainable use if its commercial value can be readily identified and recognised. However, for the bioprospecting regime to function effectively, the enabling conditions (institutional and legislative) must be established and made operational.
Lesson #3b:	The private sector (commercial and research entities) as high-stake/ influence agents of change as well as key beneficiaries of a functional ABS system are integral to its implementation. In this regard, initiatives to attract their involvement should be undertaken at an early stage

Lesson #5b	time and where possible, set the stage for initiating projects in local(g)] 7(n)-10( )-8

1.0 Introduction

17. In July 2015 the Global Environmental Facility (GEF) granted approval for the undertaking of the Medium-Tj{fe!Qspkfdu!Tfwbodjoh!uif!Obhpzb!Qspupdpm!jo!dpvousjft!pg!uif!Dbsjccfbo!Sfhjpo', hereafter referred to as the ABS-Caribbean Project for 36 months, with a total budget of US$5,635,257. That amount was divided between the GEF contribution of US$1,826,000 and US$3,809,257.00 in kind co-financing from governments of participating countries and other project partners. The project had as the overall goal p X S W Y T T S V X G S Y R X V of the Caribbean to facilitate access to their genetic resources and benefit sharing in a fair E R H I U Y M X E F P I [E] q

18. The Terminal Evaluation (TE) was undertaken after the project was completed to assess project performance (in terms of relevance, effectiveness and efficiency), and determine outcomes and impacts (actual and potential) stemming from the project, including their sustainability. The evaluation has two primary purposes:

- to provide evidence of results to meet accountability requirements, and
- to promote operational improvement, learning and knowledge sharing through results and lessons learned among UNEP and the project partners (Organisation of Eastern Caribbean States (OECS), GIZ, International Union for Conservation of Nature- Regional Office for Mexico, Central America and the Caribbean (IUCN-ORMACC), UN CBD Secretariat, Caribbean Community (CARICOM)

19. In this regard, the evaluation sought to identify lessons of operational relevance for future project formulation and implementation, especially for follow-on projects pursuing the uptake of the Nagoya Protocol and implementation of key measures to make the protocol operational in the Caribbean.

20. Biodiversity conservation in the Caribbean is under threat, and high-valued genetic resources face insurmountable hurdles due to several factors including land degradation, climate change and invasive alien species. While Caribbean countries are rich in traditional knowledge, several have enacted legislation for the protection of their environment and biodiversity, as well as laws governing forestry, land use and protected areas. However, Caribbean countries lack the institutional and legal architecture to adequately manage their biodiversity resources and provide the basis for the implementation of basic provisions of the Nagoya Protocol. Most significantly, due to limited resources and experience in the ABS area, there is still a lack of capacities (institutional, systemic and individual) within government, local communities and among all key stakeholders in this regard. There is also a lack of awareness of issues concerning ABS as well as inadequate support to implement strategies and priority activities and limited resources for developing effective ABS measures and regimes.

21. The ABS-Caribbean project was implemented in eight countries [4] of the region, all of whom are signatories of the Convention on Biological Diversity (CDB) and have made consistent efforts to meet their obligations under that agreement as expressed in national strategies, plans, regulations, and laws. Most relevant to the proposed project objectives are the recent National Reports to the Convention on Biological Diversity, National Biodiversity Strategy and Action Plans (all of which make specific reference to some aspect of access and benefit sharing and traditional knowledge). The Project is aligned with the 2014 – 2017 Medium-Term Strategy (MTS) Environmental Governance Sub-Programme, which has as its

4

- progress reports from collaborating partners
- relevant correspondence, including the Project Implementation Reviews (PIRs)
- supervision mission reports, etc
- GEF Tracking Tool
- Steering Committee Minutes
- quarterly expenditure reports
- co-financing records
- budget revisions
- technical reports, studies, publications, outreach material, etc
- Mid-Term Review/Evaluation of the project
- Terminal Report of the project including final project output
- audit report and final financial statements; and
- other reports deemed useful to the terminal evaluation of the project.

2.2 Interviews

26. Interviews were undertaken with key stakeholders utilising various means of communication, including face-to-face interviews, telephone/Skype, and emails. The interviews used as a guide, the semi-structured questionnaire developed by the evaluator, based on the template provided by the UN Evaluation Office (See Annex B). The interviews also involved the asking of some strategic questions especially those pertaining to the ToC to determine the extent to which the drivers and assumptions, deemed most critical for the achievement of impact, were found to hold.

27. Among the key stakeholders interviewed were:

- UNEP Task Manager (TM)
- IUCN Project Management Team
- UNEP Fund Management Officer (FMO)
- Sub-Programme Coordinator
- Project Partners, including CARICOM, GIZ, CBD Secretariat, OECS
- National Focal Points, personnel in other Ministries (Attorney General's Office, Foreign Affairs and Trade)
- National consultants
- Representatives of Indigenous Persons and Non-Governmental Organisations.

28. The face-to-face interviews required field visits to several countries given the regional physical spread, IA, EA and various partners (See Table 3). The field visits, particularly with the Project Management Team was very important as it allowed for a focussed application of the various survey instruments and a complete interaction with the individuals directly involved in the implementation of the project. It also provides an opportunity to observe first hand, what initiatives were undertaken which are direct outcomes of the project and obtain a better appreciation for the extent of the commitments expressed at the country or regional level for any scaling up or replication that is deemed necessary.

Country	Dates Visited	No. of Days
Costa Rica	September 22-24	3 days
Panama	September 25 2 27	2 days

35. The most significant limita tion to the evaluation was the fact that the project did not have an explicit theory of change which therefore needed to be reconstructed by the Evaluator. Some difficulties were also encountered in setting up interviews/meetings with key stakeholders.

36. The Evaluator encountered difficulties in contacting some national ABS Focal Points . Efforts to interview personnel at the Secretariat of the Convention on Biodiversity proved futile. The IUCN Project Management Team (PMT) sent notices of the impending eval uation to all ABS Focal Points and Partner Organisations. The Evaluator followed up with introductory letters (emails) requesting interviews (face to face or online). While most of the countries responded and interview schedules established, no responses were received from Barbados and Jamaica.

37. The request for interviews with the partner organisation in question did not ma terialise because none of the persons contacted felt they were sufficiently knowledgeable about the project to speak on its behalf. Their tenure with the project was brief , given the fact that they had just recently replaced someone more familiar with the project.

38. During country visits, the Evaluator interviewed stakeholders from several sectors (government, universities, contracted persons, ABS implementation trainees, NGO´s and representatives of Indigenous Persons). While attempts were made to interview Indigenous Persons in Guyana regarding their participating in training activities and other aspects of the project, not much success was achieved due to logistical problems of either bringing them

Figure 1. Project Coordination Diagram

3.5 Changes in design during implementation

58. Uifsf! xfsf! op! fwfou! uibu! bggfdufe! uif! qspkfdut! tdpqf! ps! tvctuboujbmz! bmufsfe! uif! implementation of activities. The Project had a planned start date of September 2015. However, due to delays in the disbursement

data and information on genetic resources and stakeholders are receptive to that informa tion and willing to take action based on that information.

69. For DOs to be realised, several internal factors must be seen to have some influence to allow the project to move beyond direct outcomes. These internal factors or drivers (D1 and D2, influencing the causal link between Outputs and Direct Outcomes) include demonstrated interest in bioprospecting, technical understanding of the importance of common genetic resources which exist in the region, and continued commitment of the countries to the CBD and the NP, continue to be a driving force for scientists, politicians and their constituents to advocate for timely NP implementation.

70.

legislation in some countries; Prior Informed Consent (PIC) and Mutually Agreed Terms (MAT) templates granting access to genetic resources being used; and, the use of online mechanisms for submitting licences adopted, were successfully realised, the absence of an established institutional framework for fully operationalising the ABS mechanism, and the slow pace at which the other five countries[6] are moving with efforts to sign and ratify the NP suggests that sustainability, in the absence of continued technical and financial, may not be realised in the respective countries and consequently the Impact not realised.

[6] Of the eight participating countries Barbados, Grenada, Jamaica, Saint Lucia

Figure 2: Theory of Change

5.1.3 Relevance to Regional, Sub-regional and National Environmental Priorities

77. The Project had great strategic relevance as it sought, not only to address challenges concerning the conservation of biodiversity but also to create a capacity for countries of the region to harness their genetic resources to enhance livelihood. The Caribbean, as noted in the ProDoc, is rich in genetic resources, but these are under great threat due to land degradation, climate change, pollution from nutrients, unsustainable use and invasive alien species. The region is also rich in traditional knowledge with a great variety of traditions that relate to the use of fruits, plants and animals for medicinal purposes. However, many of the countries, lack the institutional, legal, and financial capacity to establish the mechanisms which would allow them to utilise their genetic resources in a manner that would not only meet their goals of conservation and sustainable development but also exploit 0 G [(w)-9p(0 G [(w)-9p)-3((0

95. While gender was mentioned as an issue which should be mainstreamed and equal opportunities ensured, there was no stated plan outlined for ensuring or monitoring its implementation. There were no provisions for reporting on gender mainstreaming until it was included in the 2018/2019 PIR. Notwithstanding, the PMT sought to ensure gender issues were addressed and reported on in the last PIR submitted.

Criteria	Summary Assessment	Rating
Quality of Project Design	Barriers and constraints were correctly identified, and for the most part, the p02 re W* n	

Guideline document was seen as important by the countries as it would provide several benefits as follows:

- Help countries in the Caribbean region avoid competing among themselves.
- Increase bargaining power for the region and help to avoid a race to bottom between countries seeking to get the benefits derived from the utilisation of genetic resources and traditional knowledge.
- Similar ABS frameworks will make it easier to navigate the access procedure, jodsfbtjoh!sfttfbsdifstt!usvtu!jo!uif!sfhjpo!boe!jodsfbtjoh!uif!dibodes of receiving benefits derived from the use of genetic resources.
- Easier for countries to monitor compliance of the users if the countries are willing to maintain open channels of communication between each other.
- Help to devise new and innovative ways to deal with the issue of transboundary resources and traditional transboundary knowledge. This issue can be of vital importance in a region as connected as the Caribbean.

104. All forty-one of the Outputs were completed. While it is fair to state that all outputs were completed, there is still no clear indication that all of the outputs have achieved or are likely to achieve the intended Direct Outcomes. The Delivery of Outputs is rated Highly Satisfactory (HS).

5.5.2 Achievement of direct outcomes

105. The achievement of Direct Outcomes was dependent on several drivers and assumptions occurring or holding. The drivers are characterized by the strong support provided by all the stakeholders, including partner organizations who provided support, both at the national and regional levels to ensure that decision-makers, as well as users of genetic resources and TK, are informed and aware of the need for new policies, legislation, regulations and other implementing tools as they relate to the ABS agenda. The realisation of these outcomes was also dependent on the assumption that partner organisations and ILC are willing to share data and information on genetic resources and stakeholders are receptive to that information and willing to take action based on that information.

106. For DO to be realised, several internal and external factors must be seen to have some influence to allow the project to move beyond direct outcomes. These external factors (Drivers) included the preparation of policy documents embracing the sustainable use of genetic resources and the assumption that stakeholders, including the legislators and implementing partners, take an interest in ABS and embrace the information conveyed and the messages delivered by the various media.

107. While it is fair to state that awareness of the knowledge and importance of genetic resources has been heightened and decision-makers are more aware of the importance of bioprospecting, only three countries have ratified the Protocol (Antigua and Barbuda, Guyana, and St. Kitts and Nevis). Also, none of the other countries has revised their legislative framework to explicitly allow for PIC and participation of ILCs in biodiversity access agreements (DO2). That absence of uptake is also evident in the fact that no significant strides have been made in terms of increasing technical capacities and finances to facilitate data collection (DO3) and there have been no strengthening of ABS legaland governance structures to facilitate bioprospecting in the region (DO5). Also, the operationalisation of a harmonised regional mechanism to promote the exchange of relevant information among countries (DO6) is yet to materialise.

108. Antigua and Barbuda have not only ratified the NP but have also revised their Environmental Act, incorporating ABS/ Traditional Knowledge mechanisms into local legislation. Meanwhile, Guyana, Grenada, Saint Lucia and St. Kitts and Nevis have indicated plans are underway to make similar changes to their legislation. Also, Guyana has instituted an online system for the submission of application and issuing of permits to access biological resources.

109. Taking all of the above into consideration, there is little doubt that some countries made strides in helping the project achieve some of the Direct Outcomes are yet to materialise. However, not all the Direct Outcomes were realised. While it is stated that some countries have expressed a desire to continue working towards achieving these outcomes, at this stage of the evaluation, when the project has come to an end, these initiatives have not yet care yet to outcomes are yet commenced. The rating for achieving direct outcomes is Moderately Unsatisfactory (MU).

5.5.3 Likelihood of impact

110. The DOs were expected to lead to two Intermediate States (IS1 and IS2), which were the reformulated objectives and goals of the project as outlined in the ProDoc. IS1 was reformulated from the original objective to reflect the changed state resulting from operationalis

the facts on which some assumptions were based. It does seem that there was an insufficient

Assumptions	Reality
i. Local communities and indigenous peoples take an interest in ABS, trust the awareness-raising message and embrace its content	Local communities and IP (Maroons in Jamaica boe!Hvzbob*!bm!f n csbdf e!u i fjs!Ţo f x⁉! knowledge, particularly as it promised wider acceptance and rewards for their traditional knowledge.
j. Countries fully embrace the outputs of the project and institutionali se required processes and strategies in all ABS related activities, including facilitation of personnel participation in training and capacity building opportunities	They all recognised the need for Competent National Authorities but making this a reality is a slo

GEF Funds was US$1.786mn with the remaining sum of US$40,000 to be utilised to cover the cost of the Terminal Evaluation. On average, expenditure on various project elements corresponded to the sums allocated within th e original budget; however, there were a few exceptions.

117. Concerning the Co-Financing Cash and In-Kind values, the budgeted contribution from Countries and institutions was US$3,809,257. Information received on Co-Financing contributions indicated that in total the co-financi ng was valued at US$2,904,999.61. This value, however, did not include information from Jamaica or CBD.

Table 7: Co-financing Table

Co-financing (Type/Source)	UNEPown Financing (US$1,000)	Government (US$1,000)	Other* (US$1,000)	Total (US$1,000)	Total

financing letter to UNEP dated 11 April 2015 (Ref: SCBD/ABS/SBG/ET/jh184313), suggests that it would ibwf!jodmvefe!Tqspwjtjpo!pg!sftpvsdf!nbufsjbmt!qvcmjtifd!cz!uif!Tfdsfubsjbu-!tubgg! time and co-organization of joint capacity -cvjmejoh!bdujwjujft!/!Uif!DCE!qbsujdjqbufe!in Steering Committee (SC) Meetings, co-organizing meetings such as the side-events at COP 14 and 15, as well as participating in the provision of training to participating countries to demonstrate access to and use of the ABS Clearing House Mechanism.

120. In-Kind Contributions amounted to US$904,257 below the budgeted value. Except for Barbados, Grenada and IUCN, the In-Kind contributions of the other countries and agencies was therefore significantly less than the originally budgeted values. The total Project contributions are shown in Table 7 above.

121. The Actual Cost of the Project was, therefore, US$4,690,999 or US$944,258 less than the total Budgeted Cost. This figure consists of Countries Contributions which were US$920,981 less than budgeted and the Contributions of Agencies which were $16,724 more than budgeted.

122. Countries were provided with co-financing templates and instructions in completing their reports. They were repeatedly urged to submit these reports on time. Unfortunately, not all did, and several countries did not meet their full co-financing commitment.

123. The general conclusion to be drawn from the completeness of financial information is that it was Moderately Satisfactory (MS).

5.6.2 Communication

124. The PMT at IUCN-ORMACC, which included the Project Financial Assistant, and the UNEP Fund Management office (Panama) have expressed satisfaction with the responsibilities executed by each other. Financial Reports were submitted on time and met the satisfaction of the Fund Management Office. Some slight delays with disbursement caused a delay in the start-up of the project, and another disbursement delay midway through the project again slowed the pace of delivery of some outputs. In the end, a request for a no-cost extension was made and approval granted.

125. VOFQt!Ubtl!Nbobhfs, based at the Latin America and the Caribbean Office in Panama, provides continuous support and works closely with project personnel in project implementation aspects related to UNEP and the GEF implementation. Good communications between the IA and EA were maintained throughout the Project implementation period, and both offices were adequately aware of the status of the project funding. Table 9 summarises the financial management of the Project.

Table 9: Financial Management Table

Financial management components:		Rating[8]	Evidence/ Comments
Completeness of project financial information:		S	
Provision of key documents to the evaluator (based on the responses to A-G below)		HS	
A.	Co-gjobodjoh!boe!Qspkfdu!Dptut!tubcmft! at design (by budget lines)	Yes	Received copies of tables indicating Co-financing and Project Costs at design

Financial management components:		Rating[8]	Evidence/ Comments
C.	All relevant project legal agreements (e.g. SSFA, PCA, ICA)	HS	All documents were shared with the Evaluator
D.	Proof of fund transfers	HS	All documents were shared with the Evaluator
E.	Proof of co-financing (cash and in-kind)	No	Partial. No information received from Barbados concerning their cash contribution. Jamaica and the CBD provided no reports on co-financing.
F.	B!tvn nbsz!sfqpsu!po!uif!qspkfdu!expenditures during the life of the project (by budget lines, project components and/or annual level)	Yes	Summary Report received
G.	Copies of any completed audits and management responses *(where applicable)*	Yes	Audits for 2016, 2017 and 2018/2019 received
H.	Any other financial information that was required for this project (list):	Yes	Information on GEF spending and actual In-Kind Contributions received
Any gaps in terms of financial information that could be indicative of shortcomings in uif!qspkfdu!dpnqmjodf[9] with the UNEP or donor rules		Yes	Yes. Not all countries/ agencies provided data on their In-Kind or Cash Contributions
Project Manager, Task Manager and Fund Management Officer responsiveness to financial requests during the evaluation process		S	Personnel, both at the EA and IA provided all the documents requested and expressed no concern about the financial management of the project
Communication between finance and project management staff			
Qspkfdu!Nbobhfs!boe0ps!Ubtl!Nbobhfs!mfwfm! of bxbsfoftt!pg!uif!qspkfdu!gjobodjbm!tubuvt/		S	Project personnel at both EA (IUCN-ORMACC) and the IA (UNEP) confirmed their awareness of the financial status having signed the necessary approvals

Gvoe!Nbobhfn fou!Pggjdfs!

Criteria	Summary Assessment	Rating
Financial Management	Overall Financial Management rating	MS
1.Completeness of project financial information	All financial requirements between the EA and IA were satisfied. Countries were provided with co-financing templates and instructions in completing their reports. However, not all countries/agencies submitted their reports , and several did not meet their full co-financing their	

5.9 Sustainability

146. Sustainability, within the context of th is evaluation exercise, is understood as the probability of direct outcomes being maintained and developed after th e close of the project. Several outputs, intended to ensure sustainability were delivered, including the development of ABS policy documents, ABS guidelines and an online platform for the exchange of information among participating countries. As indicated in section 5.5.3 above, several of these outcomes were realised, however, given the fact that no sustainable legislative and institutional framework was created at the national level to sustain those initiatives, as well as the need for financial support, the likelihood of these outcomes being maintained is not high.

147. The countries expressed great satisfaction with the outcomes as they not only heightened their awareness of the importance of genetic resources and associated traditional knowledge, but provided them with tools (e.g. ABS guidelines, Regional Strategy and Action Plan, and tools for facilitat ing access GR and Traditional Knowledge such as PIC and MAT Templates), and a model ABS Clearing House Mechanism. All of the documents produced under this initiative, together with the training provided can be easily accessed and modified to suit the needs of the participating countries as well as other countries desirous of using those tools to enhance their capabilities in facilitating access to their GR / Traditional Knowledge using existing national and regional institutions.

5.9.1 Socio-political Sustainability

148. All of the participating countries expressed a high degree of support for the project and what it sought to achieve. Three of the eight particip ating countries ratified the NP, however, only one,Antigua and Barbuda, has incorporated the ABS mechanism into national legislation. T Q qce WseT /F3 9 T Q qce W*W2 rg5(o)5(f s)-54 Tf 1/F3 9 de3(ti)5(o)41.92 re W41.96ies

162. The shortcomings identified at the preparation stage had to do with some overambitious objectives which did not take into consideration the challenges in moving from the awareness phase to getting legislation in place to address problems identified. Among the more obvious overambitious goals and incorrect assumptions were the following:

- Data on GR in the Caribbean is sparse, and the few institutions involved in research, primarily the Universities or research entities guard their information very closely

- All countries recognised the need for and expressed support for an online forum. However, challenges in finding an institution to host the forum as well as provide ongoing management proved difficult

- Development of a Roster of Experts never materialised as these were not filled in by the countries as was intended. While this may appear to suggest a lack of experts and the absence of a large pool of resources

gender and Indigenous People, ensuring their consideration was mainstreamed in all capacity building processes.

169. While the PMT reached out to entities engaged in research activities (the University of the West Indies and ILC) through their public awareness programmes to tour operators and small scale business operators engaged in the sale of bio-pharmaceuticals and TK, there was no specific programme or sustained effort to involve the private sector. That was due, in part, to the fact that the document ʈCvtjoftt!Npefm!gps! Access and Benefit Sharing in the Dbsjccfbo!Sfhjpoʉ!the blueprint for bsujdvmbujoh!boe!ʈmaximizing the economic potential of biodiversityʉ!resources was not completed until the latter part of the final year of the project. Also, the regional database of research activities in the Caribbean region, which would have served as an information portal for sharing of information research boe!ʈthe promotion of public-private sector interactions on the Caribbeanʉ!xbt!ofwfs!gvmmy developed and remained underutilised.

170. The PMT used various communication mechanisms to engage with stakeholders. Uiftf!jodmvefe!ʈejsfdu!nffujohtOjoufswjfxt-!dpotvmubujpot!boe!ufmfdpogfsfodftʉ/!Uxp side event meetings at UNCBD COP 14 and 15 in Cancun Mexico and Egypt were well attended by beneficiary countries, partner organisations and other interested stakeholders. High-Level Meetings with Ministers proved a little more difficult. However, durin g Caribbean ABS week)Nbsdi!312:*!uif!Njojtufs!pg!Bhsjdvmvsf-!sfqsfttfoubujwft!gspn!uif!Qsjnf!Njojtufsţt!pggjdf-! Permanent Secretaries from around the region attended. Also, several regional and national institutions were represented, along with representatives from indigenous people and local communities from Jamaica and Guyana, and local community groups and students participated in the meetings.

171. The overall rating for Stakeholder Participation Moderately Satisfactory (MS).

5.10.4 Responsiveness to Human Rights and Gender Equality

172. The ProDoc, while not explicitly outlining any issues or concerns relating to human rights, did specifically, however, express the need to mainstream issues of gender in all capacity building initiatives. It also recognised the important contri bution of IPs to biodiversity conservation and made allowance for their involvement in the implementation of the project. In that regard, Component 3, Outcome 3.1 of the Logical project Framework, specifically targeted Indigenous communities and provided resources for the production of public awareness materials in the indigenous language, and in the development of templates for Prior Informed Consent (PIC) and Mutually Agreed Terms (MAT).

173. Concerning the implementati on of the project, a gender methodology was adopted and implemented by the EA to ensure effective mainstreaming of gender by ensuring that IP was included workshops convened and in materials developed to heighten awareness of the ABS process. Likewise, concerning participation by women, there was a high number of women involved in decision-making positions during the implementation of the project. Women comprised almost 80 per cent of those in attendance at SC meetings, workshops and training initiatives undertaken by the project.

174. Two workshops each were held in Jamaica and Guyana in January 2019, to ensure the effective participation of women, indigenous peoples, local communities, particularly in the consultation and design of protocols for PIC and MAT w ere convened under the project. The workshops in Jamaica allowed for the participation of persons from the Rastafarians and Maroon Community. The Guyana workshopwas held in Lethem and Georgetown, and present

182. The communication channels were well established and observed during the implementation phase. The role of the Steering Committee was very effective in acting as a medium for disseminat ing and communicate decisions and procedures among countries and key stakeholders. The project also developed a virtual platform, including a permitting system and species database, for fostering effective communication amongst countries on ABS issues which will further enha nce the ratification process through effective communication amongst parties on ABS.

183. Among the many initiatives undertaken by the project to achieve their objectives were the preparation of videos, for TV and Radio, interviews on radio and television, thea iring of PSAs in all eight countries, the translation and production of videos in six different languages for the ILCs in Guyana, and the erection of signboards at strategic locations in three countries.

184. These initiatives were complemented with the conv ening of training workshops for two persons from each of the participating countries and over 30 inter -institutional workshops in the eight participating countries.

185. Awareness-raising dialogues were held with environment ministers at two meetings of the OECS ministers of environment. Cabinet notes were prepared for members of the cabinet for all eight countries. Included in these notes was information on the Nagoya Prot ocol and the road to ratification for each country. The convening of the Caribbean Access and Benefit Sharing Week, which took place in Trinidad and Tobago from January 29-31, was aimed at generating awareness of and support for the Nagoya Protocol, under the Convention of Biological Diversity (CBD).

186. While it is generally agreed that a considerable amount of activities was undertaken in raising awareness of and support for the NP, participants acknowledged that much more is still needed to increase awareness of the importance of genetic resources . This was saliently captured by one participant who acknowledged that while there had been widespread public education that reinforced *'///the value of genetic resources and the traditional knowledge that comes along ...there is so m*

205. Though very few countries have formally initiated action to incorporate regulations and guidelines given to them, several have indicated that they have already commenced use of the PIC and MAT templates in the guidelines used to permit bioprospecting in their respective countries. They do recognise that formal amendments are required to ensure a legal basis for these measures, however until these can be achieved, they will continue using these instruments to ensure that access to their genetic resources and Traditional Knowledge are permitted on a fair and equitable basis. Going forward, however, will require continued awareness-raising and it is anticipated that PIC and MAT Templates, along with online facilitation of bioprospecting request will be replicated.

206. Notwithstanding the failure to realise those intended outcomes and impacts, the project achieved a fair amount of success, some of which, if pursued by the countries could still result in the long-term benefits being achieved. However, without financial support, and given the structural and capacity constraints which were not adequately addressed, it is hardly likely that the intended impacts will be fully realised.

Table 10: Evaluation Criteria and Rating Table

Criterion	Summary Assessment	Rating[13]
A. Strategic Relevance		HS
i. Ah4 1.2 0 0 1 re 5 s) -5 ET2s) -5 9 r) -5 1 (		

Criterion	Summary Assessment	Rating[13]
	Category 5 hurricanes struck the region during project implementation, but they had negligible impacts.	
D. Effectiveness		MU
i. Delivery of Outputs	All of the outputs were completed, though there were some delays with the delivery of some critical outputs.	HS
ii. Achievement of Direct Outcomes	Only two of the six DOs were realised, making it difficult to envisage that other intended impacts would be realised.	U
iii. Likelihood of Impact	Three countries have ratified the NP, and several others have commenced incorporation of some of the ABS guidelines for PIC and MAT. However, without the institutional support and a recognised legal framework in place, it is hardly likely the intended Impact will be realised.	U
E. Financial Management		MS
i. Completeness of project financial information	All financial requirements between the EA and IA were satisfied. Countries were provided with co-financing templates and instructions in completing their reports. Not all countries/agencies submitted their reports, and several did not meet their full co-financing commitment.	MS
ii. Communication between finance and project management staff	Communications between the EA and IA were excellent. There were two instances of disbursement delays by the IA, but good relations were maintained throughout the life of the project.	S
F. Efficiency	Efficiency was practised and achieved throughout the life of the project. With a limited budget and tight time frame, the project delivered all outputs within thirty-six months. Other measures of efficiency included the development of regional guidelines and templates, adopting a common approach the drafting of roadmaps and the use of virtual meetings to save cost on travel and reduce the carbon footprint of the project	HS
G. Monitoring and Reporting	Overall Monitoring and Reporting rating	S
i. Monitoring design and budgeting	Monitoring and design are consistent with GEF/UNEP guidelines.	HS
ii. Monitoring of project implementation	All reports, including PIRs and financial reports, were prepared. The reporting format, however, did not allow for objective monitoring of progress in implementation.	S
iii. Project reporting	Reports were prepared and submitted on time.	HS

6.2 Lessons Learned

207. The following table presents a summary of the main lessons learned from some of the qspkfdut!tvddftt!boe!dibmmfohft/

Table 11: Main Lessons Learned

Context:	The most significant comment aired in respect of the failure of the project to realise all intended Ejsfdu!Pvudpnft!boe!Jnqbdut!xbt!Tjotvggjdjfou!ujnf!U/!!Uifsf!jt!wbmjejuz!up! this assertion given the fact that several of those outcomes required changes in policy and regulations, both of which require time. That time may be relative; however, when it requires the heightening of awareness of the NP and ABS mechanisms, the preparation and approval of policy documents, and the drafting and adoption of laws and regulations, that require the approval of Cabinet and the Parliament, these could take years to materialise.
Lesson #1:	Projects intended to accomplish objectives that require structural changes and necessary supporting policy, legislative and regulatory must provide adequate time for those changes to be realised.
Application:	UNEP must ensure that in the designing of projects, that sufficient acknowledgement is made of challenges inherent in adopting policy and necessary legislation and regulations. In that regard, projects that require the adoption of new policies and legislation should be phased such that more practical implementation targets could be defined and executed.

Context:	While there were not too many complaints about capacity constraints, it was, indeed a major concern as none of the countries was able to assign to the project, one officer tasked with its dedicated responsibility ensuring its successful implementation. Persons assigned to the project were already engaged with other activities. This is not unusual, given the financial and staffing constraints faced by small countries. Provision was made in the project to assign a Project Coordinator to work with each of the countries. However, funding to engage such support was only provided for a total of 10 months out of the thirty-six-month implementation period of the project.
Lesson #2:	Regionally executed projects should be provided with adequate technical and financial support to provide for the implementation of projects. That support does not necessarily mean full-time engagement of a consultant (Project Coordinator), but the allocation of a Project Coordinator to adequately deal with issues such as engagement with stakeholders and raising public awareness-raising to obtain buy-in, particularly by High-Level stakeholders and decision-makers.
Application:	Implementing Agencies should ensure that adequate Technical Support is provided for and clear sets of undertakings defined, to ensure that the efforts mainly target outputs which are likely to be the most difficult to implement.

Lesson #5b	time and where possible, initiate projects in local communities which can be use d as models for replication in other communities. When projects are not results-oriented, there may be a risk of project teams becoming preoccupied with completion of activities and delivery of outputs, and checking them off, with no real consideration of

Annex 1. Response to stakeholder comments received but not (fully) accepted by the evaluator

Statement and Stakeholder Comment	Response of Evaluator
#6. The intervention logic was based on a log frame analytical methodology, which adequately identified outputs and outcomes but was weak in terms of identifying the pathways through which Outputs would lead to Direct Outcomes, Intermediary State and Impacts. *"I believe this is an oversimplification. The pathway to achieving the outputs where identified, the reason why some of the outcomes where not fully achieved, in my opinion was a matter of timing and/or unrealistic planning".*	Bt!opufe!jo!$74!boe!$75!uibu!x ijmf!uif![Sftvmut! Framework was useful in identifying Outputs to Outcomes, the Outcomes were not directly linked up!uif!Pvuqvut/!!Bmtp![!the reconstructed ToC was voefsubl fo!up!if mq!ftubcmjti!uif!qspkfdut!mphjdbm! structure, identify causal links between Outputs, Direct Outcomes, and the Intermediary States, through to the realisation of Intended Impact, and determine the likelihood that the intended results xjm!cf!sfbmjtfe/!!Uibu!sfrvjsfe!mjoljoh! assumptions and drivers with the respective Direct Outcomes, Intermediary State and Impacts. While several assumptions were made, not all of them held, and timing and unrealistic planning were significant issues, but so too was the absence of esjwfst/!!Ju!jt-!uifsfgpsf-!opu!bo![pwfstjnqmjgjdbujpo/! to say that the logical framework model was inadequate. Reference is also made to Table 5: Assumptions and Realities where a detailed analysis is provided of the Assumptions and how far some of them were from reality and the extent to which there were gaps in the log frame model.
$9![What this meant was that as time became a factor, and some of those assumptions did not materialise in the anticipated time-frame, several of the direct outcomes did not materialise. [*This is correct, but it is also correct to say that the executing agency together with the steering committee, did manage in most cases to substitute the unfeasible outcomes for new feasible ones, depending on the context".*	This has been acknowledged
#9. However, not all Direct Outcomes and intended Impacts are clearly discernible, raising doubts regarding their sustainability, now that it has ended. *"In deed there are some sustainability questions, but in most cases, the countries that did ratified the protocol, are continuously making improvement to apply the legislation (Antigua & Barbuda, Guyana and SKN). In the case on Saint LUCIA (which did not ratify), for example, there is an initiative to continue the ABS regional project in order to work an ABS project at national level. This is currently in discussion with UNEnv."*	Personnel in Grenada, St. Kitts and Nevis and Saint Lucia all expressed their intention to pursue follow up activities to ensure ratification of the NP. The OECS Commission as well as GIZ also indicated their willingness to support Member States that have expressed that desire to proceed with ratification. However, it was also clear from interviews with personnel in the respective countries that some of the issues which hampered ratification previously, such as capacity constraints, and finances were still of some concern, notwithstanding the promised assistance from various agencies. This is a sustainability issue which, at the time of evaluation, could not be ignored.

Statement and Stakeholder Comment

24. Report of the Workshop on the ABS Clearing House of the Advancing the Nagoya Protocolin Countries of the Caribbean Region project July 21st & 22nd, 2016
25. Inception Workshop Advancing the Nagoya Protocol in Countries of the Caribbean Region April 25, 2016 Hilton Hotel Port of Spain, Trinidad & Tobago report Four Seasons Hotel Kingston, Jamaica
26. Report of the First National Workshop of Jamaica for the Advancing the Nagoya Protocol in Countries of the Caribbean Region project July 25-26 & 28-29, 2016
27. Minutes of the First Steering Committee Meeting, April 26, 2016. Hilton Trinidad & Conference Centre, Trinidad.
28. Minutes of the Second Steering Committee Meeting; Virtual Meeting via Zoom, March 27th, 2017
29. Minutes of the Third Steering Committee Meeting; October 23rd, 2017 Jolly Beach Resort Bolans Village, Antigua & Barbuda
30. Minutes of the Fourth Steering Committee Meeting; Virtual Meeting via Zoom April 18th, 2018

project. This implies that there should be consideration of the baseline conditions, trends and counterfactuals in relation to the intended project outcomes and impacts. It also means that there should be plausible evidence to attribute such outcomes and impacts to the actions of the project. Sometimes , adequate information on baseline conditions, trends or counterfactuals is lacking. In such cases this should be clearly highlighted by the evaluators, along with any simplifying assumptions that were taken to enable the evaluator to make informed judgeme nts about project performance.

27. Communicating evaluation results. A key aim of the evaluation is to encourage reflection and learning by UN Environment staff and key project stakeholders.

- x Tubl f i pmefstt!qbsujdjqbujpo!boe!dppqfsbujpo
- x Responsiveness to human rights and gender equity
- x Communication and public awareness

iii. Likelihood of Impact

39. Based on the articulation of longer-term effects in the reconstructed TOC *(i.e. from direct outcomes, via intermediate states, to impact)*,

x

(These factors are rated in the ratings table, but are discussed within the Main Evaluation Report as cross-cutting themes as

Annex 5: Brief Resumé of the consultant

David A. Simmons has more than 25 years of experience working in various areas related to Environmental Policy, Planning and Management and Sustainable Development. Mr Simmons has considerable experience in the areas of institutional analysis and environmental policy planning and management having been contracted to undertake several related consulting assignments covering Climate Change Adaptation, National Biodiversity Strategies and Action Plans, and Coastal and Marine Policy, Planning and Management.

Mr Simmons has considerable experience of working on complex projects, e.g., the GEF-funded, and UN Environment exfdvufe!Joufhsbujoh!Xbufs-!Mboe!boe!Fdptztufnt!Nbobhfnfou!jo!Dbsjccfbo!Tnbmm! Jtmboe!Efwfmpqjoh!Tubuft!)JXFDP*U!cfjoh!jnqmfnfoufe!jo!:!Dbsjccfbo!dpvousjft<!Uif!HFG!gvoefe-! VOFQ!fyfdvufe!qspkfdu!up;!Jodsfbtf!Tbjou!Mvdjb!dbpacity to monitor MEA implementation and tvtubjobcmf!efwfmpqnfouU-!cbtfe!po!b!xjef!qbsujdjqbupsz!qspdftt-!boe!ublioh!joup!bddpvou!cbtfmjof! and priorities for national information management; and, the GEF funded and World Bank executed Jtmboet!Tpmje!boe!Tijq-hfofsbufe!Xbtuf!Nbobhfnfou!qspkfduU. He was also the lead consultant for the preparation of the Access and Benefit Sharing of Genetic Resources policy document for Guyana (2009).

He has also undertaken Evaluation exercises on several national and regional projects including the Caribbean Challenge Initiative (2014), the Bahamas Network of Marine Protected Areas (2016) and the Mid-Term Evaluation of the Energy for Sustainable Development in Caribbean Buildings project (2017). He has also facilitated national workshops which sought to mainstreaming Multilateral Environmental Agreements (MEAs) Into Policy Development: within the context of the BPOA, SAMOA Pathways, and the Sustainable Development Goals.

Mr Simmons has written and edited a number of publications and presented papers at several distinguished gatherings.

Annex 6: Quality Assessment of the Evaluation Report

All UN Environment evaluations are subject to a quality assessment by the Evaluation Office. This is an assessment of the quality of t he evaluati

	UN Environment Evaluation Office Comments	Final Report Rating
which findings can be either generalised to wider evaluation questions or constraints on aggregation/disaggregation; any		

UN Environment Evaluation
