Mid Term Review

Preparation and testing of a comprehensive model for preventing and managing the spread of invasive species on island ecosystems

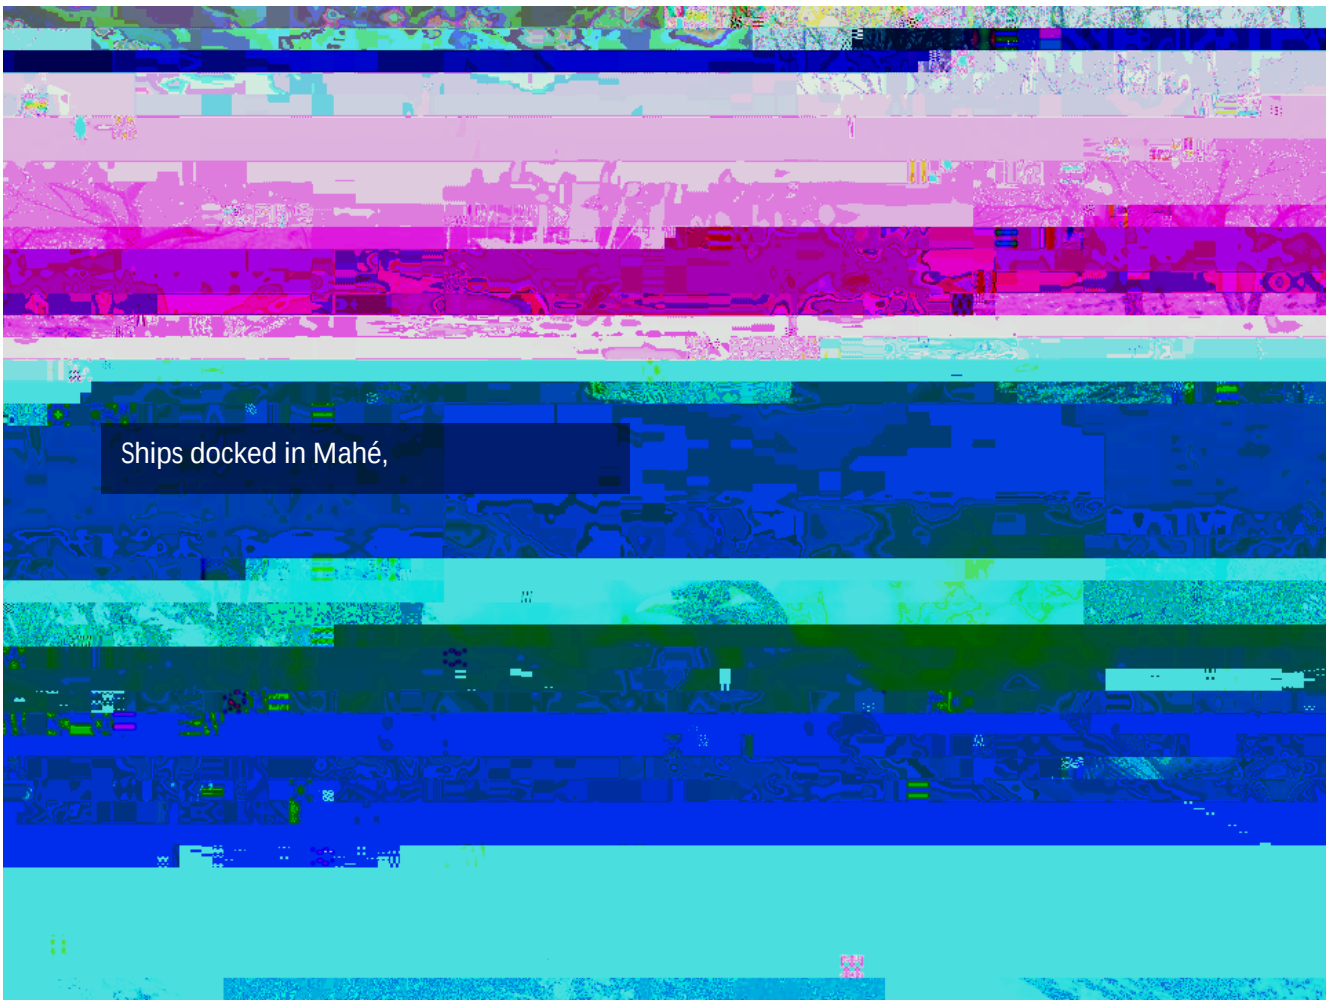

Photos by John Mauremootoo (CC-BY-SA-NC)

John Mauremootoo

July 2015

Disclaimer

Executive Summary

- Refining WIO IAS indicators as well as criteria for monitoring and evaluation of IAS management operations
- Finalising and launching of the global guidance manual
- Developing projects that can build on the achievements of the Invaz'iles Project.
- Developing an exit strategy for the project.

Recommendations to address obstacles to project implementation, and maximise cost-effectiveness, impact and sustainability

Implement a no-cost extension:

- A 1.5 year extension would be optimal leaving a year for the pilot site results to be integrated into the global guidance manual.

Adapt project design, planning, and monitoring and evaluation

- Reprioritise the project work plan and budget, reduce the scope of some activities (especially the pilot site work) and maximise synergies with other initiatives.
- All major changes to the project must be communicated with, and agreed by the SC.
- Design and implement a clear and simple adaptive planning, monitoring and evaluation system that facilitates easy understanding of current project status.
- Adapt activities to the specificities of the islands to take regional heterogeneities into account.
- Change the process of producing pilot site selection and management by potentially using pilot to add value to existing initiatives if compatible with project objectives.

Modify the process of pilot site selection and management

- Pilot site guidelines, plans, management structures and budgets should be developed in close collaboration with relevant partners at the national/island level.
- Work through organisations who are not IUCN members if these organisations are considered to be best equipped to successfully coordinate/implement the pilot intervention.

Improve project management communication and proactivity

- Incorporate WIO island experience into the global guidance manual to complement the examples from elsewhere in the world.
- Use a technical working group and a writeshop as a means of capturing WIO experience.

Revitalise project management and governance

Improve project management communication and proactivity

- Recruit a dynamic, proactive PM with both project management and networking experience and technical expertise in invasive species, based in Mauritius and with a 100% time allocation to the management of the project and clarify the PM's ToRs accordingly.
-

- Ensure that the SC meets at least one per year.
-

List of Abbreviations and Acronyms

AFD	Agence Française de Developpement
BIOPAMA	IUCN Biodiversity and Protected Areas Management Programme
BIP	Biodiversity Indicators Partnership
CABI	

MEA	Multilateral Environmental Agreements
MoAIFS	Ministry of Agro-

5.4. Result 4: Strategies

Summary

The EC-funded Invaz'iles project is being executed by IUCN to prepare and test a comprehensive model for preventing and managing the spread of invasive species on islands worldwide, with on the ground activities being implemented in WIO Islands. Through a consultative process involving 29 project partners and other key stakeholders, the mid-term reviewer assessed the extent to which the project has delivered against intended actions and results in its first three years, identified lessons, and produced concrete recommendations for the remainder of the project based on these findings.

Those consulted considered that the issue of biological invasions was highly relevant to islands in the WIO and beyond and those who were aware felt that the project design was aligned with this priority issue. Perhaps the project design and the perceived importance of the issue contributed to the project's promising initial momentum. This momentum was, however, not sustained, to the point where activities came to a complete halt in year 3. The project scored very poorly on all the parameters relating to efficiency and effectiveness. It scored better on sustainability but the positive scores related to factors beyond the remit of the project.

The strong overall conclusion of this review is that the project patently and substantially under-performed and under-delivered at the global and site-specific levels. There are a number of reasons for this. Many relate to communication failures – within IUCN, between the project management and project partners at all level, and between the project management and the donor. Other factors relate to a failure to optimise synergies with national, regional and global partners. In addition the regional and global aspects of the project, notably WIO island-based pilot site work and the development of a global guidance manual on the prevention and management of biological invasions on islands were poorly integrated. This exacerbated the divide between some who emphasised the global and others who emphasised the regional aspects of the project. Pilot sites have never been implemented and the manual has not progressed beyond its first draft. Alarm bells should have been rung a long time ago and the fact that they did not does not reflect well on those responsible for project management and oversight.

However, as stated, the project remains regionally and globally relevant and the overall project design is strong. So the MTR recommends that the project is continued and a 1.5 year extension is granted. The project does not require a major reformulation but the project description and the logframe need to be harmonised and the pilot work needs to be reframed so that it can include but is not restricted to work at the site level, and reduced in ambition - from eight to a minimum of three pilot .

Major recommendations to address the obstacles to project implementation relate to: the establishment of measures to enhance communication at all levels notably through changes in project management and governance; optimising synergies with projects and partners; and integrating project activities in ways that mutually reinforce the regional and global aspects of the project.

Key recommendations to revitalise project management and governance include: the recruitment of a new PM with an invasive species technical background and strong project management and networking skills, formalising the project gov-

e r 1 1 . 3 h a n

1. INTRODUCTION

The following sections on project background and objective, project context and the purpose of the review are adapted from the review terms of reference which is provided in full as Appendix 1.

1.1. Project background and objective

This EC-funded IUCN Invaz'iles Project ( ) has been formulated to address the need for a set of globally-relevant guidance for the prevention and management of invasive alien species (IAS) on islands around the world. The project aimed to build on the work carried out by programmes and projects around the world over the last two decades on prevention, containment, eradication and strategic management of invading species as well as legal and policy formulations and apply this to the Western Indian Ocean (WIO) islands.

The Overall Objective of the project is to reduce the spread and impact of biological invasions upon people and biodiversity of islands.

The Specific Objective of the project is to enhance the systems and strategies in the Small Island Developing States and in particular those in the Western Indian Ocean region, to efficiently prevent and manage biological invasions. The final intended outcome is a global guidance

curity systems. Both have contributed to the level and spread of technology and information to address these same problems on islands.

This action sought to use these decades of experience to develop a comprehensive model to address the same problems in other island systems and to test this in a group of SIDS and European entities in the WIO – to address the same problems and, in going so, build capacity for prevention and management of invasions at the same time. It also seeks to improve the model through new experiences. It was intended that the new and ongoing similar initiatives in the larger islands of Seychelles and Mauritius, as well as the Indian Ocean Commission (IOC), and other island states iee tim0 Td9107 Tc -0. to

Table 2.1 The Review Matrix

REVIEW CRITERIA	KEY REVIEW QUESTIONS	SUBQUESTIONS	INDICATORS	DATA SOURCES / METHODS
Relevance	1)	1. (Fixed choice response: High, Medium, Low, Don't know) - 2. (Free choice response)	1. Degree to which does the project design aligns with existing priorities at local, national and regional level. 2. Ways in which the pro-	

REVIEW CRITERIA	KEY REVIEW QUESTIONS	SUBQUESTIONS	INDICATORS	DATA SOURCES / METHODS
		factors were more important, Don't know) 4. Significance question: (High, Medium, Low9.4 544.68 146.04 0.96 ref295.44 544.236um, LoDATA SOut(()0.8(H)-4. 26.88 re959 0.96 ref65.04 544.68 0.959 0.9 Td84		

REVIEW CRITERIA	KEY REVIEW QUESTIONS	SUBQUESTIONS	INDICATORS	DATA SOURCES / METHODS
		the long term at local, national or regional levels? 4. In what way could the project adapt to strengthen the probability of longer term sustainability?	ity of the project's benefits at local, national or regional levels. 3. Measures that have been taken to ensure that the benefits realized through this project will be sustained over the long term at local, national or regional levels. 4. Ways in which the project could adapt to strengthen the probability of longer term sustainability.	

2.2. Review s2.2.

3. Findings

3.1. Project Relevance

The question specifically asked to what extent was the project aligned with existing priorities at the national and regional/global levels. Most interviewees found it hard to answer the question as they were not very familiar with the project design. However, they were given some latitude and instead commented on how closely aligned they perceived to be with existing priorities at the national/island or regional/global level.

3.1.1. The Project's relevance at the national level

Most stakeholders who could comment on the project's relevance to priorities at the national level thought that it was either high (Seychelles and TAFF), high/medium (Mauritius) or medium. Only the single Comorian stakeholder who completed the questionnaire thought that pr wi3MCID 3 BDC38SB9(n)-91 1 -91 1 -91 1 -9lthe aihwernr

Réunion/France

- Implementation of regulations to limit i

Activity 1.2: Define indicators and protocols for data collection for use in programme assessments

No progress reported.

Activity 1.3: Assess and document the economic costs and benefits of prevention, eradication, containment, and management of invasions in pilot sites as well as the costs of NO ACTION

The budget for the economics work was cut from €100,000 to €20,000.

Pilot Sites in Mayotte

Mayotte has changed its status from a territory to a department with effect from 1 January 2014. So when project started the relevant authorities agreed to work with the project on pilot sites but now the agreement is no longer valid

During the école thématique (June 2014) those from Mayotte talked about species to control and people from CBNM were interested in collaborating but no concrete plans have been produced.

An action plan for pilot site operations for Mayotte was produced but this was through DAAF (Direction de l'Alimentation, de l'Agriculture et de la Forêt) who have staff so there was no staff allocation in the action plan. They just needed the money specifically for the actions. But it was changed to go through the Conservatoire botanique national de Mascarin (CBNM) who did not have the staff.

The project can still work in close collaboration with Mayotte and other financial and administrative arrangements can be made for them (outside the project).

Pilot Sites in Seychelles

GH and OT visited Seychelles and discussed possibilities with stakeholders. Several potential pilot interventions were

Issue identified	Suggested Solutions
	plementing partners pre-identified during the three first years of the project and during the Mid-term review process. This alternative would allow a more programmatic approach to implement the pilot sites activities within IUCN and would enhance the communication potential and the visibility of the projects worldwide.
Insufficient support from project management: x Communication from project management was sporadic. x The retirement of GH at the end of January 2015 resulted in a loss of momentum as he was the main driving force behind the pilot site work.	x This issue should be resolved with the hiring of a new PM with technical expertise and a new Global Coordinator of the IUCN Global Invasive Species Initiative.
Too many sites: x The plan was to develop a total of eight pilot site (two in each of Comoros, Mauritius, Mayotte, and Seychelles) which might work in some cases but not in others.	x Reduce the number of pilot interventions to one per island. Two might be possible but this depends upon the scale of operations. The two sites proposed in the Comores, for example, would be difficult to implement as a great deal of support will be needed in terms of capacity building and planning, monitoring and evaluation.
Lack of time	x This issue cannot be fully resolved by a project extension as so much time has already been lost. The time constraint remains and must be managed by tight but realistic and mutually agreed timelines.

P

Issue identified

All

Issue identified	Suggested Solutions
from the financial unit in Nairobi.	need to frequently visit participating countries.
x Insufficient support for the project from within IUCN; e.g. the loss of staff who were working on invasives in IUCN Oceania.	x Make better use of the IUCN network that remains such as the ISSG, the Mascarene Island Plant Specialist Group, the IUCN French Committee (who are very committed to work on invasives), those working for IUCN in European Overseas Countries and Territories and IUCN staff in SIDS.
x Staff turnover. GH retired	

Issue identified	Suggested Solutions
x The EC Delegation was primarily interested in the regional benefits of the project.	guidance manual. The added value of being an

Issue identified	Suggested Solutions
cause of the lack of progress in the Invaz'iles Project.	

3.3.2. Institutional/Political Issues

Issues that relate to the IOC

Issue identified	Suggested Solutions
x The IOC has procedures that can slow down project implementation.	x Invaz'iles is not an IOC project per se so there may be scope to establish more streamlined processes than would be possible for projects implemented by IOC. x Move the project from IOC.
x When dealing with government the IOC does not always go through the correct channel. e.g. in Mauritius communications were directly from IOC to NPCS (National Parks and Conservation Service) but they must go through the parent ministry (MoAIFS - Ministry of Agro-Industry and Food Security) first.	x Establish and document clear lines of communication in the project to improve the efficiency of stakeholder interactions.

Finding the right entities to work with at national level

Issue identified	Suggested Solutions
x The entity chosen may not always be the right organisation to work with at national level, e.g. they have the capacity but are overwhelmed with projects or invasives is not their core mandate.	x Go beyond IUCN member organisations when looking for national partners.

This contrasts with the comment from a national stakeholder that “the project is not cost-effective because nothing has been done.”

Measures proposed to increase project cost-effectiveness are outlined below.

3.6. Sustainability

3.6.1. Sustainability at the national level

Degree to which the existing policy and institutional environment contributes to the longer term sustainability of the project's benefits at the national level

Supportive factor	Relevance to the project
Environment.	

Mauritius/Rodrigues

Supportive factor	Relevance to the project
x A stable government that can support the project.	Raise awareness among decision-makers by: x Developing a briefing package/information module to sensitise decision-makers on the magnitude of the IAS issue and the benefits of systematic IAS prevention and management. x Distilling an "elevator pitch for invasives" from this briefing. x Organising a regional workshop for decision-makers to deliver this information module. x Engaging political advocates for biodiversity as champions of IAS prevention and management and of the project. Didier Dogley of Seychelles the recently appointed Seychelles Minister of Environment and Ameenah Gurib-Fakim the newly appointed President of Mauritius could potentially fulfil this role. x Maximising the involvement of central government by engaging them through the IOC and the EC Delegation. x Following the example of South Africa, establish a financial case of ongoing management though pilot interventions to establish the economic costs of biological invasions and the benefits of management that can reframe IAS management as an "investment in ecological infrastructure/resilience."
x Support from some private sector landowners and businesses such as the Francois Leguat Tortoise Park in Rodrigues and private landowners who are restoring forest plots under the UNDP-GEF Mauritius PAN Project. x	x These private sector champions can support the project's objectives including pilot interventions.

Supportive factor	Relevance to the project
x Those working in the agricultural sector in Mauritius are familiar with the use of biocontrol as a vital pest management tool. Institutions such as the Mauritius Sugar Industry Research Institute (MSIRI) and the Department of Agriculture have considerable expertise in this area.	x Synergies with the agricultural sector can be explored so that relevant expertise is utilised and to ensure that invasives are managed as a cross-sectoral issue.
x The UNDP-GEF PAN expansion project.	x Links should be explored with this national initiative.
x The NIASS although it has not been costed nor implemented.	x Analyse the current status of NIASS under Result 4.
x A range of relevant IAS prevention and management efforts have been undertaken for species recovery and ecosystem restoration in Mauritius (including offshore islets and Rodrigues).	x These good practices can be highlighted in the global guidance m (s)4.4(Tf-0.0.6.1(7o6f8.0ppd no)1.9(r)43(nt)2.6(i

Supportive factor	Suggested project responses
other countries (e.g. South Africa and Australia) have potential for use in WIO Islands and biosecurity	

Issue identified	Suggested Solutions
<u>Changing priorities over space, time and among stakeholder groups leading to conflicts of interest:</u> The priority given to invasives is highly context specific. For example: x Invasives are more prioritised in Seychelles islands managed for conservation than on the mainland. x was considered to be a useful plant when it was introduced to Rodrigues several decades ago because the islanders faced an acute shortage of fuel wood and fodder at that time. Since then there has been a switch from wood to gas and the species is taking over valuable land. x Farmers in Comores value fast growing agroforestry trees such as despite their invasive tendencies.	x Acknowledge the potential conflicts of interest by adopting a highly inclusive definition of an invasive species such as:

Issue identified	Suggested Solutions

Issue identified	Suggested Solutions
curity legislation if goods from one country are allowed in without being subject to strict conditions. This can create a precedent which other countries can cite and exploit.	
<u>Staff turnover at senior governmental levels in project countries:</u> x In all countries there is a regular turnover of key individuals at senior levels in government. Generally the new person will have to learn about a topic such as invasive species and decision-making is slowed down while this individual is learning; a process which may take years if it happens at all.	x Engage high level decision-makers.

4. Conclusions and Lessons Learned

In its first three and a half years the Invaz'iles Project has clearly and substantially under-

or that these achievements were effectively negated in the minds of some key stakeholders by failures to progress in key areas.

The outstanding failure of the project to date has been the inability to progress on pilot site interventions. From the perspective of the participating islands the pilot sites are seen as the public face of the project although in terms of relative budget allocation they are clearly not the project's most important component. However, they are of great strategic value for the project and offer the potential for catalytic actions if the obstacles that relate to effective collaboration can be overcome.

It was not clear whether the interconnections among the project's activities had been explored in detail. For example the review of the draft global guidance manual and the pilot site management guidelines provided excell(t)-6.34662.5(o)p(a)-4(n)-6.1(c(h)-

- Guidance on international instruments of relevance to IAS (initiated under GRIS - Global Register of Invasive Species).
- A review of national and regional projects that directly or indirectly have implications for invasive species prevention and management.

- Contract an editor(s)/facilitator(s) to capture and consolidate the information provided.
- Contract a drafting team to assist with inputs from each island.

Activity 1.2: Define indicators and protocols for data collection for use in programme assessments

- Define activity and result indicators when formulating pilot intervention plans (carried out in conjunction with Activity 4.2).

Activity 1.3: Assess and document the economic costs and benefits of prevention, eradication, containment, and management of invasions in pilot sites as well as the costs of NO ACTION

- Investigate the feasibility of

- PM to work in close collaboration with GIER and ISSG to disseminate information.

5.2.

Activity 3.1: Conduct preliminary technical missions to scope levels of biological invasions and assess capacity needs of key stakeholders

- Develop a rapid capacity assessment for invasive species prevention and management in the region as a basis for capacity building through formal instruction and exchange visits (see Activity 1.6).

Activity 3.2: Define and agree on criteria for selection of pilot sites

- Technical missions to agree pilot activities and produce a costed action plan.
- Modified pilot selection criteria to be agreed upon at the Project Steering Committee Meeting held to finalise the revised project logframe.

Other possible pilot interventions

The following potential pilot interventions were suggested:

- Rat eradications from offshore islets.
- Development of a national invasive species strategy.
- A baseline study of the extent and impact of invasive plants in Comores.

5.3.3. Mauritius/Rodrigues

Recommended Pilot Site Intervention

There are several factors that support the implementation of pilot site activities in Rodrigues. The RRA has prioritised the prevention and management of invasives species as part of its branding of Rodrigues as an ecological island, there are good existing collaborations between MWF, RRA and the Forestry Service Rodrigues, the local community is engaged and many local people are actively participating in invasive plant management and ecosystem restoration work. Last but not least, is widely perceived as a threat to the ecosystems and livelihoods throughout the island of Rodrigues.

Current control efforts, while laudable, are not keeping pace with the rate of spread. Biological control needs to be initiated as a matter of urgency. The pilot programme could comprise of the following activities: A visit from biocontrol experts from CSRIO - Commonwealth Scientif2.6(o)Tw (-)u9(n6)3.1(d)-6.2lven6dnstrialese-3.1(r)-1.c4(h)-6.1O(r)-7.1(r)-1.gu9(n6)3.2(i)-13(

economics of the many vertebrate eradications undertaken on Seychelles' islands. This information can be incorporated into the manual.

Activity 4.4: Finalise, translate, publish and disseminate the Global Guidance on the Prevention and Management of Biological Invasions on Islands

- Finalise the manual and publish in English, French and Spanish.

Activity 4.5: Officially launch the Guidance Manual and publicise

- Use the IUCN's network to launch and publicise the manual.

5.5. Recommendations to address obstacles to project implementation, and maximise cost-

Modify the process of pilot site selection and management

- The total number of potential pilot sites should be reduced.
- Potentially use pilot (which may or may not be site-based) to add value to existing initiatives if compatible with project objectives.
- Pilot site guidelines, plans, management structures and budgets should be developed in close collaboration with relevant partners at the national/island level.
- W

- Review the membership of the SC so that more diverse perspectives are introduced. For example representatives of relevant projects could be represented.
- Circulate clear project status reports to the SC with details of actions taken, degree of progress, challenges and opportunities and suggested next steps
- Provide easy to read summaries of project reports.
- Ensure that the SC meets at least one per year.
- Hold SC meetings in French insofar as possible.
- Make use of existing regional gatherings to hold SC or technical working group meetings opportunistically.
-

- Collaborate closely with relevant projects selected under the call for proposals scheme as appropriate.

FFEM Coastal Zone Management Project

- Ensure that actions do not inadvertently contribute to biological invasions, for example through widespread planting of potentially invasive species for erosion control.
- Work with the FFEM project to facilitate networking with those working in coastal management in WIO Islands including TAFF.
- Work with the FFEM Project to facilitate awareness raising among the stakeholders to ensure that IAS is seen as a cross-cutting issue.

Renewable Energy Programme

- Ensure that actions do not inadvertently contribute to biological invasions, for example through widespread planting of potentially invasive species for erosion control.

PRPV Programme

- Collaborate to bring together those working on biological invasions that affect agriculture and biodiversity to share information, awareness raising tools, expertise, and management approaches.

IUCN BIOPAMA Programme

- Establish what relevant information is available for the participating countries through BIOPAMA and input invasive species information for incorporation into the BIOPAMA databases where possible.

FEDER Herbarium Network Project

- It is important to establish links with herbaria throughout the region so that invasives remains a priority for them, especially in Comores where the herbarium is being established.

Explore synergies with national projects

Comores

- Work in close collaboration with the UNDP-GEF protected area project to help ensure that invasives are effectively incorporao-

5.5.5. Develop a methodology for monitoring project outcomes and potentially impacts

Thus far the project's reporting system has emphasised activities and not results (outcomes and impacts). In the early stages of a project this is a justified course of action. Even though the Invaz'iles Project has been going for three and a half years it is still in its early stages in terms of progress achieved. However, it would be valuable to initiate an internal project monitoring and evaluation system that addresses outcomes, and possibly impacts as well, as soon as possible. There are a number of possible outcome and impact assessment methodologies available and advice can be sought from M&Habe

6. Appendices

Appendix 1: Review terms of reference

Mid Term Review

Preparation and testing of a comprehensive model for preventing and managing the spread of invasive species on island ecosystems

Terms of Reference (TOR)

24th of April 2015, final version

A. Background

This action has been prepared to address the need for a set of globally-relevant guidance for the prevention and management of invasive alien species on islands around the world. The project aimed to build on the work carried out by programmes and projects around the world over the last two decades on prevention, containment, eradication and strategic management of invading species as well as legal and policy formulations and apply this to the Western Indian Ocean (WIO) islands.

The Overall Objective of the project is ***to reduce the spread and impact of biological invasions upon people and biodiversity of islands.***

The Specific Objective is ***to enhance the systems and strategies in the Small Island Developing States and in particular those in the Western Indian Ocean region, to efficiently prevent and manage biological invasions.*** The final intended outcome was global guidance of relevance to main island groups around the world while the main effort of capacity building and ecosystem management is to be carried out in the WIO.

To achieve the Specific Objective, four complementary results were defined:

Result 1: ***Knowledge*** – Increased knowledge, awareness and expertise on the successful prevention and management of the spread of biological invasions on islands

Result 2: ***Partnerships*** – Partnerships developed, established or strengthened to enhance collaborative management of biological invasions on islands and island states between countries, governments and non-governmental bodies

Result 3: ***Management*** – Prevention and managed of biological invasions improved in selected pilot sites as indicators of good general practice

Result 4: ***Strategies*** – Strategies to strengthen national, regional and global policies and actions to better prevent and manage biological invasions on islands developed and agreed upon.

The full description of the project is provided for in Annex 1.

B. Context

The primary target areas for this project include the islands and islets in Mauritius, Seychelles, Comores and Mayotte, as well as French island territories in the IO region. Within these target islands, the pre-project situation varied from extremely serious invasions by alien plants and several domestic and wild vertebrates and micro-organisms to lower levels of the same – all with some impacts on local livelihoods. In some cases, there are islands and islets that are not permanently occ

C. Rationale or Purpose for the Mid Term Review

The project was initiated on the 1st of February 2012 and was scheduled to have a mid-term review. Since inception the project has suffered delays but nevertheless has delivered against some of its

*Note: An initial draft of the review matrix is provided for in Annex 3. The reviewer will be required to further refine these questions and develop a core set of indicators as part of the proposed methodology and process – which will be reviewed and approved by the EC delegation in Mauritius.

F. Methodology

In further developing the methodology and approach, the reviewer should make reference to and ensure that the review adheres to the minimum standards of the IUCN Monitoring and Evaluation Policy (Annex 4).

The review will be conducted through:

- A review of key literature (pertaining to relevant national and regional priorities, global standards and good practice, as well as the project itself);
- One to one interviews with key informants;
- Field visits to a select number of potential pilot sites; and
- A focused group discussion with the Steering Committee also involving the IOC around the preliminary review findings and recommendations.

The review should seek to ensure that findings and recommendations are based on an in-depth understanding of the context and realities within which the project is operating – taking into account existing priorities as well as capacities and willingness to engage (both during and after the duration of the project). Additionally, the review should endeavour to ensure that all findings are substantiated with supportive evidence (qualitative and quantitative).

Special attention should be brought to complementarities of the project with other ongoing regional projects, especially those based at the IOC (EU-Biodiversity; FFEM- gestion zones cotieres; possibly Island).

Based on the assessment above, the reviewer should provide concrete recommendations for the remainder of the project, including any reorientations or/modifications required to achieve the objective of the project, including on methodology, organisation, activities, and results. Orientation documents should include a proposed revised logframe and scheduling, amended project description and cost repartition as relevant, and implementation proposals to ensure a successful completion of the project.

G. Qualifications of the Reviewer

-2(c5(l)4ew)-17.5(er)]TJ 03.89TwTw 15.554 0 Td ( )Tj EMC /47

The reviewer will be selected based on the following criteria:

Annex 1:

https://www.dropbox.com/sh/sshh1dt2hrfesgw/AADzljalxVT28k49FDBdyJOfa?dl=0

Annex 2:

https://www.dropbox.com/sh/q55z2iqefns3yn1/AAAOOcunAQNAKkTavpYI_xtQa?dl=0

Annex 4:

http://cmsdata.iucn.org/downloads/the_iucn_monitoring_and_evaluation_policy_2013.pdf

Appendix 2: Data collection instruments

Mid Term Review Questionnaire

Can you suggest ways in which the project's design could be adapted to strengthen its relevance to regional level priorities?

Yes		No	

If yes please list suggestions in the box below

2. To what extent has the project has delivered the planned actions in the four results areas?

2.1) Knowledge: Increased knowledge, awareness and expertise on the successful prevention and management of the spread of biological invasions on islands

Substantially

[redacted]

5.2. What tangible measures have been taken (inside and outside the project) to ensure that the benefits realized through this project will be sustained over the long term?

5.2.1) At the national level:

Many		Some		None		Don't know	

Please give examples of relevant tangible measures in your country/territory?

Date	Activity
23 June	Meeting with Hubert Grandjean (Attaché, EC Delegation to Mauritius, Comores and Seychelles)
	Briefing meeting with Eric Vanhalewyn (First Secretary and Head of Section, EC Delegation to Mauritius, Comores and Seychelles)
	Journey to Reunion
24 June	Journey to Comores
	Meeting with Yahaya Ibrahim (Scientifique CNDRS - Musée National des Comores)
25 June	Meeting with stakeholders from the Université de Comores (Herbarium and Department of Science)
	Further discussions with Yahaya Ibrahim about pilot sites in Comores

Name	Institution	Job title	Stakeholder group	Consultation format
	(CNDRS)			
Tatayah, Vikash	Mauritian Wildlife Foundation			

Soubeyran, Y., Meyer, J., Lebouvier, M, De Thoisy, B., Lavergne, C., Urtizberea. F. and F. Kirchner (2014). Dealing with invasive alien species in the French overseas territories: results and benefits of a 7-year Initiative. Biological invasions 17, 545-554.

SPREP (2009). Guidelines for invasive species management in the Pacific: A Pacific strategy for managing pests, weeds and other invasive species / compiled by Alan Tye. SPREP - Apia, Samoa.

Veitch, C. R.; Clout, M. N. and Towns, D. R. (eds.) 2011. Island Invasives: Eradication and Management.

To

Appendix 6: Revised proposed logframe

Revised project logframe and project activities (based on the results of the Mid-term review and the meeting with the EC delegation on the 17th of July 2015)

	Intervention logic	Objectively verifiable indicators of achievement	Sources and means of verification	Assumptions
Objective(s)				
	To reduce of the spread and impact of biological i(gi)-0ng w i2(e 1(t)9.9e9ph5 0a26(lo)5t82426)8(b)10(a)4(s)6(e)aa(gi)-0ng w82.1(.7(i)8(v)6.1(e()1.7(s)t)6(a			

		and documented		
		Guidance manual on best practices produces and disseminated,	Copies distributed, number of download, websites analytics	
		- Training schedules for technical staff and other stakeholders in invasion prevention and management developed and implemented	Training session assessments, training course documents	Potential partners willing to participate
Result 2: Partnerships	Partnerships to enhance collaborative management of biological invasions in islands and island states established and/or strengthened between countries, governments and non-governmental bodies	Partnerships signed and being implemented effectively	Signed Partnership agreements (for example between institutions and for pilot interventions)	Political tension over contested island(s) do not prevent technical exchange and cooperation
		- Network of technical experts established and fully operational	Regular implementation reports	
		- Mechanisms established and implemented to promote sustained collaboration between WIO Island states	WIO invasives network reports	
		- Data exchange and compatibility between systems regional and global is improved	WIO invasives network reports and project reports.	Partners/countries willing to participate and agree on common standards
Result 3: Management	Prevention and management of biological invasions improved for selected pilot interventions as indicators of general practice	- Pilot intervention plans developed and being implemented in Comores, Rodrigues and Seychell t Tw 3.41 0(i)-1(n)-62(ue)9(s/7(r)]TJ-0.004 h(l)5(oB)2.6(s)8.6.9(l)-0.9(		

				pilot interventions
		- Lessons and experiences from pilot interventions identified, documented and shared widely	WIONIS network reports; project report.	Partners participating actively in the implementation of pilot interventions
Result 4: Strategies	Strength and weaknesses of strategies at national, regional and global level documented	- A comprehensive baseline of existing assessments on the effectiveness of institutional arrangements, policies and regulations documented and set of globally relevant guidelines and procedures developed and widely shared	Global guidance manual published	Countries willing
		- Common IAS indicators and criteria for monitoring & evaluation of IAS systems are available	Project reports	
		- Development and implementation of awareness raising activities for decision-makers on the importance prevention and management of biological invasions on islands	Participation of decision-makers in awareness activities	Willingness of decision-makers to participate in awareness raising activities

Activities	

Activity 1.1:

Result 1,
Knowledge

	Activity 3.4: Train and mentor WIO island pilot interventions coordinators and other practitioners and relevant people. Activity 3.5: Develop and implement pilot intervention plans Activity 3.6: Develop and implement a communication strategy to ensure key stakeholders are aware and willing to engage in pilot intervention activities Activity 3.7: Learn from progress and performance of pilot interventions and disseminate the lessons learnt (through the WIONIS network)
Result 4: Strategies	Activity 4.1: Assess strengths and weaknesses of strategies and their implementation at national, regional and global level and provide relevant recommendations to address the gaps in the WIO islands. Activity 4.2: Develop and propose operational indicators for invasives species prevention and management in islands.
