Table of Contents

ACKNOWLEDGEMENTS 4
EXECUTIVE SUMMARY 5
ACRONYMS 9
CHAPTER 1 INTRODUCTION 11
BACKGROUND 11
EVALUATION PURPOSE, SCOPE AND QUESTION FRAMEWORK 12

PHASE TWO? 56
CHAPTER 6 RECOMMENDATIONS 58
RECOMMENDED ADJUSTMENTS DURING THE REMAINING PERIOD OF THIS PHASE 65
RECOMMENDATIONS FOR STRENGTHENING IN PHASE 2 66
CHAPTER 7 CONCLUSIONS 68
ANNEX A EVALUATION TERMS OF REFERENCE. 70
ANNEX B: EVALUATION FRAMEWORK 83
ANNEX C. DOCUMENTS REVIEWED OR CITED 89
ANNEX D. LIST OF INTERVIEWEES 91
ANNEX E: PROJECT FIELD VISIT REPORTS 97
ANNEX F: TWEAKING THE EXISTING LOGFRAME 115
ANNEX G: POSSIBLE LOGFRAME FOR THE FUTURE 121

Chris Hails cjhails@gmail.com
Sheila O'Connor ocosheila@gmail.com
Ghazala Shahabuddin

knowledge of habitat usage and distribution is becoming understood in places where it was poorly known. Anti-poaching efforts have received much-needed support although it is too early to assess

Table 1. Details of Ongoing Projects in ITHC

1337 Wildlife Conservation Society (WCS)	Aug 2015	Myanmar, India	Northern Myanmar-India border	6 PAs-including Kaziranga TR (India); Hukaung Valley WLS and Htamanthi WLS in Myanmar- and connecting forests/settlements
1490 Wildlife Asia	April 2017	Myanmar	Dawna and Karen Hills of South-western Myanmar	Complex of Community Forests, proposed PAs and existing PAs including Kweekoh and Yumuyoh

Table 2. Budgets allocated by project (as of October 2017).

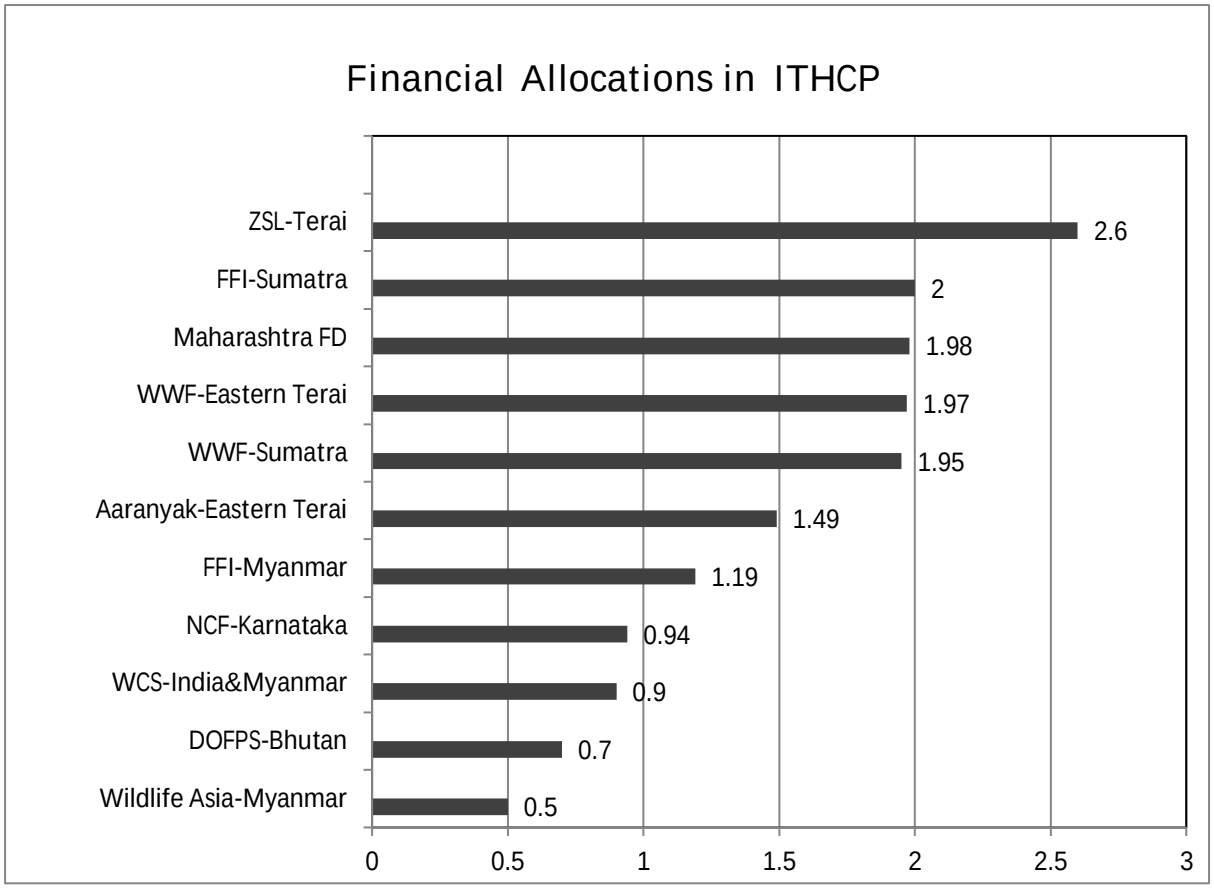

Figure 1. ITHCP Project Portfolio (as of October 2017).

EVALUATION PROCESS AND DATA COLLECTION TOOLS

The evaluators have conducted this review and analysis in an independent and unbiaendumbiald ioucndn ha20(n anuc

Table 3: Sample Sizes for Various Methodological Approaches

CHAPTER 2 STRATEGIC RELEVANCE AND DESIGN

This chapter focuses on the extent to which the ITHCP programme is aligned to the Global Tiger Recovery Programme (GTRP), the IUCN Programme 2017-2020, and National Tiger Action Plans. It also explores whether the programme design (including any nested projects) represents a necessary, sufficient, and appropriate approach to achieve positive changes in the status of tigers and their habitat, as well as any human beneficiaries that may be targeted by the work. The focal questions below served as a guide to structure interview and survey questions, and they help frame the findings but they are not necessarily answered specifically in each chapter.

identified as the area where KfW and IUCN could have the greatest impact, and where there was greatest need. The originators of the programme believed that there was already a lot of investment and activity in abating the international trade in tiger and tiger parts, and in the development of

Building a programme wide team that engages in evaluation, learning and sharing in a more formal “system” of adaptive management.

Design Elements	Assessment of ITHCP
Strategic action plan- goals, objectives, actions and theory of change, assumptions	At the programme level a simple log frame exists that was proposed by the initial feasibi

Design Elements	Assessment of ITHCP
informal analysis, adaptation and lessons	first for a programme of this size for IUCN, and is a positive step forward. Also, the ITHCP Secretariat developed a self-assessment form for the project activities. However as yet there is not a sufficient focus on evaluation, learning and sharing. More formal and informal mechanisms that bring together the results of any type of evaluation, of monitoring exercises, and of lessons learned are needed. The ITHCP Secretariat seems to understand the importance of thi

complemented by other approaches, e.g. policy, advocacy, and legislative improvements , which may bring programme level impacts. Futures strategies and partners will likely include private and public-sector engagement and development, e.g. palm oil or development infrastructure. It will also be worthwhile to revisit the approaches and activities linked to livelihood improvement, as they seem to be somewhat ad hoc, short term and not yet designed for multiplication. IUCN and KfW should also explore financial sustainability and the role that they can play in donor coordination, engagement with GTF and other international bodies that are important in the T x 2 (doubling tiger numbers across their range) challenge.

CHAPTER 3 EFFICIENCY

In this chapter, we examine how well resources and inputs (funds, expertise, time) have been converted into programmatic results. Efficiency considers both financial and human resources and examines how staff, partners, and stakeholders are organized, communicating, and operating. It is also important to assess the role and added value of IUCN as an implementing agency including

Table 6: Details of Expenditure in ITHCP Projects

Project Code and Lead	Starting Date	Approx. Duration (assume end Dec 2018)	Expenditure as of June 2017 (% above or below expected)
1337 WCS (India & Myanmar)	Aug 2015	3.5 years	-37.8
1311 WWF-Germany (Sumatra)	Aug 2015	3.5 years	-26.7
1334 Aaranyak (India)	Oct 2015	3 years	-19.8
1338 FFI- Myanmar	Dec 2015	3 years	-41.0
1341 DoFPS Bhutan-RMNP	Dec 2015	3 years	-41.4
1309 WWF-Germany (Nepal-India)	Feb 2016	3 years	+1.6
1327 ZSL Terai			

hand), in a systematic monitoring and supervision cycle. It is possible to borrow skills and expertise for short periods to undertake tasks such as project monitoring. The Terms of Reference of the PAC, includes both grant selection and monitoring, but the members have not been commissioned to carry out any supervisory activity since completing the project selection. Further they reported that they had not been involved in project supervision and monitoring, though their TOR (Terms of Reference) did mention project reviews.

It is possible that the extra time spent with Grantees for proposal revisions (2015-16), did not allow the Secretariat time for closer supervision of projects that had started earlier during August-

a range of social/environmental impacts and trade-offs in most such projects. The review process ends in the preparation of an ESMP (Environmental and Social Management Plan) that lists the mitigation measures and that should be put in place at project initiation. ESMS should ideally be carried out after the social baseline study, and completed during the project preparatory or project inception phase. This is essential so that ESMS screening of potential impacts is done based on this data, also project design can be modified (if needed) and risks, effectively managed, during implementation. However, for several projects, the ESMS review process could not be completed as anticipated, and spilled over into the implementation phase. Consequently, the ESMP is not yet in place in several projects.

The reason for delays and difficulties in ESMS review process seems to be weak understanding of its relevance amongst most of the Grantees, who perceive it as a stand-alone process, rather than an integral part of project design and implementation. Most Grantees also felt that the process was complex and that they lacked the skills/capacity to effectively anchor the process. In general, project teams found themselves unable to complete the review process satisfactorily or to leverage it for better project design and management. Some projects took on a specialised consultant to do the work (e.g. WWF-Sumatra) and a few iterations were then required to produce the ESMP. Such problems are understandable given that the ESMS review process of IUCN was undertaken for the first time in ITHCP. Despite these challenges some project leaders said that they had learned a lot from the process and that it had strengthened their projects, especially in creating an understanding of certain human dimensions that they may have otherwise overlooked.

In order to make the ESMS process more effective, we suggest that it should be done immediately following, or overlapping, with the baseline socio-economic study, and that both should be completed B/F4 11 Iaproje, and that both should be

CHAPTER 4 EFFECTIVENESS

This chapter focuses on whether the programme is doing what it said it would do, and whether we

the evaluation found that the delivery against Output 2 is of high interest in certain countries, such as India and Nepal and that activities (Box 5) are moving forward; however, it is too early to tell at a programme level whether the output is on track to being achieved.

Box 5. Typical specific activities for Output 2.

Preventive and responsive Human/Tiger conflict measures are operational
Develop insurance schemes
Predator proof mechanisms/ response

In the IUCN mid-term report the self-assessment generated by the projects and ITHCP Secretariat had 33 cells that could be assessed and that were related to HTC (11 projects x three main activities). It was noted that only 19 cells were completed, suggesting or confirming either that HTC activities are not important in all areas, or that this work is not yet planned, or there is no data available. It may also be because there are low levels of HTC in project areas such as in FFI Myanmar and WWF Sumatra, due to overall very low density of tigers. There is more conflict due to bears and crocodiles in central and south Sumatra rather than tigers. In Aaranyak project area, too, elephants are more of an issue than tigers. Having a programme level output on HTC mitigation implies that conflict is one of the key problems /threats across the portfolio. This did not seem to be the case amongst ITHCP projects at the present time, although there is a need to keep watch as tiger populations grow so may the conflicts. But of course, taking precautionary steps for HTC fits well with building community support. For those projects that did report on their HTC activities, in general they felt they were going well. Some positive examples of this were noted during site visits in Nepal and India, and also that it was a significant topic of discussion and exchange at the Pench ITHCP workshop.

The recent addition to the ITHCP portfolio of a project exploring HTC best practices should also be better understood in terms of its added value to delivering on this output. From the mid-term report the recommendation for this project states that "the study focus only on ITHCP projects as they cover the entire suite of different human tiger conflict scenarios that occur throughout the tiger range (i.e. rare interactions, livestock predation, human fatality etc.)". It would be helpful to have a logic chain that links this project to the indicator for Output 2.

As with Output 1 which focussed on resources and capacities for effective management, evaluating progress towards this HTC output is challenged by the lack of clarity in the output, the indicator (Box 6), and the target; all of them would benefit from being more measurable, and having "milestones" set to look at progress over time. Baselines did not appear to be available across all projects. Another example of ways in which these elements could be improved to allow for better assessment of effectiveness is that the output might be more powerful (and measurable) if it read something like this- *Zero HT conflicts occur in target communities* (to be further defined for each project). In

Box 6: Indicators for Output 2: Human-tiger conflicts are mitigated.

-Mitigation of human-tiger conflicts in the villages improves and situation with regard to livestock losses according to perception of communities

Target: Communities in and adjacent to target tiger habitats report on an improved situation with regard to HTC, including improved situation with regard to livestock and human losses.

Areas for Improvement and Recommendations

Based on the ITHCP instigated self-assessment (undertaken for the mid-term report) one conclusion was that "the activities that are progressing well include those focused on the monitoring of tiger and prey populations, and poaching and human-wildlife conflict mitigation. The activities that are taking longer to become operational due to the need to develop infrastructure include those focused on protected area management and the provision of alternative livelihoods for local communities."

The evaluation noted that there is an absence of activities at programme level around influence,

particular context. Be clear on the "right" scale for intervention, and clearly define how to multiply or leverage more from funding, activities and partnerships.

- Define programme level strategic actions such as influencing global tiger conservation efforts perhaps including larger funding opportunities.
- Enlarge the capacity of the coordination team to include programme/project cycle and adaptive management expertise.

CHAPTER 5 SUSTAINABILITY AND IMPACT

Tiger conservation has deep and intractable challenges that extend over many decades, and the changes required go beyond the financial sustainability of the programme of work itself. The assessment of impact and sustainability will consider the extent to which the results to date (bearing in mind the short implementation period of ITHCP at the time of the evaluation) are likely to persist and grow as needed to sustain tiger populations and their habitats across selected parts of their range. In many ways, assessing sustainability is testing whether or not a conservation initiative has been designed well, and is implementing an adaptive management approach, since the level of engagement of stakeholders, the learning that is shared, and the persistence of outcomes will ultimately determine the resilience of the programme/project beyond its lifetime.

Focal Questions:

What measures/enabling conditions (e.g. policy, legislation, capacity,

EARLY DAYS BUT ENCOURAGING SIGNS FOR SUSTAINABILITY AND IMPACT

In many ways sustainability and impact go hand-in-hand when dealing with tiger conservation. We can only be sure of real long-term impacts which stabilise tiger populations and their habitat when change is adopted permanently by those with influence over the long-term threats and drivers. In this programme, the primary stakeholders with such influence are governments and local communities living in proximity to tiger populations. There are positive signs (see below) that the main elements of the programme are on a trajectory to be sustainable in the projects areas given sufficient, and consistent, time and support.

Due to the relatively short period for implementation prior to this review, there is rather little we can conclude with certainty in the form of real long-term impacts at this current time. Several of the projects are demonstrating encouraging results that have positive implications for long-term success:

impact will be less deniable and that much greater. This is what we mean when referring to "Programme-level" conclusions and influences; in shorthand we speak of the "whole being greater than the sum of the parts", skilfully managed 2+2 can equal 5!

At the current time, the ITHCP is not well-situated to draw up programme-level conclusions and lessons in this way. The current design, and on-going monitoring work is very much project based and activity focussed (see Chapter 2: Strategic Relevance and Design). In this report we make suggestions for how this could be corrected, and we have been informed that the Secretariat has some records which can be used as a starting point.

Armed with broader conclusions drawn from the whole suite of projects the Secretariat, or IUCN and

expatriate origin and this seems to be in situations w

4. All projects report an increase in using management effectiveness tools of various types to help identify issues, and improve management.

Improved livelihoods are still developing and outreach is still expanding so it is hard to say whether there is yet any impact. Although some projects have established good baselines, others are still working on these, and follow-up social surveys have not yet been repeated. This requires huge effort and so will take time. Nonetheless several projects report a marked improvement in interest and sympathy for the conservation efforts amongst local communities even if this is anecdotal. More time is needed for this to be completely regarded as an impact. The biggest challenge for the community work is how to magnify it. Some of the projects have made huge efforts to reach out to villages and households (the ITHCP Secretariat reports a total of 41,000 beneficiaries, all of under-privileged social groups), but in the densely populated landscapes of South and South-east Asia there still remains a huge outreach needed to change the habits of a sufficient people number of to be able to claim enough has been done. Furthermore, in the absence of a systematic assessment of threats and drivers it remains uncertain as to the real impact on the ITHCP Outcome. To enable scaling up of the results to date, adoption of the best lessons and examples by a range of government departments and development agencies would seem to be the best course of action.

In conclusion, despite the short time-frame for implementation, there are clear signs of impacts emerging from the work. Direct attribution to the KfW programme is much harder to ascribe due to the prior history of work in this field, and the experience and lessons upon which ITHCP is standing. However, the ITHCP seems to be filling some niches which were previously neglected and by astute application of the funds is having its own very positive effects on the overall challenge.

PHASE TWO?

There has been some discussion for a Phase 2 of the ITHCP. In the opinion of the reviewers, this would be highly desirable given the long-term nature of the solutions to the opportunities of leveraging both development gains and ecosystem security in the context of tiger conservation.

It is beyond the scope of this evaluation to give full consideration to the establishment of a Trust Fund which was suggested in the original feasibility study submitted to KfW in 2013. Given the current financial markets an “interest-bearing trust fund” at the current level of investment would not yield sufficient annual income to be interesting for this project. It is possible that other donors could be attracted to such a fund, and if it were a “sinking fund” (i.e. allowing spend-down of the original capital in addition to the earned interest) then this could perhaps spread the current level of investment over several years more years than is currently available. However, the time involved in sourcing donors and setting up and running such a fund may be prohibitive and would require an in-depth cost-benefit analysis.

Given the scale of the challenge of the Global Tiger Recovery Programme (GTRP) expanded funding is well warranted, and the ITHCP is well-placed to be a leader in that effort. In 2018 the GTF have been commissioned to carry out a “stock-taking” study of the progress of implementation of the

CHAPTER 6 RECOMMENDATIONS

Throughout this evaluation report we have recorded positive findings and areas that are proving to be challenging and require additional work. In this chapter, we bring together a core set of recommendations that are divided into 1) those which could/would involve adjustments during the remaining period of the current phase of ITHCP, and 2) those that would help strengthen IUCN's role in tiger conservation globally and regionally, with a strong portfolio of tiger projects and could be adopted in the recommended Phase 2 of this Programme.

We begin this chapter with a table (Table 8) that summarizes the results of the evaluation framework assessment tool used by the evaluation team. The tool asked the evaluators to score independently against 16 criteria which form the fundamentals of the evaluation framework and questions. By sharing this here, we aim to display some, not all, linkages between our findings and our recommendations. Other supporting information is found in the body of the report.

Areas that stand out as working well to very well include work associated with strategic relevance, focus on core issues, progress on activity, ways of operating and some aspects on sustainability. The weaker areas where improvements could influence ITHCPs' process, practice and results include design, monitoring, evaluation and learning- adaptive management- in the programme and project cycle as well as scaling up mechanisms, and evidence of the status of targets and the level of attribution.

Rating/Score	Description of Strong Performance	Average

Rating/Score	Description of Strong Performance	Average Score	Evaluator Brief Justification [Combined]
			and creating learning mechanisms and running workshops. It is recognised that

Rating/Score	Description of Strong Performance	Average Score	Evaluator Brief Justification [Combined]
	5. Actions have been identified under the ESMP and implemented and monitored.	2.2	The plans have been developed with some difficulty partly because the ESMS is new to IUCN, comes across as quite complicated, The approaches can be difficult to translate to the field, and it is presently disconnected from project/programme design and implementation as seen as separate. Not yet clear what actions have been triggered. Having said that, many projects seem to have learned from the exercise. Monitoring of ESMPs will move forward when the plans have been completed and implemented fully.
Impact	1. Most/all goals/outcomes—stated		

Rating/Score	Description of Strong Performance	Average Score	Evaluator Brief Justification [Combined]
Sustainability	1. Most or all factors for ensuring sustainability of results/impacts are being or have been established.	2.7	The selection of some larger NGOs or Government Departments for implementation lends itself to sustainability. In addition, linking the projects to national level Tiger Action Plans in most cases also helps to ensuring sustainability. However, there is not sufficient emphasis on general sustainability through creating/strengthening enabling conditions (e.g. capacity, policy and legislation), nor on how to influence larger contextual issues that are likely to affect conservation initiatives, e.g. political and social change, large scale development.
	2. Scaling up mechanisms have been put in place with risks and assumptions re-assessed and addressed.	1.7	Most scaling up depends upon governments adopting the interventions. There are few signs of searching for permanent solutions or for "scaling up" the results of 11 projects into something bigger. Mechanisms not fully used for assessment of risks and assumptions and understanding how they might affect results, impact andt affect results, [(a)4(ndt)10(a)5(uf)5(ec [[((mp0≥30(mpact)p0≥)5(on)-21(l)5(en

RECOMMENDED ADJUSTMENTS DURING THE REMAINING PERIOD OF THIS PHASE

Most of the proposals below touch on several evaluation framework elements although they are only listed once.

Design and programme/project adaptive management. To some extent, the ITHCP seems to be

Grantees should be required to carry out a social analysis as a part of their design phase, on which the ESMS screening of potential impacts can be done.

Sustainability.

22. Look for additional investors from sources already well-connected with IUCN so that the full benefit of the lessons learned from Phase 1 can be realised and applied more widely.
23. Capacity-building should be built-in as an intrinsic component of the ITHCP, to enhance skills such as project management, social survey methods, reporting and monitoring. This was mentioned as one of the important hurdles to effectiveness by several stakeholders.
24. Systems need to be created for regional networking and knowledge/skill-sharing, which can help synergise tiger conservation efforts at the landscape level.

Strategic Approaches.

25. Continue to develop the landscape approach with people at its core, but expand multiplication methods and other strategies such as policy and advocacy and target additional actors, e.g. private sector or development infrastructure operators and funders.

CHAPTER 7 CONCLUSIONS

IUCN and KfW are relative newcomers to the tiger conservation landscape. They bring a unique partnership of a science based and biodiversity oriented international conservation union with 1,300 members and 10,000 experts, and the German Government through KfW,with a development bank's perspective on people and environment, experience in the region, and expertise on development challenges.

ITHCP focuses on core tiger conservation issues, and is beginning to make important contributions as its projects get up and running and activities are rolled out and implemented. ITHCP has been able to mobilise 100+ partner organisations in this endeavour. The strategic approaches that are most favoured and most successful are those concerning protected area management and law enforcement, although with barely three years into the Programme they still have some way to go to be on track to deliver on outcomes. The programme and its projects focus heavily on human tiger

BOX 9: SOME THOUGHTS ON GRANTS PROGRAMMES IN IUCN

IUCN is a good choice for agencies wishing to deliver conservation results via grants programmes. It manages the world's largest network of environmental experts, is politically neutral, has good relationships with both the public (government and NGO) and private sectors, and has a global network of offices. It operates in a highly transparent manner and has procedures and systems which are sound enough to satisfy the rigours of being a GEF implementing agency.

Integrated Habitat Conservation and Eco-development in Vidharba Tiger Landscape	1487 Nagpur	India	Department of Forests, Govt. of Maharashtra	Dec-16	Dec-18	1,986,802
Karen Wildlife Conservation Initiative (KWCI)- Conserving tigers and indigenous knowledge in the Dawna-Karen Hills, Myanmar	1490 Wildlife Asia	Myanmar	Wildlife Asia, Karen State	Apr-17	Dec-18	499,985
					total	15,643,217

More details on the individual projects available here: https://www.iucn.org/sites/dev/files/content/documents/ithcp_project_portfolio_snapshots_april_2017_8mo.pdf

Purpose and Objectives of the Evaluation

The overall purpose of the midterm review is to strengthen ITHCP as a grantmaking mechanism and means of delivering outcomes and impacts for integrated habitat and tiger conservation. To that end, the specific objectives of the evaluation are to:

1. To assess the relevance and appropriateness of the ITHCP approach to the challenges and constraints faced by Grantees, local beneficiaries and tigers/tiger conservation in the project areas.
2. To assess the effectiveness of the ITHCP and its projects in achieving early markers of programme and project outcomes and to analyse key un t/fnstraints faced by

A draft evaluation matrix with sub-questions for each of the above key evaluation questions is attached and expected to be finalized by the evaluation team in the inception phase of the review.

Intended Uses and Users

This midterm review is commissioned by KfW. The main users and uses of the evaluation are expected to be:

- IUCN and ITHCP management to adjust its efforts in grantmaking and supporting the delivery of conservation action, outcomes and impacts at the midterm of the programme;
- The Director General of IUCN for the purpose of taking decisions on other grant-making schemes;
- The Director of the IUCN Biodiversity Conservation Group for the purpose of managing the ITHCP;
- The IUCN Strategic Partnerships Unit as a key audience;
- KfW to adjust their support for tiger conservation and integrated grantmaking schemes (e.g Trans-frontier Conservation Areas in Southern Africa);
- Individual project managers to align themselves with programme level objectives and as learning for large NGOs' own tiger programmes for future collaboration;
- The Programme Council for the purpose of improving the governance of the IUCN-KfW relationship.

Evaluation methods and questions

All the projects are designed based on the programme logframe, but due to the variety of Grantee partnerships the operational set-ups differ. IUCN suggests sampling three to four (3-4) projects for field visits, and using this as input to design a checklist for a desk study of the remaining projects (a total of seven to eight to be reviewed). The sample drawn for the field visits should be as representative as possible; selection should be made on the basis of a pre-defined set of criteria to be agreed during inception (e.g. geographical location, size of project, type of intervention, type of Grantee, time that project has been under implementation etc.).

This evaluation will be expected to use mixed methods intended to allow a degree of triangulation and synthesis. Methods may include: a survey of Grantees and key stakeholders (using both quantitative and qualitative questions), a desk review of relevant documentation, semi-structured interviews, field observations and/or focus groups. All Grantees will attend a four-day Midterm Technical Workshop (October 2017, India) and time will be made in the agenda for interviews or focus groups. The evaluator will be expected to attend the October Midterm Technical Workshop to collect data and present preliminary findings.

A post-graduate degree in biological, social or management sciences with an emphasis on community based natural resource management and landscape-scale conservation programmes;

Experience with evaluation of grantmaking programmes;

Experience running or evaluating Asia specific conservation programmes

A minimum of 10 years of experience working in the field of evaluation and a proven track record of evaluation work in conservation and development (writing sample to be provided);

At least 10 years of experience in conservation or development in the field;

Ability to work with limited supervision;

Superior English language skills.

Individuals or firms who may meet part but not all of the requirements and therefore interested in applying as part of a team can inform IUCN (Julie.griffin@iucn.org) for their names and contact information to be shared with other interested parties. Such teams should submit one bid with a lead contractor clearly indicated.

Outputs and deliverables

Inception report with a finalized Evaluation Matrix, details of data collection (people to interview/survey, dates), including tools, and agreed dates for subsequent deliverables.

Participation at the October Midterm Technical Workshop in India for data collection (through facilitated focus groups, interviews) or presentation of preliminary findings

Draft report

Final report

A powerpoint (or other visual, shareable format) presentation of the final findings and recommendations for the key audiences and users of this evaluation and/or two online/webinar-type presentations

Work plan and budget

Start date and evaluator appointed	End August 2017
Inception note including final evaluation matrix	Mid September
Data collection and analysis, including visits to HQ and sampled project sites	September – mid-November
Participation in October Midterm Technical Workshop, India	October
Draft report	Early December
Final Report and presentation of final report	Early January 2018

Annex: DRAFT Evaluation Matrix

EVALUATION CRITERIA

Effectiveness	2. To assess the effectiveness of the ITHCP and its projects in achieving early markers of programme and project outcomes and to analyse key underlying risks, assumptions and constraints which have or may affect intended outcomes and impacts.	Is the programme being implemented as expected? Are the projects being implemented as expected? Are there elements of the programme that need to be redesigned? What early markers of progress towards conservation outcomes have been observed? What early markers of progress towards livelihoods and development outcomes have been observed? What underlying, risks, assumptions and constraints have or may affect outcomes? To what extent do project activities address the key conservation threats and ultimately fulfil the programmatic objectives of ITHCP? (list of activity types to be provided by ITHCP). To what extent have the actions under the projects' Environmental and Social Monitoring Plans (ESMP) been implemented? What tracking is in place to monitor the outcomes of these?	1. 2. 3.	Interviews Document review (Survey data, if survey used)

		How is the information generated from monitoring being used for adaptive management at project and at programme level? What mechanisms are in place to learn from the work? How is learning being documented? How effective is the programme level governance? Review the set-up and functioning of the Programme Council and Advisory Committee.		
Sustainability and impact	4. To assess whether measures are being put in place to ensure impact and sustainability of outcomes, i.e. whether programme interventions can be expected to significantly contribute towards addressing the challenges identified *ex-ante* in the longer term.	What measures are being put in place to ensure benefits continue after the end of the Grantees' projects? After the end of the ITHCP? What knowledge or learning has been generated through the programme and how is it being documented and shared?	1. 2. 3.	

With a view to ensuring the ITHCP is optimally suited to efficiently address identified challenges and constraints, provide both short-term operational recommendations, and propose longer-term adjustments and modifications for consideration in the design of a potential future phase.

Criteria	Umbrella Question	Focal Questions	Indicator	Data Source
		SR4. Are the "benefits" and beneficiaries clear for the programme as a whole and within projects? Are women, indigenous groups and marginalised groups included?	SR4a. Description of target groups in design/log frame SR4b. Assessment of project design and reports SR4c. Responses to survey/interview questions	
		SR5. Are the required budget proportions appropriate for the objectives and outputs of the Programme, and secondarily the projects?	SR5a. Comparison between priorities and proportions	
Effectiveness	Is the ITHC programme, and are its projects, doing what they said they would do, and are there indications that ITHCP, and the projects, are on track to achieve intended outcomes?	E1. Is the programme, and are the projects, being implemented as expected?	E1a. Achievement Indicator (part of assessment tool) E1b. Results of assessment tool E1c. Stories from programme and projects	-Desk Study, -Review of Technical Reports, -Assessment Tool, -Interviews, -Site Visits, -Workshop Focal groups -Summary Analysis
		E2. Has there been progress towards the stated outcomes of the ITHCP and the projects? What evidence/early markers are available? Are there signs of threat reduction and indirect threats showing positive improvement?	E2a Achievement Indicator- Conservation Outcomes E2b Achievement Indicator- Livelihood/development outcomes E2c. Stories/Narrative from technical reports E2d. Results of Assessment tool	
		E3. What factors (including risks, capacity etc.) have influenced (or could influence) expected outcomes and are they being actively monitored?	E3a. Desk analysis results E3b. Survey and site assessment results E3c. Survey and Interview results	

Criteria	Umbrella Question	Focal Questions	Indicator	Data Source
		Have assumptions been clearly stated and/or are there indicators of invalid assumptions?? Have there been significant changes in the context (e.g. political, pressures) since the programme was conceived and began implementation?		
		E4. Which approaches/actions seem to be most effective, and which not? Are there early indications of successful (or not) activities/approaches?	E4a. Assessment tool results E4b. Survey results E4c. Technical reports analysis E4d. Workshop discussions	
		E5. Does ITHC programme and its projects show adaptation to changing factors and as a response to monitoring information?	E5a. Analysis of logframe and reports E5b. Lessons/learning described and archived	
		E6. To what extent have the actions under the projects' Environmental and Social Monitoring Plans (ESMP) been implemented? What tracking is in place to monitor outcomes of these actions?	E6a. Achievement Indicator (part of assessment tool) E6b. Documented use of tracking tools E6c. View of the ESMS Coordinator at IUCN	
Efficiency	Are the institutional set up (governance, human resources, grant making mechanism) and ways of working creating an efficient and			

Criteria	Umbrella Question	Focal Questions	Indicator	Data Source
		SI4. What knowledge or learning has been or is likely to be generated through the programme, and how is it being documented and shared to positively impact the long-term conservation tiger efforts?	SI4a. Assessment of technical reports SI4b. Assessment of ITHCP wide publications, documents, communication pieces SI4c. Level of engagement and shared learning at workshop	
		SI5. Is there evidence- early markers- that the status of tigers and their habitats is improving as a result of efforts supported by ITHCP?	SI5a. Change in threats assessment SI5b. Change in population status SI5c. Change in attitude and engagement levels	
		SI6. What are the 3-5 key changes that should be made to strengthen any follow up programme? What 3-5 key approaches/actions should continue because they work well and/or show promise?	SI6a. Recommendations from key stakeholders	-Workshop -Survey -Interviews

ANNEX C. DOCUMENTS REVIEWED OR CITED

A. Published Documents/Reports

1.

20. Roy, S. 2017. Mission Report, KfW & IUCN, Bhutan & Nepal. February 24, 2017.
21. Roy, S., *Minutes of the Programme buuuuuo-6(m)2dM-5i>B118.3 743.97 Tm0 g6[*

ANNEX D. LIST OF INTERVIEWEES

S.No.	Organization/ Project	Name & Position	Type of Interview
1.	IUCN	Inger Andersen, Director-General, IUCN & Programme Council	In person
2.	IUCN	Jane Smart, Director, Global Director, Biodiversity Conservation Group.	In person
3.	IUCN	Julia Marton-Lefebvre, former-DG, IUCN	Virtual
4.	IUCN	Lucy Deram, Director, Global Strategic Partnerships	Virtual
5.	IUCN	Jean-Christophe Vié, ex-Dy Director, Species	In person
6.	IUCN	Sugoto Roy, Coordinator, ITHCP	In person/virtual
7.	IUCN	Thomas Gelsi, Prog Asst, ITHCP	In person/virtual
8.	IUCN	Allessandro Badalotti, SOS Programme	In person
9.	IUCN	Linda Klare, ESMS	In person
10.	IUCN	John Karuri, Prog. Finance Manager	In person
11.	IUCN	Juli 0 0 1 70f 155.3 36.775 reW* n	

17.	KFW	Nina Otto, KfW	Virtual, SM
18.	KFW	Matthias Bechtolstein, Senior NRM Adviser, KfW	Virtual, SM
19.	KFW	Moritz Reme, KfW	SM
20.	WCS	Madhu Rao, PAC	In 6.4ers, nS5ad] TJETQq7

35.	1309 WWF India	Kamlesh K Maurya, Assistant Manager (WWF)	In person
36.	1309 WWF Nepal	Kanchan Thapa, Biologist (WWF)	In person, SM
37.	1309 WWF Nepal	Rajendra Suwal, Dy Dir (WWF-Nepal)	SM
38.	WWF India	Ravi Singh, Director, WWF-India (Partner)	In person
39.	WWF India	Sejal Worah, Programme Director, WWF-India (Partner)	In person
40.	WWF India	Dipankar Ghose, Director, Species & Landscapes Programme, WWF-India (Partner)	In person
41.	1309 WWF India	Joydeep Bose, Senior Coordinator, Species and Landscape Division, WWF-India (Partner)	In person
42.	WWF India	Pranav Chanchani, WWF-India (Partner)	

85.	1500 Awely	Alienor Scrizzy	

conservation efforts will endure, and 2) multiplication strategies need further thought and design so that there is a bigger "bang" for each investment, and 3) placing the project in the larger context is also needed to acknowledge and mitigate any negative impacts that additional or growing economic development and political change may bring.

Recognizing that it is difficult to attribute change at outcome levels to single projects, it is worth noting that early "contributory" markers of impact include growing tiger populations in the Nepalese areas of the Chitwan-Parsa- Valmiki complex, (though the official national survey of tigers would not be complete until early 2018), and what seems like a growing interest by communities to help conserve and benefit from living as neighbours to tigers.

***

CASE STUDY 4 (SOC)

ITHCP Project 1327: ZSL-Terai

4

Background

In Nepal, the National Tiger Recovery Plan (NTRP) aims to stop poaching of tigers, which is considered the primary threat. The approach is to focus on core "resource" areas (which can be protected and which have a viable tiger population) and to manage, enlarge and connect these areas to each other and to other tiger habitat areas to improve the long-term viability of the species. This project focuses its support on the recovery of tiger populations in the Terai Arc Landscape, a vital TCL connecting India and Nepal. It is largely believed that the future of wild tigers is not only dependent on the extent and quality of their habitat including their prey but also on the well being

CASE STUDY 5 (GS)

ITHCP Project 1311 WWF Sumatra

Background

The WWF Sumatra project is one of the two earliest projects in ITHCP, initiated in August 2015 and amounting to €1.95 million. The project had therefore been underway for almost 2.5 years at the time of the evaluation trip. While the project is led by WWF Germany (Project Lead- Kathrin Hebel), it is operated by WWF Indonesia, YAPEKA and INDECON team in the field. The project covers the Rimbang Baling landscape of 5094 Sq km encompassing the Bukit Rimbang Bukit Baling Wildlife Reserve (hereafter BRBBWR), the Bukit Bungkuk Nature Reserve (BBNR) and other forest and non-forest lands in its surrounding, in Riau Province of central Sumatra.

Field Itinerary

I based myself in Pekanbaru city, where the WWF (Central Sumatra) office is located, and from where BRBBWR is a four-hour drive away. In WWF office, I had two extensive discussions with the project team, one immediately before going to the field sites and one discussion just after. Discussions were also held with the team of the BBKSDA, Riau Province which is the technical implementation unit in Ministry of Environment and Forestry dealing with species conservation. I also met with the chief of ecotourism development in the Department of Tourism at Provincial level, Riau (in order to understand the governmental role in ecotourism). I was in the area from Nov 13-17, 2017.

During the field trip, I spent 2 days in Tanjung Belit village located just outside the Wildlife Reserve where most of community/livelihood and awareness projects have been undertaken so far. Tanjung Belit is located on the River Subayang, which along with Bio-Bio subtributary circles the northern

engagement with local residents. The focus group discussion with the farmer beneficiaries did not indicate that a clear strategic plan for the agro-commodity activity is being thought about. As of now, no activities, other than with farmers' groups, are planned at the village level to improve livelihoods or reduce dependency on the NP. Therefore a different, multi-pronged approach could help in accelerating the pace of work in the livelihood component of the project even during the remaining portion of the project period.

On the whole, I feel that the impact of the FFI Sumatra project may turn out to be lower than expected. This is because targets for various activities under the project appear a bit low as the grant money has been spread thin over four very large and important tiger-bearing PAs. The coordination issues across multiple sites and partners are likely to cause further hurdles in the satisfactory achievement of the project targets. Also, the project is co

ANNEX F: TWEAKING THE EXISTING LOGFRAME

Making the Existing Logical Framework more useful to evaluate progress in the Programme and Projects and recommendations for improved monitoring and reporting.

EXISTING LOGICAL FRAMEWORK AND KPIs	EVALUATORS ANALYSIS, AND ADVICE ON HOW TO MAKE IT MORE ACCURATELY MEASURABLE
OUTCOME: Improved conservation of selected tiger populations and their habitat that also incentivizes local community support and participation in tiger conservation through the creation of tangible livelihood benefits	To be able to properly understand whether this Outcome is achieved or some greater definition will be needed: define what "conservati n

	Increased number of tigers living there at the end of the supported projects. (The numbers and date of time of achievement of the target are to be defined after selection of intervention areas; depending on the selected geographical areas for intervention, stabilization of tiger numbers may also be considered a success.)	Since the Goal of GTRP is Tx2, then doubling should be an obvious target. However, to recognise that doubling may not be possible everywhere, a more meaningful target would be an estimate of the carrying capacity at project end taking into account improved habitat and prey estimates which should result from the project.
	2. Degree of management effectiveness in supported tiger habitats (e.g. METT or Management Effectiveness Tracking Tool)	Medium quality indicator: refers to a relative survey score not actual ecological change which is what the target is.
	Baseline: Management effectiveness in the programme areas at the beginning of the individual projects (e.g. SMART, CA/TS, METT or other suitable index).	Most places do not have good baselines and those that do usually only apply to Protected Areas, so this is a challenging baseline to establish. Where good baselines do not exist, establishing accurate scores now will be helpful to a phase 2. Due to the nature of tiger conservation there is a need to go beyond protected areas as well.
	Target: Management effectiveness in Programme areas at the end of operations significantly improved. (Level of improvement to be defined after selection of intervention areas and adjustment of methodology; for protected areas, Green List certification could be considered, increase of tiger range and increased prevalence of tiger prey as additional information)	Need to d

Current Framework	_____	Suggested improvements. For each goal, objective (outcomes and outputs) indicators would be established
Resources and capacities for management of tiger habitats are improved and put to good use		1. An Integrated landscape plan is developed and implemented for each tiger reserve, buffer zone and corridor [by 2018) 2. Long term sustainable financing is made available for the implementation (including monitoring of the integrated tiger habitat landscape plans [by 2019] 3. Management effectiveness (under the integrated landscape plans) has shown marked improvement [from 2014 baselines] 4. Government, civil society and communities have the key capacities required to fulfil their role in implemented integrated landscape conservation plans [by 2018]
Human-tiger conflicts (HTC) are mitigated		5. Government, civil society and communities actively participate in reducing human-wildlife conflicts [by 2018] 6. Mechanisms are in place to significantly prevent human-wildlife conflicts from arising [by 2018]
Local communities in supported tiger conservation landscapes proactively su		
