A nudge in the right direction

External Review of the IUCN project
Strengthening Voices for Better Choices

Frits Hesselink
Jean-Paul Ledant
Chantal van Ham

Utrecht - Brussels, September 2009

A personal note

For us the external review has been a very interesting and challenging task. Omissions and misinterpretations in the report, as well as its conclusions and recommendations remain the responsibility of the two external evaluators. Yet, we have benefited from the support of different sources.

The frank and informative briefings by IUCN and the European Commission did provide us with a wider view on the project and put us on the right track. In most of the project countries we visited, IUCN had arranged valuable support for the evaluation in terms of logistics and meetings with project stakeholders and experts on the national forestry situation. During our debriefings at the IUCN offices we noticed a keen interest in our findings and conclusions. Feedback from these offices always meant an enrichment of the evaluation and strengthened the basis of our recommendations.

We felt very welcome when visiting beneficiaries and stakeholders that were involved in the project. They made us feel at home and participated with frankness in dialogues about experiences and opportunities derived from the project. We have used time and ideas of many people in many organizations. Not in the last place of outsiders, not directly involved in the project – such as other development organisations, third country's Embassies, local consultants, journalists and business people. We acknowledge the importance of the contributions to the evaluation of all our informants. We sincerely thank them for their openness and support.

Frits Hesselink
Jean Paul Ledant
Chantal van Ham

Abbreviations and acronyms

AFLEG	Africa Forest Law Enforcement and Governance
COMIFAC	Commission des Forêts de l'Afrique Centrale (Central African Forest Commission)
DfID	Department for International Development
DG	Directorate General
DGF	General Department of Forest Management
DGIS	Directorate General fro Development Cooperation (The Netherlands)
DRC	Democratic Republic of the Congo
EC	European Commission
EAFLEG	East-African FLEG
ETPA	Equity, Transparency, Participation and Action
EU	European Union
FAO	Food and Agriculture Organization of the United Nations
FGLG	Forest Governance Learning Groups
FLEG	Forest Law Enforcement and Governance
FLEGT	Forest Law Enforcement, Governance and Trade
FWG	Forest Working Group
GFTN	Global Forest Trade Network
GTZ	German Agency for Technical Cooperation
IIED	International Institute for Environment and Development
ITB	Industrie de Transformation du Bois (Wood Processing Industry)
ITTO	International Tropical Timber Organisation
IUCN	International Union for Conservation of Nature
IUCN ARO	IUCN Asian Regional Office
IUCN ESARO	IUCN Eastern and Southern African Regional Office
IUCN SUR	IUCN Regional Office for South America
M&E	Monitoring & Evaluation
MSD	Multi-stakeholder Dialogue
NGO	Non-governmental Organisation
NPC	National Project Coordinator
NREG	Natural Resources and Environmental Governance (Ghana)
OVI	Objectively Verifiable Indicator
PCM	Project Cycle Management
PFS	Private Forest Sector
RCO	Regional or Country Office
RECOFTC	Regional Community Forestry Training Centre
REDD	Reduced Emissions from Deforestation and Degradation
SVBC	Strengthening

4. Monitor and assess impact of VPA and other arrangements
5. Continue or develop new awareness raising and communication actions

Recommendations for next steps at global IUCN level
6. Organize a discussion on learning lessons from the SVBC project
7. Capture practical learning on multi-stakeholder dialogue
8. Codify the process of forest governance

Recommendations to IUCN for future project design
9. Develop project ideas in advance
10. Base multi-country projects on country-specific needs
11. Invest more time in project design: feasibility, inception phase, kick off meeting
12. Include knowledge management and communication strategy in project design
13. Involve partners in project design
14. Involve adequate expertise for designing innovative multi-stakeholder dialogue projects
15. Involve adequate methodological expertise for problem analysis
16. Involve adequate methodological expertise for Log frame preparation
17. Prepare a feasible monitoring framework even in the case of intangible and unpredictable ovn(vTw 10.02 0 l0d2JE

1. Introduction

Daily and all over the world decisions in forest governance are taken, that have unintended adverse effects. Choices are often made based on wrong assumptions. Unfortunately we pay for these mistakes by loss of forests, loss of income, loss of biodiversity and ecosystem services. In our understanding the project Strengthening Voices for Better Choices (SVBC) aims to give a nudge in the right direction to forestry departments, forest companies, forest communities and other forest stakeholders. It specifically does so by facilitating dialogue, offering platforms for interest groups to find common ground and work on better choices with respect for the freedom, position and interests of each group.

The project is mainly funded by the European Commission and is carried out by the International Union for Conservation of Nature (IUCN) with the specific objective of promoting “policy, legal, institutional and economic arrangements that contribute to improved forest governance” in six key tropical forest countries (Brazil, the Democratic Republic of Congo, Ghana, Sri Lanka, Tanzania and Viet Nam).

The project started in February 2005 and was completed by the end of July 2009. An internal mid term review was carried out in 2007. In June 2009 IUCN commissioned this final external evaluation of the project, as foreseen in the project document. The draft report was ready early September 2009. After two rounds of comments the final version was realized in November 2009.

This evaluation report starts with a description of the methods used by the evaluation and a project fact sheet, summarizing the main facts and figures about the project. It then analyzes context, preparation, design, synergies, strategies, organization, monitoring and evaluation, budget, external constraints, activities and results, outcomes and impacts, crosscutting issues and sustainability factors. This analysis explains and comments the different steps and components of the project in order to support the assessment, which wraps up positive and negative aspects on each evaluation criterion: relevance, coherence, effectiveness, efficiency, sustainability and impact.

2. Methods and limitations of the evaluation

The purpose of this evaluation is to assess relevance, coherence, effectiveness, efficiency, sustainability, and impact of the project and to learn for future similar projects and activities. The complete Terms of Reference for this review are presented in Annex 1.

2.1. The evaluation method and process

The review was conducted by the authors of this report during the period mid June to mid August 2009. The overall evaluation approach follows both the IUCN[1] and the EC[2] evaluation methods. It is also based on the principles of the logical framework approach proposed by the EuropeAid "Project Cycle Management Guidelines" (2004)[3].

Two external senior review experts made up the team together with an IUCN young professional, who was assigned to the team to learn. The complementarities of knowledge of the two senior evaluators proved to be very useful. Despite the presence of an IUCN staff member the senior consultants guarantee that the evaluation is external and independent.

A face to face briefing was conducted by the global project coordinator on 16-17 June where the evaluators made methodological comments to the ToR which could adequately be taken into account. With the global project coordinator and the head of the IUCN monitoring and evaluation unit the team formulated an evaluation matrix (See Annex 2). The team then prepared an inception note and interview protocols, which were approved by IUCN on 23 June 2009 (see Annex 2).

The evaluators reviewed key documents (see Annex 3); conducted formal and informal telephone and face-to-face interviews with IUCN staff, external advisers and key informants, and representatives of the project's various internal and external stakeholder groups (see Annex 4).

The team attended on 23-24 June 2009 a Chatham House conference in London, where the project was presented. They also used the opportunity to interview key stakeholders. On 30 June the team had a meeting with key representatives of the European Commission to be further briefed on the context of the project, the links with the activities of the Commission in the field of Forest Legislation Enforcement Governance and Trade (FLEGT), Voluntary Partnership Agreements (VPAs), and the expectations the Commission experts had of the evaluation. One team member attended a project workshop in Nairobi (6-8 July 2009), where lessons learnt on multi-stakeholder dialogues were shared and more face to face interviews could be conducted. The team then visited together the project in Ghana (9-14 July). In the last two weeks of July individual team members visited the project office in Bangkok, the project in Viet Nam, the Democratic Republic of Congo and Brazil.

For the evaluation it was extremely useful to observe and experience the project in action during the presentation in Chatham House, the Nairobi write-up workshop and a Tripartite Stakeholder meeting in Brazil. The field visits that were organized in Ghana, Brazil and DRC were also a very good means to provide insight in the reality of the project on the ground. Finally it was useful to meet with some members of the mid term review face to face. Not all countries could be visited and the time was too

[1] IUCN (2004) Managing Evaluations: A Guide for IUCN Programme and Project Managers, IUCN, Gland, Switzerland and Cambridge, UK. 40 pp.
[2] http://ec.europa.eu/europeaid/evaluation/methodology/index_en.htm and EC (2006) Evaluation methods for the European Union external assistance. Guidelines for project and programme evaluation. European Communities, 44 pp.
[3] http://ec.europa.eu/europeaid/multimedia/publications/publications/manuals-tools/t101_en.htm

short to evaluate the country projects individually. The short missions to the four countries only could serve as information contributing to the evaluation of the overall project.

On 28 July a team debriefing meeting was held in Brussels with the global project coordinator on the various missions and first conclusions were drawn from the country visits. Subsequently telephone interviews were held to collect additional information. The report was written in August and a first draft was presented to IUCN in mid August. IUCN comments and corrections are integrated in this final report.

In total, 112 formal interviews were conducted, of which 30 were with people from within IUCN and the project and 82 were with people external to IUCN. For a list of respondents see Annex 4. Interviews were used both to learn about the perception of stakeholders about different aspects of the project and to collect data that were crosschecked and used for the assessment.ssment.ssm

evaluation was more present than at the country level. In some cases the evaluation seemed to be seen as an uninvited add on to the daily workload.

- For many external stakeholders the “borders” of the project and the distinction between the project and IUCN were not clear at all.

Regarding the evaluation itself a major constraint was the lack of adequate and monitored indicators referring to a single and clear logical framework. As explained below the project used several logical frameworks and had also implicit objectives. The evaluators decided to refer to the overall logical framework (part of the project document) but they could not ignore the existence of others and this overall logical framework reflects complicated logical links between results. Moreover the indicators were both discussable and unmonitored. Therefore the evaluation could not clearly focus on adequate benchmarks especially for assessing effectiveness and efficiency.

A project has a formal structure laid down in the project document and the log frame. A project has also an informal structure that is reflected in the reality of the work on the ground. Project evaluations are carried out against the formal structure of the project. That may not always do enough credit to the many positive results and impacts of the project and the enthusiasm and hard work of the project staff. This is especially the case with ‘high risk’ and complex innovative projects that deal with issues that have still to be defined by key stakeholders, that have intangible outcomes, and are based on changes in culture, organization or the social environment. Strengthening Voices for Better Choices is such a project. As far as possible the evaluators have tried to have an open eye for these aspects of the project.

Strictly speaking the project has functioned more as a program within the wider IUCN Forest Conservation Program than as a project per se. The tension between project and program approach (for differences between project and program see Annex 8) may have partly to do with the complex nature of addressing governance issues and processes in a project, partly with the way IUCN operates. The evaluators have made a number of comments on this issue, e.g. it is difficult for external stakeholders to make a distinction between the project, the Forest Conservation Program and IUCN. All these comments have to be seen in the light ofct per se

3. Project Factsheet

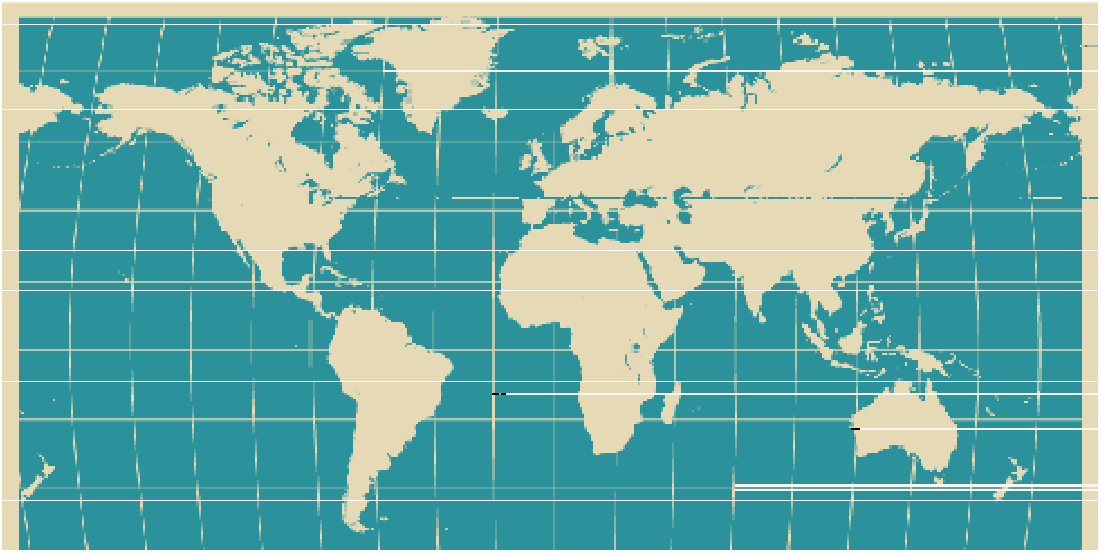

4. Project analysis

4.1. Context

The project takes place in the broad context of global concerns regarding the rapid depletion of forest resources in developing countries with its adverse social, economic and environmental impacts. Poor forest governance is deemed to be a major driving force of those trends in addition to its role in diverting resources from development. When the project was designed responses to those concerns included the regional FLEG initiatives (supported by the FLEG multi-donor partnership), the EC FLEGT Action Plan launched in 2003, the European Commission (EC) “Program on tropical and other forests in developing countries” (now replaced by the Thematic Programme For Environment and Sustainable Management of Natural Resources including Energy) and the IUCN Forest Conservation Program.

The project is part of the IUCN Forest Conservttion

	activities (Knuckle) a newly established Protected Area was depriving local communities from access to natural resources.
Viet Nam	Forests are important biodiversity hotspots and play key roles in the water regime and in livelihoods of minority groups, but after having worked on Community Forest Management SVBC mainly addressed wood industry based on imported raw material. Important reforms are on-going. Public participation and civil society have in Vietnam a different connotation than in the other project countries. Viet Nam participated to the East Asia FLEG ministerial conference (Bali, 2001).

Since the beginning of the project this overall context has been changing quite rapidly. At the level of the European Union, the EU FLEGT Action Plan was followed by the FLEGT regulation adopted by the Council in December 2005. This allowed for control of the timber import from countries entering

As a result of the supply-driven approach in the project preparation the overall project logical framework was applied equally in all target countries regardless their particularities. This has led to the need for subsequently adapting the project and for spending time on building local ownership, which may have reduced the overall efficiency. Country specific log frames were therefore prepared during project implementation (thus late) and were based on problem trees, which helped making them relevant to the context. Some methodological comments should however be made on those problem trees (see Annex 6).

4.3. Project design and logical framework

4.3.1. Multi-country structure

IUCN is a knowledge-based organization. It provides credible, trusted knowledge. IUCN convenes and builds partnerships for action. It has a global-to-local and local-to-global reach and aims to influence standards, policies and practices. Based on this value proposition the project is designed to work in 6 countries and at different levels (from local to global). This provides a good basis for developing a valuable experience and learning lessons of broad applicability. Indeed opportunities to exchange lessons learnt were perceived as the main added-value of the multi-country aspect (see Annex 5) by project coordinators:

> *"In the four international meetings we could see what was happening in other countries, you could see where you were lagging behind, where you could go faster. In cases of staff turnover the new coordinator could learn from his peers."*

- Project staff and consultants cannot easily select or fine tune their activities in order to optimise their contribution to the project specific objective.
- Evaluators cannot identify which action or means contribute to one particular result and therefore cannot assess the cost-effectiveness of the results.

The overall log frame does not indicate clearly to what extent each result is valid for each country. In SVBC there was a clear tendency to pursue all results in all countries. However as mentioned above there was also a need to tailor the project to the context of the six countries. For this purpose country problem trees and log frames were developed. These logical frameworks had a simpler structure (with "parallel" results) but (except in Sri Lanka, the only country where a selection was made in the expected results of the main log frame) they had no explicit link with the overall project log frame. In Sri Lanka there has also been a special log frame for the pilot site area. The result is a project based on different logical frameworks.

The purpose in the main log frame covers in fact 6 objectives (one per country), there are several other log frames with their own purpose and moreover additional goals (not reflected in the log frames) were pursued in parallel (for example to learn lessons of broad applicability or to strengthen voices as suggested by the title). The project therefore had many objectives (both explicit in the log frame and implicit) without clear hierarchy between them. This implies a high risk of competing efforts. Annex 7 provides more detailed comments on the logical framework approach.

4.3.3. Programme structure, fuzzy borders and multi-facetted reality

Because of its different objectives pursued in different locations the project is not as centripetal (focused on one single and unique purpose) as recommended by the log frame approach. On the contrary it has in fact a centrifugal structure, as it channels resources through one single institution (IUCN) for several scattered achievements. This centrifugal structure (corresponding more to a program than to a project approach) entails constraints for result-based management and efficiency because of the risk of competing efforts. It also makes monitoring and evaluation (including this evaluation) more difficult.

A consequence of this structure is that stakeholders face difficulties in identifying the boundaries of the project and distinguishing it from IUCN or other IUCN activities (in particular from the project Livelihoods and Landscapes). This tends to reduce ownership of the project by external stakeholders and contributes to the difficulty in this evaluation to identify the specific outcomes of this project.

The fuzzy borders of the project and its multi-facetted aspect, linked with its multiple objectives and actions, is notably reflected by the diverse perceptions of the stakeholders on the essence of the project. Answers to the question "How stakeholders perceive the core/essence of the project?" include the following (see annex 5 for more details).

movement) and in other cases the project tried to reduce the dependency (as in Sri Lanka). The livelihood aspects also unintentionally generate a tension between the focus on the local beneficiaries and the focus on the governance system. Finally it should be added that rural development alone is usually a difficult job even when it is not combined with forest conservation concerns. Therefore related activities cannot be just marginal tasks of staff who are mainly involved in forest governance. This implies not only a risk of failure but also a risk of negative impact through raising excessive expectations that cannot be fulfilled.

Halfway the project a choice was made to focus – where possible – much more on support to FLEG and FLEGT and to position IUCN strategically as a facilitator of multi-stakeholder dialogues for forest governance. IUCN as a union of governments, NGOs and academia has a unique reputation as convenor. It has proven it's convening power on many occasions. The project increasingly aimed to capitalize on this role and to position IUCN in international forest governance processes as a reliable

also made its own recommendations on the project. Several recommendations were subsequently implemented by the project. Before the meeting several members of the project steering committee visited a project country/site to get to know the project better. The committee was then turned into a more general advisory group for IUCN on forest governance. This Group also met once and discussed the project and other issues.

For specific expertise the project could call on the advice and guidance of a number of IUCN senior advisors on law, economics and forest management. Being placed in the IUCN regional or country Forest Conservation Programs the project also had – at least in theory - wide access to knowledge and experience of other IUCN forest experts and could also bring 'real life experience' to their work. A range of project partners complemented the knowledge base and networks of IUCN in the various countries. This was meant to enhance local ownership and add value to other initiatives on forest governance. Some global partners were represented in the project steering committee. In practice these partnerships worked in a mutually beneficial way in some countries or cases, but not always. In the organogram of the project document the organizations is pictured as follows:

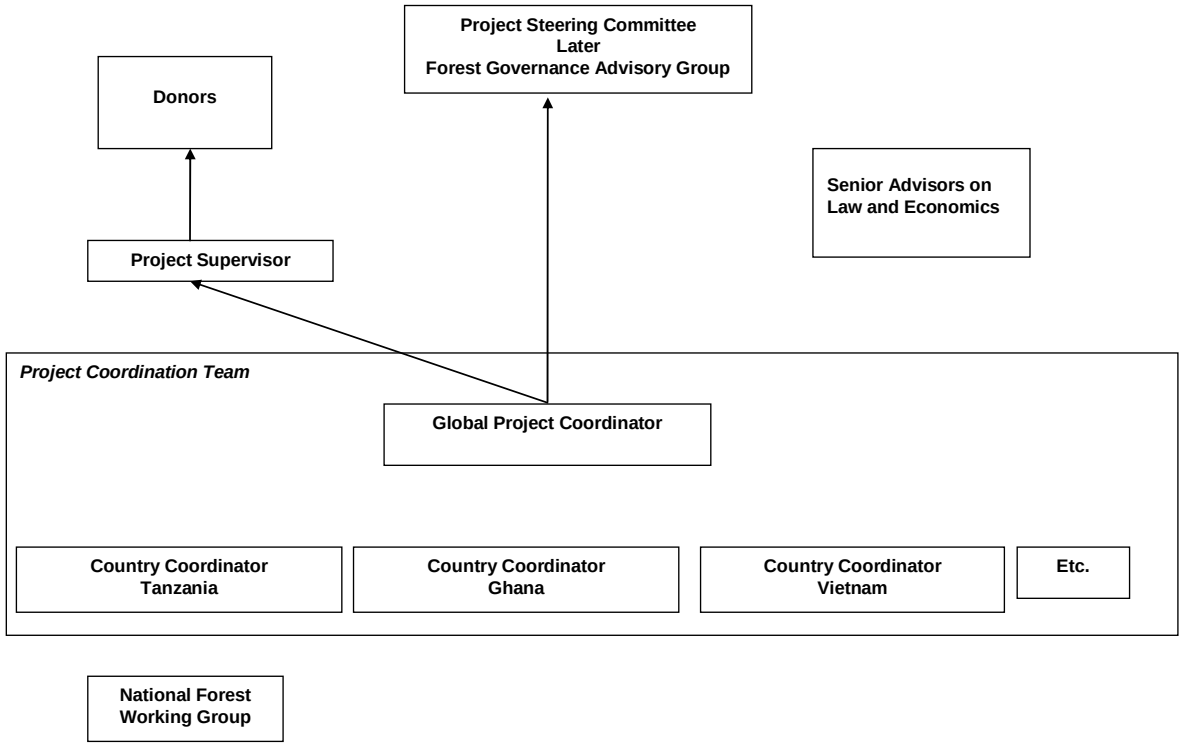

in providing an international context to the country projects. One also can say that the project had a rather heavy overhead structure, as one external stakeholder comments:

> *I would forget about the heavy global structure of legal economic and forest advisors: they had no added value.*

4.6.2. Management

The project came across a range of management challenges as a number of issues was not resolved at the time the project was granted and sanctioned. These included the sharing of overheads: equally among implementing offices, only by the office that developed the project or another ratio for sharing. Finally a choice was made for the latter.

One internal stakeholder comments that a next time:

> *"They should involve countries in the design, share overhead (countries should get 7% of the 400 thousand); there should be more time to create demand for this project with government, and only 15% of total project funds should go to global and regional advisors."*

Another issue not explicitly reso9t explicitly reso

double reporting lines; more ownership of senior management of RCOs (regional director, head of program)"

"Prevent staff turn over by providing more leadership at country, regional and global level."

"Avoid the perverse incentives in RCOs in HRM for a project. I would have the global project coordinator recruit the national staffs and avoid double reporting lines."

"Financial reporting procedures tailored to fit the requirements of the donor were not in place at the start of the project, neither were procedures for knowledge management (capturing of lessons learnt, internal and external communication), monitoring and evaluation of project progress. The project did not foresee in an inception phase that could deal with these issues in an efficient bottom-up fashion."

"I would elaborate much more on knowledge management and communication in the design phase of the project."

"Have a 3-6 month inception phase before the project really starts. Have budget and time for a few close advisors to the global project coordinator to help him set up financial procedures, monitoring and evaluation procedures and knowledge management."

Not surprisingly the mid term review pointed at a number of points to be improved that were directly related to the issues mentioned above.

4.6.3. Knowledge management and Communication

The project did not have a project information system with clear rubrics, where all relevant information could be easily stored and accessed. Formal reports were used as the main ways to capture and disseminate knowledge internally and externally. The project assumed that reports would be sufficient communication towards internal and external stakeholders. In reality most external stakeholders indicated that they either had not seen the reports or had not had enough time to read them.

The project did not pay much attention to communication, in the beginning. An intern prepared a communication strategy. This paper addresses how to prepare a communications strategy and does not provide any concrete guidance for overall project communications. The absence of a concrete communications strategy has led to a wide variety of opinions – internally and externally on what the project really was about (more details are given in annex 5). And more importantly sometimes important stakeholders did not even know the project existed. The title of the project was in some countries used as a brand. In explaining the brand some stakeholders (including country coordinators) thought the idea was better choices at the local level, others at thought of better choices the national level. Moreover the brand 'Strengthening Voices for Better Choices' unintentionally promises more than a project can deliver in a four year period: governance reform takes much more time.

Lack of consistent messages on what the project is about often leads to confusion, misunderstanding, lack of appreciation and a negative image. This is also the case with Strengthening Voices for Better Choices. The communication efforts since end 2008 did not focus on communicati]TJ -22 .00ra-3(eBkrefo)5(r-ludi)7(nt c

and wrong perceptions of IUCN's position in some countries, especially vis-à-vis the FLEGT and VPA negotiation processes.

External stakeholders comment e.g.:

> *"IUCN is conservation, working with people, livelihoods and development. Dialogues for forest conservation would be typical IUCN business. Forest governance is an innovation or new business for IUCN and maybe a bridge too far. It is a question for IUCN whether they really want to move in this direction. It is not clear whether IUCN wants to position itself in governance."*
>
> *"It is not a typical IUCN project, as IUCN is not associated with proactive political work. It would be good if IUCN continues with this new path and communicates this clearly."*
>
> *"IUCN seems to be very satisfied with the project. They did not communicate their role properly, clarifying what added value could be. Communication is IUCN's biggest problem."*

The mid term review clearly pointed out the weakness in communications. The response of the project has been to formulate country communication plans 'to get the messages out'. In an effort to speed up corporate project communications a number of glossy brochures were produced. In the absence of an overall communication strategy the unintended effect of these brochures was that in countries such as Ghana and Viet Nam the partners in the multi-stakeholder dialogues felt that IUCN was claiming the credits for something that at least had been a joint effort.

An external stakeholder comments:

> *"IUCN should not claim ownership of MSD; IUCN should explain better its role and position. It should serve and support but leave the ownership with the government. These MSDs have to be fed with evidence based pilot studies. IUCN cannot deliver those, but should ask others to do them in stead of trying to everything themselves. IUCN should not make glossy brochures with their logo of initiatives it organized with others."*

4.7. Monitoring and evaluation

4.7.1. Monitoring and internal evaluation

The project log frame provides objectively verifiable indicators and sources of information that can be used by the project managers to monitor and evaluate progress towards the objectives and desired results. In hindsight the evaluators have question marks on some of the indicators, as detailed in Annex 7.

Day to day monitoring was done by the supervisors in the regional or country offices, where the country coordinators were situated. For a day to day monitoring there is a particular need to have short term indicators, giving quick information in order to allow adjustments in time. From this perspective some indicators of the logical framework, which could be useful for the final evaluation, are not necessarily adequate. For example the percentage of forest offence cases dropped on procedural grounds in the fourth year of the project is a difficult indicator as it hard to prove that such a drop could be attributed only to the project. And even if it could, it is hard to see this in the court recordings as such recordings when they are accessible, are always published a year or more later. Therefore there was a need to define intermediary milestones, outputs and indicators showing the progress towards the achievements of the objectives.

Project reporting took place on a monthly basis for internal use and on yearly basis to update the donor. The project reports describe project activities towards results but don't refer systematically to the indicators or sources of verification from the log frame. It seemed they also were not discussed extensively during project coordination team meetings. A check how adequate they were in reality has not taken place. Monitoring and evaluation was basically performed through visits by the global project coordinator, progress discussions in the yearly project coordination team meeting and the mid term review.

The mid term review of 2007 pointed out that much had to be improved in the field of monitoring. It concluded “a common absence across the countries of detailed indicators and plans to monitor all aspects of project implementation”. It recommended to formulate for each country cascading log frames country and monitoring and evaluation plans. The recommended monitoring and evaluation plans were made in five of the six countries; all in a very late stage. They are formulated on a rather abstract level. They do not contain clear milestones, that are easy to assess. In conversations with project staff monitoring and evaluation seemed to be something that was an (“almost mythical”) discipline beyond normal project management activities. The task to make a monitoring and evaluation plan was perceived as an extra ‘add on’ on the daily workload and not as a real help. In reality the plans were rarely or not used. The draft 2009 Project Coordination Team Report lists achievements (often framed in terms of activities) and does not provide insight into how monitoring and evaluation actually has worked in practice.

4.7.2. Mid-term review

An important instrument for evaluation has been the 2007 mid term internal review. The mid-term review identified 34 overall recommendations and several recommendations at country level. The final evaluation team considers that several recommendations were addressing structural issues generated by the design and quick preparation of the project, an aspect that the mid-term review did not assess. For this reason all efforts to implement recommendations were not fully effective. An additional constraint, which is also valid for the current final evaluation, could be that the recommendations were not sufficiently internalized by those who had to implement them.

To a certain extent the recommendations of the mid term review were followed. A rapid assessment of the responses given to the 34 overall recommendations (see Annex 13 for more details) shows that at least 17 (50%) were effectively followed, 7 were more or less correctly followed, 6 are unclear (due to the limitations of the final evaluation) and a small group of 5 is negatively assessed, which means that despite the possible efforts made to handle these recommendations they were still valid by the end of the project. In particular the mid-term review did not really change the way the project operated regarding monitoring, as explained here above (4.7.1). However it was useful in promoting many improvements.

4.8. Budget, costs and mobilisation of means

4.8.1. Budget

The total budget of the project was roughly 4.26 million Euros. The co-funding rate of the European Commission is 77,68 %. Projects from DFID and DGIS provided a substantial part of the co-funding.. The various IUCN offices also contributed by acquiring funding from local sources and joint projects with other partners. Especially in Brazil and the DRC the project was successful in raising extra funds. Roughly half of the budget was at the discretionary power of the regional and country offices. Budget decision were made on the advice of the country coordinator. The total budget was administered by the Asian Regional Office.

The Tsunami of 2005 affected the operations of the IUCN offices in Bangkok, Sri Lanka and East

4.8.2. Costs

	Original budget	revised budget		
Expenditure Description	Costs (in EUR)	Costs (in Euro)	Difference (in Euro)	(in %)
HUMAN RESOURCES	1.455.675,66	1.762.196,73	306.521,07	17,39
TRAVEL	198.062,91			

4.8.3 Use of means

The main means for a project that addresses an issue of forest governance are human resources, both at the country level and the global level. For the posts of country-coordinators, IUCN had to hire external experts. In all but one country the project had to deal with staff turnover, hiring of new staff and getting the new country coordinators up to speed. Not in all cases the country coordinators had the same effective support from the regional or country offices. Most respondents from country offices

Expected result 1 and related activities (assessments)

The logical framework foresaw two separate assessments, one on customary law and one on economic frameworks. Instead of producing two reports the consultants, carrying out the assessments were requested to look at links between the two and come up with one report. Merging both assessments can be considered as fully justified in

- In DRC a study on timber flows in Beni province: this study was commissioned on request of the EC delegation but does not contribute clearly to the specific objective. The SAIA report (du Preez and Sturman, 2009) should be considered as contributing to lessons learnt (R5).
- In Sri Lanka a socio-economic assessment for the Knuckles area.
- In Viet Nam (bi-lingual) appraisals on community forestry (Hue and Bac Kan) to be used to revise MARD guidelines and a study on governance indicators.

Expected result 2. New approaches tested (pilots).

The project document describes the rationale for this result as follows: "As the urgency to enhance forest conservation and management continues to grow, the need to test and assess new and innovative approaches to forest governance becomes ever more acute. There is a particular need to develop a better understanding of: the potential benefits and risks of devolved decision making at the local level; the ways in which traditional/customary practices and national forest policies and laws can become more mutually supportive; and the potential role of the private sector in supporting such arrangements. These is also an important need to develop just and equitable approaches, which will empower local stakeholders and make a tangible contribution to livelihood improvements. To this end, the project will support the implementation of "cutting edge" approaches to improved forest governance in each of its six focal countries. The lessons and experiences of these pilot activities will be presented and analysed in the National Forest Working groups (see Result 5), which will use them in the formulation of actions for improved governance at national level."

In different ways, forums for dialogue have been established or developed, which have reduced conflicts between different stakeholder groups and generated a better mutual understanding, at local, provincial and national levels. The project also facilitated interaction between groups that historically had no dialogue at all, such as communities and the government and communities and the private sector. However not all the activities developed in the pilot sites were truly innovative and because of the timing they could not address the obstacles to be identified by Result 1 as suggested by the log frame.

Summary per country:

Country	Summary of actions and achievements on expected result 2.
Brazil (Acre)	The stakeholders consider the pilot component as a strong contribution to their interaction and commitment to work jointly. The project was notably successful in promoting responsible purchasing, timber certification and restructuring State Forums.
Ghana	Three sites were selected for pilot activities but they were effective in only one. The project improved the relations between community and forest services and promoted livelihood, although their economic viability and contribution to the project purpose are doubtful.
RD Congo	Significant progress has been made in developing structures for dialogue that did not exist before. Many stakeholders indicated that they have been given the opportunity to share their views and opinions with other groups and work together more effectively in finding solutions for problems.
Tanzania	The pilot has resulted in empowering local communities to feel ownership and responsibility for the forest. It created a new attitude among the district forest service that governance is not only a matter of using the stick, but that the 'drum' or participation can also be a powerful additional tool.
Sri Lanka	A local forum has been created in which stakeholders can discuss their concerns. Support to alternative livelihood has been provided. This was apparently more effective than in Ghana, but had the same unclear link with the purpose. It also received only a modest contribution of the project, compared to the inputs provided by project partner Dilmah). A national multi-stakeholder forum – the first of its kind in Sri Lanka – was created (as the project steering committee) to address broader issues of forest conservation. This structure had then to be transformed into a National Forest Working Group, but its future is still under discussion.
Viet Nam	The pilot has been discontinued, because it did not add enough value to similar ongoing initiatives. The project opted instead to do a comparative study on

	community forestry that could be used in the FLEG(T) process. In two provinces cooperation in this study and in other initiatives with the Provincial Departments on Agriculture and Rural development has resulted in more openness for participatory approaches in those institutions.

There are still needs for a continued support at pilot site level, for example in Ghana and DRC. Key obstacles identified in the legal and economic assessment, such as the clash between institutional and customary law and the weak implementation of the legislative framework present extra challenges to implement solutions resulting from multi-stakeholder dialogues, initiated by the project. Another problem is that in some of the countries, it is not clear
to what extent IUCN and the project have contributed to the results achieved. Involvement of other donors, international and local organisations or the government also play a very important role in these results.

Expected result 3. Capacity development and related activities (training)

As the title 'Strengthening voices for better choices' indicates, a project's important aim is strengthening of capacities and empowering key actors in communities, civil society, private sector and government to take the leadership, plan, coordinate and manage an interactive process towards forest governance reform. A relatively large part of the original budget was set aside to support training in governance (€ 460.000 – only the pilot activities were budgeted higher at roughly € 600.000). These were estimates at the time of the design of the project.

There was no learning, empowerment or capacity development strategy formulated in the design phase or in the beginning of the project. In Sri Lanka and Viet Nam a training needs analysis was carried out by RECOFTC. RECOFTC experts also gave a workshop to all country coordinators on how to carry out a training needs assessment and the developed a manual for the project on capacity building needs assessment. Respondents who had directly or indirectly worked with RECOFTC indicated that the added value of their interventions for the project had been minimal. It is possible that the RECOFTC competences are more in the field of community forestry and not enough in the field of transitions in governance and working at the national and international policy level.

The RECOFTC studies and approaches addressed the gaps in technical knowledge at various levels of stakeholder groups that needed to be addressed. They were unfortunately too generic to identify concrete entry points and priorities to take a next step in the process of forest governance reform. They did not articulate the often implicit demand for learning in stakeholder groups and focused more on a general overview of gaps in knowledge in the technical and legal aspects of governance reform and not or not enough on the process aspects. As one internal stakeholder commented:
It was a mistake to contract RECOFT, they did not have the right background to guide us on how to set up capacity development for governance issues.

In all countries training workshops and orientation sessions were organized for government, civil society and private sector on forest governance. As the project had to create the demand – especially on the national level – for such training workshops, the number of workshops on improved forest governance, forest law and global forest policy were less than originally foreseen. Much of this demand was created in Ghana and Viet Nam during the national and international FLEG(T) and VPA processes. These processes themselves proved to be powerful learning by doing opportunities on how to realize new arrangements for forest governance. Similarly the country exchange visits in the project were impressive learning moments, especially where government staff had to explain to their visiting peers the rationale, organization and steps in the process of FLEG(T) and VPA. Participation in international meetings (e.g. Chatham House, World Conservation Congress etc.) - facilitated by the project - also provided important learning opportunities.

In most countries training workshops were also organized on facilitation skills needed for multi-stakeholder processes or consultations for forest governance. Again only half of the budget originally set aside for such trainings was used. The trainings – as far as the evaluators could study them - included a lot of methodologies used in community forestry, e.g. participatory rural appraisal, semi-structured interviews etc. There were fewer indications for training in specific knowledge, attitudes and

skills for multi-stakeholder dialogues. The input of the Keystone Institute was restricted to interaction with the VPA Steering Committee and various stakeholders in Ghana and a report. This report remained virtually unknown to the other countries.

The absence of a strategy for empowerment or capacity development (with milestones and indicators) in the countries was in most cases compensated by the apparent flexibility and responsiveness of the country coordinator to make support available for training where the need seemed to arise. The downside was at least in one case that when important needs, e.g. interest based negotiation skills training in a VPA process were identified, the training budget was already fully used.

The original log frame provides concrete figures about different groups of training beneficiaries. The training workshop reports do not in all cases provide clarity which of these groups were targeted, or how many exactly attended. The impact of learning was not measured: the reports do not provide insight to what extent a positive change in knowledge, attitudes and skills was reached.

Despite the cuts in the training budget, the evaluators also could not find in any of the country or project progress reports a deviation from the log frame with respect to training results. Given the impact of the project in most countries however, one could say definitely that capacities were enhanced although it is difficult to track which interventions contributed to this fact and which did not. And to what extent trainings contributed to the desired project results in capacity development.

Expected result 4 and related activities (FLEG)

The project has substantially contributed to the FLEG process, especially in the VPA (pre-) negotiations of Ghana and Viet Nam. The main inputs were raising awareness, building capacity on FLEGT, and facilitating stakeholder dialogues among the various stakeholders groups (Government, businesses and civil society). The activities of the project contributing to FLEG/-0.0021(ted 0.0et)9(y). T4.0022 Tw 20r-

	bring together representatives of government, businesses and civil society and facilitate a meaningful dialogue on FLEG(T) issues..

name national forest working group (e.g. in Brazil the name is State Council, in Sri Lanka National Forest Forum) or function as a formal working group (e.g. the stakeholder consultations in the (pre)negotiation process in Ghana and Viet Nam resulted in formal and informal networks for forest governance reforms).

The project also did not succeed in the publication within two years of its assessments of legal, policy and economic obstacles for forest governance reform. This may have been a too ambitious target. A range of publications are due in 2009. The project did not realize five IUCN policy briefs, but did realize a number of presentations on forest governance and a number of brochures for use in international forums. A key document of the project is the written input into the public consultation by the European Commission on the 'additional legal options to combat illegal option'. This document was produced with specific inputs from country project coordinators. The communication activities to disseminate lessons learnt from the project can be summarized as follows.

“Change in attitude takes more time. Preparation and selection of leaders of stakeholder groups are important.”

“MSDs take a long time and have their own dynamics, there is a need to work on concrete milestones.”

“Negotiation between government and private sector alone does not bring good solutions.”

“You need to build capacities in communities to get their voice heard.”

Relevant quotes from external stakeholders:

“Space for discussion is key although it can take time; critics are very valuable and useful (both positive and negative), it makes us more humble, help us correcting our mistakes and helping others correcting their own mistakes.”

“The process is unpredictable. A mono-strategy would be ineffective.”

“Recognize the importance of your partners, once they are recognized as important they support you.”

“Set out clear rules of the game right from the start.”

	Commission. Contribution to District Forest Committees.
RD Congo	Several platforms established (Bikoro, Province, National + 32 Comités de Vigilance at village level), although their sustainability should be confirmed.
Tanzania	District by-laws, New Harvesting Guidelines, Awareness raising activities on FLEG, Contribution to FLEG policy briefing notes for EAFLEG, Revamping of National Forest Working Group
Sri Lanka	Forest Protection Plan; KEPA Management Committee; National Forest Forum.
Viet Nam	Contribution to awareness and understanding on FLEGT of related stakeholders, notably through the translation of FLEGT documents and the contribution to several stakeholder meetings

4.11.2. The impact as the contribution to the overall objective

The overall objective was to have arrangements in place at regional level which contribute to sustainable and equitable forest conservation and management. This could not be achieved at this point in time. So we can only assess whether conditions have been put in place for such a future impact. These conditions are:
(a) that the promoted arrangements support sustainable and equitable forest conservation
(b) that lessons learnt (in terms of recommendations for arrangements) are of broad applicability
(c) that they are disseminated to external stakeholders who are ready to use them for the same purposes.

(a) Although e.g. in Ghana it was “not apparent how the VPA Steering Committee incorporated the various (and sometimes divergent) opinions of the various stakeholders into their recommendations to government” (report “the VPA process in Ghana”, may 2009), in general one can say that the project contributed to such new arrangements. Several arrangements built with the contribution of the project clearly contribute at least to sustainability.

(b) Lessons learnt will presumably be helpful for promoting similar processes and arrangements in other countries, but as explained above they still have to be captured and disseminated.

Is not clear at all that everywhere all stakeholders support the overall goals of conservation and sustainable development and those negotiations always reduce inequalities instead of replicating them. In particular the focus on legality (notably in FLEGT issues) is not always and per definition consistent with the objectives of sustainability and equity. There may be a need to systematically assess the environmental and social impact of arrangements (VPA and others) in order to check to what extent their effects can be positive and to recommend how to enhance them.

4.11.3. The external effects

The project has generated or may potentially generate other effects, including side-effects and contributions to objectives that were not in the main log frame:

- Better mutual understanding and dialogue, cultural changes and attitude changes of stakeholders vis-à-vis each other (including for example less social exclusion of pygmies in DRC), therefore a reduction of conflicts
- Concrete learning experience and capacity building in forestry departments on effective interaction with stakeholders in governance issues, which contributes to sustainable achievements
- Interest from other project and countries on the VPA multi-stakeholder process in Ghana
- Reduction of damaging practice in the project countries and regions (for example in Tanzania and Brazil) and potential reduction of illegal practice abroad (VPA in Viet Nam can have an impact on Laos, responsible purchasing in Acre can have an impact in Rondônia)
- Establishment of IUCN in new locations, for example Acre.

Although these impacts are unquantifiable, the project had many positive social, economic and environmental consequences and most are assessed positively by the evaluation team. Broadly speaking it can be stated that the project has changed the speed and the trajectory of governance

4.12. Crosscutting issues and sustainability factors

4.12.1. Crosscutting issues

The main crosscutting issues relevant to the project are gender, indigenous peoples, marginalized groups and the environment.

Country	Sustainability
Brazil	Strong prospects for sustainability due to broad political support, effective dialogue, commitments and long-term decisions already taken and relative level of development; however the civil society in Acre is weak (needs for a new role after its political victory) and there is still a facilitating role to be played by IUCN or another similar institution (not necessary in a project approach, but may be as permanent institutional arrangement).
Ghana	At national level sustainability is ensured by the nature of VPA and the budget support given in the natural resources sector, however the need for such external pressures reflects a lack of local ownership. In Assin Akropong (pilot site) initiatives to create livelihoods (bee keeping, grass cutter rearing, mushroom production, and snail farming) show little evidence of economic sustainability.
RD Congo	Sustainability of the newly established institutions should be strengthened. People have other priorities and lack of resources. Representatives from villages in multi-stakeholder platforms, expect a payment or support with transport to be able to participate in meetings. This mentality towards support from international organisations, seems to block capacity building and the development of self-initiative. Many participants indicated that the project is in an early phase and cannot continue without support from IUCN and other external partners.
Tanzania	The pilot has taken root both in the communities and in district forest service. The consultations of private sector and the multi-stakeholder approach form an irreversible experience. The IUCN project Livelihoods and Landscapes can offer some continued support where needed. However continued external support is needed for local and national processes. Fortunately political will exists in the current administration to take next steps in forest governance reform.
Sri Lanka	The sustainability of the local forum in Knuckle will benefit from newly created mutual understanding. Efforts were apparently made for the economic viability of livelihood initiatives although excluded persons or communities may expect more. Support to recurring activities (e.g. transport facilities for forest patrols) will be sustained by using part of funds generated from ecotourism activities. The future of a national forum is still under discussion.
Viet Nam	The VPA process is on-going. Further support to the FLEGT awareness raising and agenda setting process at higher levels in MARD can be realized e.g. with support from LLS. IUCN has to better coordinate, plan and execute its interventions towards the government in dialogue with other actors (e.g. FSSP, EC, Vifores).

4.13. Perceptions of stakeholders

The quality of a project does not only depend on how adequate, effective and sustainable outcomes and results are and how efficient the use of time and money has been. From an organisation perspective the quality of a project also depends on how major stakeholders perceive the project and such quality, especially when the project is closely associated to the name of the organisation and when the borders of the projects are unclear as in SVBC. Reputation is the perception by stakeholders of the added value of an organization. In terms of reputation management: “perception is the only reality!”

Therefore the evaluators have also analyzed various perceptions of internal and external stakeholders in Annex 5. Those are opinions of stakeholders that should be clearly distinguished from the data that they provided and that contributed along with other information sources to the views of the evaluators.

Many stakeholders have a positive perception of SVBC and IUCN’s role in forest governance and multi-stakeholders processes. Most external international stakeholders see a clear role for IUCN in a

variety of supporting roles in multi-stakeholder di

5. Evaluation

5.1. Relevance

Evaluation approach

Under this criterion we consider primarily the justification of the specific objective and expected results as stated in the initial project log frame. The specific objective is considered as justified if it addresses existing needs and contributes logically to overall objectives in line with the policies of the donors and IUCN. The expected results are considered as relevant if they are necessary and sufficient to achieve the specific objective.

Positive aspects

The specific objective of the overall SVBC project is considered fully relevant both to the European Commission, to IUCN and to the local needs in all six project countries. The process reflected by the expected result is relevant as well, at least at the multi-country level. The project was flexible enough to adapt to changes in the context (for example in cases where a VPA process started). From the perspective of learning lessons that are broadly applicable for multi-stakeholder dialogues related to forest governance (an implicit objective), the overall approach of working in several countries and at several levels is also highly relevant.

Negative aspects

The proposed expected results are steps in an iterative process instead of being complementary contributions to the specific objectives that have to be achieved in parallel. The expected results are also very broadly defined allowing for flexible interpretations. In practice this lead to pursuing expected results at a stage where they were no longer relevant (for example result 1) or in such a way that they were not clearly contributing to the specific objective (for example economic activities in result 2). Therefore all activities were not necessarily relevant to the objective. Although the selection of the six countries reflects the interest of IUCN as a global organisation expecting lessons of broad applicability it does not directly contribute to the expected added-value that the target beneficiaries in each country could expect from co-operating with others.

Differences between countries

The six countries are very different with respect to the forest governance context and therefore the adequacy of a same log frame (or the grouping of the six countries in a same project) is questionable.

Overall assessment

The project is relevant at the highest levels of its logic of intervention (overall and specific objectives) but not fully at lower levels (expected results). Because the expected results in each country do not clearly contribute to the foreseen arrangements in others, the justification of having the 6 countries in a single project is weak with respect to the explicit purpose of the log frame, which consists of building arrangements in parallel in 6 different countries.

5.2. Coherence (external and internal)

Evaluation approach

Coherence refers both the complementarities with other initiatives (external coherence) and to the internal consistency of the project.

Positive aspects

Overall assessment

Satisfactory but variable effectiveness.

5.4. Efficiency

Evaluation approach

Efficiency refers to the ratio between results and costs. The assessment is constrained by the lack of measurable (and measured) indicators and also to the unclear linkages between inputs and outputs. This is notably the result of the accountability system in IUCN and from the fact that many results and activities are interdependent.

Positive aspects

The project had significant outcomes and impacts (internal or external to the logical framework) at low costs. Positive factors include embedding into the wider IUCN Forest Conservation Program, high flexibility towards changing contexts and the synergies found with other actors.

Negative aspects

Efficiency as been hampered by a series of difficulties and constraints including external factors (for example the Indian ocean tsunami in the beginning of the project implementation period), the project design (need for adapting the project to local context, implementation of activities that are not clearly contributing to the purpose), structure (multi-country and multi-continental project implying extra-costs that did not result in sufficient added-value at country level), geographic scope (travel costs due to long international and internal distances), the fact that activities were implemented without contributing to the purpose (abandoned activities in Viet Nam, late assessments, poorly relevant training) and project management (poor focus on targets and milestones, no working monitoring system, 'loneliness' of project coordinators, insufficient support received by them, lack of knowledge management and effective communication, long delays before receiving approvals from IUCN advisors etc.).

Differences between countries

The overall efficiency seems much higher in some countries (for example in Brazil) than in others.

Overall assessment

The average efficiency could be improved.

5.5. Sustainability

Evaluation approach

Sustainability refers to the extent to which outcomes will be maintained after the end of the project activities. At this stage it can only be assessed indirectly through conditions or factors of sustainability.

Positive aspects

Many outcomes are inherently sustainable, for example the better mutual understanding among stakeholders, collaboration and dialogue between private sector, government and civil society, conflict reduction, lessons learnt, capacities and knowledge built, institutional and legal arrangements, conflict reduction, awareness and knowledge on Forest Governance issues and FLEG(T) processes, will certainly remain long after the project implementation period. Many processes supported by the project will continue and IUCN can still play a role as a permanent institution or at short term through other projects (e.g. LLS).

Negative aspects

Participatory forest governance reforms and participative multi-stakeholder dialogue take a long time and in some countries the project has not achieved all the results that were expected to contribute to

the continuation of the reform process. In many cases there is still a need for a continued support and facilitation role by IUCN or a similar organisation. Funds for this are not guaranteed. Some actions (for example promotion of alternative livelihood in Ghana) show little evidence of sustainability. Some processes supported by the project require external pressure (e.g. Ghana). Awareness raising and capacity development are also needed beyond the fore

6. Conclusions and recommendations

6.1. Recommendations to IUCN and local partners for next steps at national level

Several activities implemented by SVBC require a long term support or involvement. Therefore it is strongly recommended to ensure the minimal continuation required. Sometimes there is also a need to strengthen the sustainability of specific achievements or to address new problems. Although this can be done sometimes by other stakeholders, IUCN staff should still feel responsible to ensure that this happens. It is not necessary that all those activities are gathered in one single project similar to SVBC and some of them can be envisaged through other IUCN projects (for example LLS). The required further support should be identified on a case by case basis. The limitations of the current evaluation make it impossible to identify what follow-up exactly should be provided in each country and which new interventions should be designed locally. However overall recommendations can be made with some country-level suggestions as examples:

1. Continue facilitating on-going multi-stakeholder processes

IUCN has played an appreciated and valuable role in facilitating multi-stakeholder processes. These processes are not completed and sometimes have a permanent nature. IUCN as a permanent institution (not as an external assistance project) should continue to play a facilitating role where it is invited to do so, as far as resources are available.

2. Strengthen multi-stakeholder platforms and their sustainability

IUCN has contributed to the setting up of multi-stakeholder platforms that sometimes still need to be strengthened and made more sustainable (that is less dependent on external projects).

Brazil	Refer to the problem and objective tree approach to help decide priorities in "multi-sector agenda" implementation, by selecting key feasible actions that can generate significant impacts.
Ghana	Continue the support of multi-stakeholder dialogues in the implementation phase of the VPA and support the REDD dialogues with the knowledge of networks, opinion leaders and IUCN facilitation skills.
RD Congo	There is a need for continued support building sustainability of multi-stakeholder structures. Continue building the information flow between 8(D.52 0.48 0.4 9.0.4 so

Country	Suggestion
Brazil	“Strengthening voices” of local communities should be a priority. The local interest for REDD and payments for environmental services should be taken into account when designing new projects or activities.
Ghana	Assess and improve the economic viability of sustainable alternative livelihood in the pilot site.
RD Congo	There is a need for addressing clearly the tension between local demands and forest governance issues.
Tanzania	Continue to work on empowerment in the Rufiji district,

7. Capture practical learning on multi-stakeholder dialogue

The project has generated a wealth of learning on multi-stakeholder dialogue. Unfortunately most of this learning is implicit learning and not codified. Somehow the focus of the country coordinators has been mostly on the activities and doing them right, and not on capturing lessons learned with regards to the process of forest governance reform, and especially the participation aspects of governance processes. Therefore it is recommended to capture practical learning into an online toolkit, guidelines or roadmap for government agencies and NGOs that engage in interactive approaches for forest governance reform and or consultation processes with the private sector and civil society to support a process towards a VPA. Active participation of the field partners and staff of SVBC is recommended both for the quality of the tool and for their own learning process. As this is also of interest to the European Commission for its work on VPAs and related activities, the Commission should explore to what extent they could participate and support such an exercise.

8. Codify the process of forest governance

Codify the process of forest governance reform as accomplished in the various innovative arrangements in the various countries of the project. Codification means a description of the various steps in the process. Such description can be the basis for analysis to identify milestones, principles, tipping points and lessons learnt. In Vietnam, e.g. the internal respondents could not reproduce anymore the various steps taken in the VPA process. A beginning of a description of these steps was made based on interviews with external stakeholders(see annex 11). Make such codification exercise a routine in similar projects, e.g. Livelihoods and Landscape. For an example of codifying lessons learned on milestones and tipping points in multi-stakeholder dialogues in Ghana see technical annex 10. Once the participation processes are described in the various countries, the added value of a multi-country project can be made explicit: by comparing the descriptions a global synthesis can be made.

6.3. Recommendations to IUCN for future project design

9. Develop project ideas in advance

Diagnosis (problem analysis) and project ideas are to be prepared in advance with IUCN partners in countries and locations where IUCN intends to work, including the current SVBC countries and other countries where IUCN involvement has to continue. Project ideas should ideally be ready before any call for proposals. In the case of multi-country approaches, it is advisable to explore to what extent IUCN meetings (World Conservation Congress, World Parks Congress or regional members meetings) can provide informal platforms to brainstorm with a wide range of project stakeholders on project ideas. Special brainstorming formats to generate project ideas could be developed to facilitate such meetings.

10. Base multi-country projects on country-specific needs

Multi-country projects should ideally group country projects, prepared in advance as a response to local problem trees, when this grouping provides a concrete added-value. This can e.g. be a shared trans-boundary resource, or issues for which exchange of experiences can benefit stakeholder groups in each country.

11. Invest more time in project design: feasibility, inception phase, kick off meeting

Sufficient investment in project preparation is important in general and especially in case of a large project having a strong innovative character. Attention should be paid to the time required, the sequence of steps, the need for participation, and the balance between global IUCN concerns and local needs in project preparation. A preceding feasibility study should be the basis for the project. If a feasibility study is not possible the project planning should include an inception phase or at least a kick-off meeting in which a number of issues can be dealt with before the projects really takes off on the ground.

12. Include knowledge management and communication strategy in project design

During the feasibility study or inception phase it is also recommended to brainstorm with all disciplines on the knowledge areas needed for the (innovative) project, the framing of rubrics needed and the methods how to generate or access, store and disseminate the necessary new knowledge. For each knowledge area it should list the main concepts and define these in clear rubrics or headings. The rubrics should be used consistently in all forms of internal and external communication.

With representatives of the end-users the project team should brainstorm on the most effective means and modalities of knowledge storage (project documentation and information systems) and knowledge dissemination (e-news letters, reports, list serves).

The organization of bottom-up collection and capturing of implicit knowledge and lessons learned by global advisors should not be organized in a top-down expert approach (that can be used for capturing explicit knowledge) but in a mutual peer learning approach. (See Annex 9)

In the design or inception phase, the project team should define priority target groups for the three areas of communication: internal communication, external (corporate) communication about the project and external communication to market the products, services and lessons learnt of the project.

To make sure all project staff understand the essence of the project and use the same messages in their external communication about the project, a communication strategy should be designed during the feasibility of inception phase. The communication strategy should include short messages for key audiences on the essence of the project, the role of IUCN and the added value of the project to the priorities of key stakeholders.

The project team should develop a communication strategy for all three areas of communication based on an assessment of current knowledge, attitudes and behaviour of each target group and the desired knowledge, attitudes and behaviour. On the basis of this assessment the team should formulate communication objectives, and then identify and budget the most appropriate communication means.

Communication works, if it is planned in a participatory way (with input of key audiences), and when it is strategic. The latter means that communication is less about information, but more about the context, the trust, the motives and the values of the various target groups. Communication works if it results in attention, hits a subconscious emotion that triggers interest, excitement and willingness to act. In the design phase specific ToR have to be formulated for expert communication staffs, to avoid that other staffs who are more content oriented ge

16. Involve adequate methodological expertise for Log frame preparation

- Log frames (logical frameworks) should be built and used with adequate discipline (see Annex 7). They should not be prepared only for obtaining funds, they should be a tool to use during the project implementation, to define what should be done and to monitor what is done.
- "Expected results" should be pursued in parallel in order to contribute complementarily to the purpose (specific objective); in other words no result should be a condition for or a step towards another one and together expected results should be necessary and sufficient to obtain the purpose; expected results are "objectives" in the objective tree having no causal links (arrows) between them and being all causes of the purpose.
- The "purpose" (specific objective) should reflect a single idea and be the direct consequence of all expected results; this was is not the case when a similar purpose is pursued independently in different countries.
- Large scale or multi-country projects/programmes can have cascading log frames, but in this case the hierarchy between log frames should be explicit: the purposes of low-level log frames should become the expected results of the overall log frame.

17. Prepare a feasible monitoring framework even in the case of intangible and unpredictable outputs

In the development phase of a project when a log frame is prepared, one should define indicators of the objectives and results, with clear target levels. These indicators should be as objectively verifiable as possible. The indicators should be used both to provide a concrete and clear understanding of the expected achievements and to monitor progress. They also can help to fine tune the wording of the objectives and results.

In addition to the indicators mentioned in the log frame, with their target levels, it is also necessary to formulate intermediary targets and milestones to guarantee an efficient implementation of the project.

The need for objectively verifiable indicators poses a particular challenge for projects leading to unpredictable and intangible results, in particular for projects that support participatory processes or multi-stakeholder dialogues. These challenges and constraints should not be a reason not to formulate such a project, but to invest in extra efforts to guarantee accountability and measurability. There are no easy solutions to these challenges, but in project development it is important to rely on a clear distinction between the outcomes of the supported process and the objectives of the project. If e.g. IUCN wants to interfere with existing forest governance processes its objective should not be the outcome of the process (for example new arrangements decided) but the improvement of the process (for example a more balanced representation of marginalized stakeholders, an improved organization of the dialogue, an enhanced support among key stakeholder groups).

6.4. Recommendations to IUCN for future project implementation

18. Focus on the purpose and the log frame

It is important to continuously focus on the project purpose and refer to its log frame. Several recommendations made above contribute to this: a clear and unique purpose (specific objective) also reflected in the title, clear logical links between the results and the objective and a unique logical framework.

During implementation the focus on the purpose and reference to the log frame should be part of the project culture. Therefore it is important

- To keep a continuous eye on the log frame (it should be posted on the walls of the project office!);

20. Clarify the role of global coordinator (in case of multi-country project)

Internal IUCN respondents also have a range of suggestions to clarify the role of the global coordinator of multi-country and innovative projects such as Strengthening Voices for Better Choices. Many respondents mention that the role of the global coordinator should not be focused mainly on providing advice and backstopping to country coordinators and monitoring progress of the project. The most frequently mentioned suggestions on the role of the global coordinator can be summarized as:

- to provide leadership to the project, to constantly keep the purpose and objectives clear to the project staff and translate the complexities of issues into practical language that tell project staff what they can do about it 'next Monday'
- to invest in human resource management of project staff, constantly enhance their professionalism (including the updating of their knowledge and skills) and focus on learning on project purpose and objectives.
- to be constantly alert on the tendency to make things more generic or more complex and turn that around by making things more simple and strategic.
- to listen to experiences and ideas of country coordinators, then provide direction and speed things up – this implies an output based management style as opposed to a input management style, which seems part of the current management culture.
- to constantly work on a culture of transparency, trust, learning, open communication and other IUCN values.

21. Invest in knowledge management

To operational knowledge management the global project coordinator should make it one of his priority responsibilities and tasks. He should regularly survey the degree of satisfaction of the end users of the project knowledge to explore how to improve knowledge management.

22. Organize communication

The global project coordinator should make it is his responsibility to make sure that the gap between how external stakeholders perceive the project and its added value and how internal stakeholders would like the project to be perceived, is as small as possible.

The global project coordinator also should make sure real communication expertise is used that has the competence to focus on the 'irrational-emotional-intuitive' parts of the brains of the audience. This has nothing to do with good illustrations, pictures, clear messages, but much more with the fact that e.g. words do not only have a dictionary meaning but also strong positive or negative associations. It is important that a global project coordinator hires communication staff who are familiar with issues such as framing, target group research, marketing, decision science research, etc.

Simple stakeholder satisfaction surveys among key stakeholder groups at the end of each calendar year of the project could help identify where the project needs to improve its communication or services (a ten minute telephone call can do miracles and creates a lot of goodwill).

Explicit credits should be given to others in publications about a multi-stakeholder dialogue, this will create positive word of mouth by these groups on IUCN's role. Glossy brochures with only the IUCN logo on the front page have the opposite effect.

Donor and partner communication should not be based on the assumption that project progress reports are (thoroughly) read by all representatives of the donor: remember that 'memos do not communicate'. Short personal e-mail flashes, with links to a project web-site with rubrics, visuals and short texts that are based on user-research are much more effective.

6.4. Recommendations to IUCN for carrying out an (external) review

On the basis of the experiences of this external review the evaluators have a few recommendations. The first is based on the need to already have a critical look at the log frame during an internal mid term review. The second is based on the need for more time in the preparation phase of an evaluation.

23. Select midterm evaluators that have not been part of the design team

- Include one or two evaluators in the internal mid term review team that have not been part of the design of the project, which makes a more independent and critical look at the log frame possible.

24. Invest in the preparation of an evaluation

26. Explore the possibility of capturing and disseminating lessons learned in multi-stakeholder dialogues to improve forest governance

Multi-stakeholder processes are vital instruments for forest governance reform and sustainable development projects. It is therefore recommended to capture the practical learning in the Strengthening Voices for Better Choices project into an online toolkit. Such toolkit could contain guidelines for government agencies and NGOs that engage in interactive approaches for forest governance reform and or consultation processes with the private sector and civil society to support a process towards a VPA. As this is of interest to the European Commission for its work on VPAs and related activities, the Commission should explore to what extent the Commission could participate in and support the development of such toolkit.

Annexes

Annex 1. Terms of reference and inception note

Terms of Reference

Final External Evaluation of the Strengthening Voices for Better Choices Project

May 2009

Background

The project “Strengthening Voices for Better Choices” promotes the development of improved forest governance arrangements in six key tropical forest countries in Africa, Asia and South America. Three broad categories of

Proposed Methodology

The evaluation team will collect a mix of quantitative and qualitative data from field visits, document review, survey and interviews. The exact nature of the methods to be employed and the workplan for the evaluation will be developed further with the evaluation team and will be captured in their inception note.

Qualifications of the Evaluation Team

The evaluation team will be comprised of two senior evaluators. The evaluation team will work closely with the SVBC project team and the Forest Conservation Programme, but is expected to have a clear independence from both and will include the following qualifications:

- At least ten years experience leading and conducting evaluations;
- The demonstrated ability to evaluate standard evaluation criteria such as relevance, effectiveness, efficiency and sustainability in a manner useful to the evaluation's client
- Experience with an action learning approach to conservation programmes;
- Experience in reviewing conservation programmes, and in this case, experience in understanding the role of governance and forest issues in South America, Africa and Asia;
- Ability to communicate orally and in writing in English. French and Spanish language skills would be a desirable asset.

The evaluation team will be supplemented by an IUCN Young Professional and the evaluation team will therefore have responsibility for integrating and mentoring this individual into the evaluation process.

Schedule and Deliverables

The proposed schedule has the following milestones:

- Finalization of the Terms of Reference (mid-May)
- Engagement of the Evaluation Team and preparation of the inception note and workplan (end-May)
- Data collection and field visits (June-July)
- Report writing and submission of the draft report (mid-August)
- Incorporation of comments and submission of the final report (end-August)
- Presentation and discussion of the findings and recommendations during a meeting to an audience of EC and IUCN officials and selected others in Brussels (September)

Annex 2. Inception Note with Evaluation Matrix and Work Plan

Inception Note

	implementation arrangements (including partnerships) contributed to the realization of the objective and desired results?		partnerships and their contribution	documents
5. Sustainability	5.1 Are there any indications that arrangements built by the project will be maintained in the future?		Degree of stakeholder support for these arrangements Degree to which these arrangements respond to stakeholder needs & interests Degree of financial commitment to sustain the arrangements	Interviews with stakeholders
6. Impact	6.1 Are there indications that the arrangements are sufficient and adequate to contribute to improved forest governance?	6.1.1 Do the arrangements promote improved forest management (sustainability and equitability)?	Degree to which the stakeholders are satisfied with process and the extent to which stakeholders have documented what good governance looks like. Degree to which the arrangements respond to the assessments.	Interviews and assessments & desk study
	6.2 Are there indications that stakeholders who were involved in unsustainable (or illegal) practices have changed knowledge, attitudes or behaviour positively?		Perceptions in the project environment	'watchdogs' case studies, stakeholder interviews
	6.3 to what extent are the lessons learned applicable, disseminated and used in and beyond the project?	(communications, including to the EC)	Degree of uptake of lessons in international processes and institutions	Interviews with international organisations, desk studies,

Annex 3. Key documents

Arthur, E. & Kyeretwie Opoku. 2007. Strengthening Voices for Better Choices. Ghana Country Assessment Report. (77 pp).
Description of the Action. “Strengthening Voices for Better Choices: Enhancing Forest Governance in Six Key Tropical Forest Countries in Asia, Africa and South America”.

Millikan, B.H. 2009. Forests, public policy and governance in the Brazilian Amazon. Assessment Report to the IUCN as a contribution to the Global Forest Governance Project: Strengthening Voices for Better Choices (84 pp.)
Mkwizu, Y. and S. Milledge (2008), Can participatory forest management assist with local level forest governance? The Arc Journal, Issue 21, Tanzania
Moore, P., Greiber, T. and Baig S. (2009), Global synthesis of Strengthening Voices for Better Choices country assessments, IUCN
Mwashiuya, E.T. (2007), Training in legal issues pertaining to community control of natural resources, Rufiji district, a consultant report
Mwashiuya, E.T. (2007), Summary of laws and policies that govern land and natural resources in Tanzania, Land, Forest, Wildlife, Fisheries, Environment & By-Law Making Process, Dar es Salaam
SVBC IUCN FLEG Project in Ghana. 2006. Community Forestry and sustainable forest management. Myth or reality. Sharing experiences on community forestry in Ghana. Proceedings IUCN Workshop on making forest community practices an effective tool for sustainable forest management. Akyawkroom, June 2006.
UICN. 2009. Agenda Multisetorial Da Produção Madeirera Empresarial. (15 pp).
Wintle, S. (2006), Communications Strategy, Global Forest Governance Project: Strengthening Voices for Better Choices, Sri Lanka.

Ghana

Adewale Adeleke Yekini	SVBC Country Coordinator, IUCN Ghana Project Office
Samuel Kofi Nyame	Project Coordinator, IUCN Ghana Project Office
Chris Beeko	VPA Coordinator, Forest Commission of Ghana
Dr. Richard Gyimah	VPA Secretariat, VLTP Project Analyst, Forest Commission of Ghana
David Guba Kpelle	Forest Instrument project; GFTN, Forest Commission of Ghana
Isaac Apetorgbor	District Forestry Manager, Forest Services Division
Sete Kadoudu	Deputy Forestry Manager, Forest Services Division
Alex B. Asare	RMSC, Forest Commission of Ghana,
Mrs Konadu Pokuua	RMSC, Forest Commission of Ghana,
Awuan Ian Edward	RMSC, Forest Commission of Ghana,
Kyeretwie Opoku	Coordinator, member Forestwatch Ghana, Civic Response
Emelia Arthur	Member of the Forest Watch Management Committee, Forest Watch, Ghana
Rebecca Dottey	Former Coordinator, Forest Watch, Ghana
Ama Kudom-Agyemang	Freelance environmental communicator
Albert Katako	Programme Coordinator Forest and Natural Resources, Care International
K. Samuel Nketiah	Head of Tropenbos programme in Ghana, Tropenbos International
Alex Dadzie	Vice President Ghana Timber Association
Clare Brogan	Consultant, EC NREG Consultant, FRR
Ton van der Zon	Environment and Water Advisor, Royal Netherlands Embassy

DRC

Joel Kiyulu	, SVBC Country coordinator, Project office
Joseph Ipalaka	Member of Parliament, DRC
Rose Lisweya Bomeka	Secrétaire Exécutif, Gouvernement Provincial
Mr. Ngirima	Inspecteur de l'Agriculture de l' Equateur, Provincial Government
Norbert Endoto	Provincial Minister in charge with the environment (Equateur prov.)
Dr. A. L. Kalambayi wa Kabongo	Secrétaire Général à l'Environnement et la Conservation de la Nature
Alain Pénelon	FLEG technical assistant, FLEG COMIFAC
Iola Leal Riesco	Forest Governance Co-ordinator, FERN
Mari-Lise Du Preez	Researcher on forest and fisheries, SAIIA
Francoise Van de Ven	Secrétaire Générale, FIB , RDC
Timothée Alunga	Ingénieur de prospections, Ledya, private sector
Bokele Wanyoke	President CDV Nkalamba, Village representative
Norbert Itale	Administrateur Bikoro, Local government
Toma Lompese	Forest Engineer, ITB
Joseph Matonde	Priest, president of consultative Council/Bikoro
Jean-Baptiste Yoka Ibongu	Traditional Chief , Bikoro
Mamie Mboliaka Boongo	Women Representative Bikoro territory
Révérend Joseph Nzee Boika	Representative indigenous peoples Bikoro Village
Daniel Nkake	CDV President Itipo, Village
Ali Boufoud	Auditor, ITB Bikoro
Berger Bompema	Secrétaire Général REBOGOF, Provincial MSD structure
Willifried Ipaka Kebadio	Responsible for radio broadcast Mbandaka
Jean-Pierre Kundu	Directeur provincial, Fédération des Entreprises de Congo, Mbandaka
Arthur Mayambo	Ingénieur agronome, FAO, Mbandaka
S. Ngoyi, G. Kalongi, B. Nzemba	Representatives of Media in Kinshasa
François Kapa	Project facilitator FAO, Kinshasa
John Mafolo	Project facilitator, ICRAF Kinshasa
Bienvenue Ngoy	President, GTF
Alain Gallez	Attaché de la Coopération au développement, Belgian Embassy

E. Bola Bobonda Mamambe	Président National Union pour le Développement des Minorités (UDME/ONGH)

Tanzania

Abdalla Said Shah	Head of Tanzania Office, Senior Program Manager IUCN
Mkwizu Yassin Bakari	Program Officer Environment & Climate Change Norwegian Embassy
Leo Rwegasira	District Lands and Natural Resources Officer, Rufiji District Council, Tanzania

Sri Lanka

Shiranee Yasaratne	Former IUCN Country Representative, Sri Lanka
Karunaratne Nimal	SVBC Country coordinator
Prof Shantha K. Hennayake	Former IUCN SVBC Country coordinator, Sri Lanka

Viet Nam

Dr Vu Van Trieu	Country Representative, IUCN Viet Nam
Vu Minh Duc	Head Governance and Business Unit, IUCN Viet Nam
Ly Thi Minh Hai	Environmental Governance Officer, IUCN Viet Nam
Tran Manh Hung	National Coordinator Forest Governance Project, IUCN Viet Nam
Jake Brunner	Program Coordinator, IUCN Viet Nam
Tran Kim Long	Deputy Director ICD, MARD
Prof. Dr. Ngai	Director, DARD, Bac Kan province, MARD
Dr Ha Chu Chu	Director, ECO-ECO
Hoangh Thanh	Program Officer RD&EC sector, EC Delegation to Viet Nam
Nguyen Quang Tan	RECOT0 Pg/P a.RTfssoc7(at MACOT00 Pg/P 0.0029 Tw 10.02 0 0 10.02 70.86 405

forest policy and start a review on policy reform; communities would not be aware of governance matters.

In Tanzania the chambers of commerce and other representatives of the private sector would not have been engaged in meetings on forestry with the government. This was the first time they were consulted on FLEG.

Asked “what would be different in your country, had there been no IUCN or project”, external stakeholders frame the added value of IUCN to FLEGT processes as follows:

Some low and mid level people in a few departments in one Ministry have now idea about FLEGT (not the decision makers) and some directors of private companies; IUCN Bangkok presented information from Malaysia, Ghana and Indonesia in our workshops. Without IUCN that would not have happened.

IUCN made only small contributions. But what IUCN did, they did very well.

If IUCN had not done it, there would have been weaker local ownership and a weaker negotiation position.

In Ghana certain changes would not have been achieved so smoothly. The likelihood of reasonable decision making in forestry would have been less. IUCN had an impact on the

How stakeholders perceive the role and core capacities of IUCN in multi-stakeholder dialogues in forest governance processes

A multi-stakeholder dialogue can be held in different ways and with different degrees of participation. The role of government communication is different in the various phases of the policy cycle. Likewise a multi-stakeholder dialogue in a pre-negotiation phase of a VPA can be very different from one during the negotiation phase. In the latter the government always is the official coordinator, convenor and organizer. The role of a facilitator in a multi-stakeholder dialogue therefore can have many faces depending on the phase, the modality of dialogue the government has opted for and the socio-political context in the country. As one respondent commented:

The atmosphere in the country, our culture of democracy, our tolerance for opposing views, the role of the media, the stage of our forest policy realizi

Using experiences with improving governance in 6 countries to draw through exchange lessons learned for the global level (the total is more than the sum of the parts)

FLEGT awareness raising.

How stakeholders perceive the lessons learnt from the project

Questions on lessons learnt are apparently understood very differently between stakeholders. Respondents may refer to their own learning, to the learning of other stakeholders, to the findings of studies, to messages the project wants to deliver, to the achievements of the projects or to recommendations they want to promote.

Several IUCN staff consider that stakeholders learnt a lot from multi-stakeholder dialogues:

> *Through multi-stakeholder dialogues governments realize that the stick is not always needed. Government understands that for law enforcement they need public support and the right enabling conditions.*
>
> *Private sector now knows more about the context the operate in; they have a more positive attitude towards the law and now follow the procedures.*
>
> *Communities know about the law and forest management.*

Others internal stakeholders explain lessons learnt from the project on MSD or FG:

> *Change in attitude takes more time. Preparation and selection of leaders of stakeholder groups are important.*
>
> *MSDS take a long time and have their own dynamics, there is a need to work on concrete milestones.*
>
> *Negotiation between government and private sector alone does not bring good solutions.*
>
> *You need to build capacities in communities to get their voice heard.*
>
> *Reforms in the countries are ongoing but statutory law has major flaws, often there are clashes with customary law and the institutional framework is often confusing and weak.*

IUCN staff also identify lessons learnt for similar projects, which to some extent overlap with the next question (what should be done differently next time?)

> *Need for planning, communication, more field activities to influence policy, more community forestry…*
>
> *IUCN is weak in relation management, advocacy and facilitation; policy decision making is still a black box for us, especially in our country"*
>
> *You should have a link with the local level when dealing with national FLEGT processes".*

Several external stakeholders explain what lessons can be learnt or were learnt by themselves on MSD or FG:

> *Space for discussion is key although it can take time; critics are very valuable and useful (both positive and negative), it makes us more humble, help us correcting our mistakes and helping others correcting their own mistakes.*
>
> *It pays to have stakeholders involved.*
>
> *The process is unpredictable. A mono-strategy would be ineffective.*
>
> *It is important to recognize that all stakeholders matter.*
>
> *Set out clear rules of the game right from the start.*

There is a new concept: sharing benefits not losing them because of illegal activities.

Forest governance needs MSDS: it creates relationships, trust, understanding, empathy, credibility. It engages communities. It builds capacity and support in society.

Forest companies have to make social responsibility contracts, which is a benefit for the local people.

Others explain what lessons can be learnt for conducting similar projects:

Need to clarify the expectations in the beginning.

It is not always easy to implement a multi-country project.

Recognize the importance of your partners, once they are recognized as important they support you.

Project manager from the beginning has surrounded himself with a group of key leaders from major stakeholder groups. This is vital for the process.

It is important to identify the right individual as project coordinator; and give him the time.

Don't impose your ideas, the Government should feel it is the author of the good ideas we have suggested to him.

Build partnership with institutions having the same philosophy.

Money: Brazil is much more expensive than Ghana or Viet Nam.

Work phase by phase (but do not plan for several years).

IUCN should not claim ownership of multi-stakeholder dialogues.

IUCN should explain better its role and position. It should serve and support but leave the ownership with the government.

Allow for time and resources.

Networking competences of staff is important (science is not enough).

It is easier to work on concrete issues (for example sustainable purchasing).

Sometimes the answer consists of positive or negative judgements on the project:

IUCN has been clever at using their resources quite flexibly to have involvement in places where it is really needed.

People in the villages are aware that the forest companies are not their enemies. There is more control over the administration, more transparency on where the collected money flow to.

There is more willingness to rethink policy statements taking into account better the realities on the ground, the perceptions of people.

NGOs had to find a new role with the new government, we improved their capacities of analysis and ability to make proposals.

Governance means different things to different people especially with regard to tenure rights. That has not been addressed, as too political.

The Regional Office has important human resources, not sufficiently used.

Less isolation is demanded by stakeholders at different levels including the EC:

Involve all stakeholders.

IUCN should communicate better with us; invite us to project meetings and brainstorm more with us.

IUCN should not work in isolation, it should seek strategic alliances.

Strategies should be designed with partners.

IUCN should not work in isolation and do everything alone.

Do joint fact finding as part of MSD and not through consultant reports.

Although this does not answer the question many external stakeholders, mainly beneficiaries, respond to it by expressing their wish for a continuation of the project:

Continuation of the activities of IUCN is required.

The process needs a long term support, we are just in the beginning of the harvest (the results were obtained in the last period, the outcome would be lost is the project stops.

Time is needed for reaching the objectives. This project cannot finish yet.

We are on the good way now, but before leaving people have to be prepared on the next phase. People have to be capable to take over. Most projects stop with the contract and people are not yet ready.

This was a pilot study that needed to be continued and followed up. There are new initiatives but without them the project would not have been sustainable.

The wish for continuation is often associated with a wish for more budget, a broader scope and more action (*"More training is required")* notably on capacity building and training. However the demand is also on quality:

Capacity building should be more systematic (need assessment, annual plan, selection of participants…).

Additional themes are sometimes recommended, some at local (charcoal production risks in DRC) other are more global or general (REDD, environmental services and non-wood products, markets abroad).

Finally some external stakeholders wish more focus on communities and field work:
IUCN should support those who live far away in the forest.

Focus more on the grass roots level, engage communities more concerning issues as land use, and benefit sharing.

SVBC was too ambitious, IUCN should do case studies on governance on the ground as evidence for policies.

Annex 6. Comments and guidance on problem trees

The SVBC overall log frame is not explicitly based on a problem tree or any other assessment of the specific situation in the six countries. Country-specific problem trees have nevertheless been prepared later on as the foundations for country-specific log frames. Although this can be considered as a valuable improvement those problem trees still show some logical weaknesses:

- The approach does not fully prevent from the “circular rationale” consisting of justifying a project by the lack of the solutions it proposes: this happens with the many problems formulated as “lack of…” or with problem trees built around a “central” problem identified at the beginning as the target of the future project.
- Therefore a “tree” shape (with one single “trunk”) is maintained, focusing on a central problem identified in advance, ignoring the potential direct links between “roots” and “branches”.
- The problem tree in Ghana includes a contradiction that is frequent in FLEG issues: it both considers that illegal practices are a problem and that the law is not adequate.
- Problem trees also include very generic problems (for example “The policy and legal framework in Viet Nam for forest management is not sufficiently and effectively implemented”) which do not adequately show the precise causal links between their causes and consequences.
- All arrows do not reflect a cause-effect link or linking overlapping problems (e.g. Sri Lanka).

Properly done problem trees can be very valuable tools for project preparation (including for a participatory design of the project) but also for the type of assessments that were prepared under

Annex 7. Comments and guidance on logical framework

1. Unique or cascading log frame(s)

A project should be based on a unique logical framework. If the project is complex and has several components each component can have its own log frame but it should have an explicit link with the overall one: the specific objective of the component log frame should exactly correspond to an expected result of the overall one. And there should be no implicit log frames or objectives run in parallel.

In SVBC there were country specific log frames disconnected from the overall one and parallel objectives which were not reflected in the log frames, for example “strengthening voices” (as reflected in the title), learning lessons of broad applicability promoting the “ETPA” concept (equity, transparency, participation and action), tripartite approach and broad forest governance (beyond the focus on legality) as reflected in project documents or possibly positioning IUCN as a key global actor in forest governance reforms (as suggested by the geographical coverage of the project).

With different and disconnected log frames (explicit or implicit) SVBC is a project difficult to understand, to manage and to evaluate. The main expected benefits from log frames that is to provide a common understanding of the project rationale and a single tool for monitoring and evaluation, are lost.

The table below (at the end of the annex) compares the project log frames

2. Logical links and hierarchy between objectives

All objectives should be included in the logical framework and logically linked with a unique specific objective to be achieved by the end of the project. The specific objective should represent one improved situation. Other objectives should either justify the specific objective (be a consequence of it and therefore considered as “overall objectives” which the project contributes to) or be intermediary steps towards it (be causes of the specific objective, products of the activities and considered as “expected results”).

In the project these rules were not fully respected:
As explained here above there were several explicit or implicit log frames;
The specific objective of the overall log frame in fact is 6-fold as it represents 6 improved situations in different countries, pursued in parallel;
The indicator of the specific objective includes a target to be reached after the project (while per definition the specific objective should be achieved by the end of the project).
Because the outcomes of the project are very unpredictable and out of control due to the dependence on participatory processes, the “arrangements” referred to in the purpose tend in fact to have a status of overall objective;
A part of Result 5 contributes directly to the overall objective without contributing to the specific objective;
Expected results of the overall log frame are not all clearly contributing to the purpose and therefore tended to be considered as additional objectives of the same level (i.e. objectives to be pursued even without contributing to the specific objective).

This contributes to reducing the added value of having a logical framework and makes the project difficult to understand, to manage with efficiency and to evaluate

3. Links between expected results

Result 2: New and innovative approaches to overcoming the obstacles to good forest governance pilot tested and assessed.	The contribution to the purpose is not explicit; therefore R2 tend to justify activities at local level that were not all contributing to the purpose (for example support to the implementation of Knuckles management plan in Sri Lanka, training on mushroom cultivation and bee keeping in Ghana). The reason why approaches should be innovative is not clear.
Result 3: Selected representatives from government, civil society and the private sector have enhanced skills and knowledge which enable them to participate more effectively in the development and implementation of forest governance reforms	A very "open" result making room for capacity building before the needs have been assessed.
Result 4: Awareness of, and commitment to, FLEG processes and action increased and sustained.	The logical link with the purpose is unclear. R4 is not necessarily relevant in all six countries but was considered in all countries.
Result 5: The lessons learned from the project's experiences are effectively captured, analysed and disseminated at the local, national, regional and global levels.	Dissemination at regional and global levels does not contribute to the purpose but contributes directly to the overall objective. If the six countries (referred to in the purpose) have been selected in order to learn lessons to be disseminated at regional and global level (referred to R5) there is an inversion in the hierarchy between ends and means.

4. Objectively verifiable indicators

The log frames should identify clear and verifiable targets. Indicators and sources of verification should be defined in order to provide a concrete description of the expected achievements and demonstrate that it will be possible to testify to their achievements. Indicators should be defined at the right level; therefore indicators of a particular result should not reflect its causes or consequences.

In SVBC the 2 last objectively verifiable indicators for Result 3 reflect consequences of Result 3 and the objectively verifiable indicators for Result 4 reflect the actions contributing to Result 4. In fact the 5 expected results of the overall log frame include steps to define (Result 1), implement (Result 2) and evaluate (Result 5) actions. This suggests that the project had to define its own targets when pursuing them. This is related to some confusion between inputs and expected outputs: the assessments of problems to be solved - the studies referred to in Result 1 - and participation are both parts of the methods and of the products of the project. Moreover several country specific log frames have no clear and qTc -0.00y5cothe objectively verifiable indicatng

Comparison between project log frames

Colours tend to track similarities between country log frames and the overall one.

	Overall Project	Brazil	Ghana	DR Congo	Tanzania	Sri Lanka	Sri Lanka local	Viet Nam
Overall Objective	Forest							

	Overall Project		Ghana	DR Congo	Tanzania	Sri Lanka	Sri Lanka local	Viet Nam
	forest countries, and enjoy the active support of government, civil society and the private sector.			equitable and transparent manner.				
Result 1	Policy, legal, institutional and economic obstacles to sustainable and equitable forest management identified in six priority countries.	l and ment s at orest nies and unities proved	Adequate procedures for allocation of TUCs and management of forest resources agreed and implemented	Relevant in formations for adequate decision making on forest laws international policy (FLEG) and information market developments market to consult are available to local and national stakeholders.	Coordination mechanisms in place and used effectively among stakeholders working on Forest governance at national level and at local level	Policy, legal, institutional and economic obstacles to sustainable and equitable forest management identified	Institutional mechanism (including communication) are set up and operated for the community and landowner involvement in the management of KCZ	Stakeholder are better informed and aware about growing and changing market demand for timber of Viet Nam, including about policy, legal and economic issues
Result 2	New and innovative approaches to overcoming the obstacles to good forest governance pilot tested and assessed.	e social egments of e forest ector are rticulated and	Capacity to enforce forest law strengthened (R2a) organized					

	Overall Project	Brazil	Ghana	DR Congo	Tanzania	Sri Lanka	Sri Lanka local	Viet Nam
Result 3	Selected representatives from government, civil society							

Annex 8. Differences between projects and programs

During the evaluation it became clear to the evaluators that not all internal stakeholders had a clear picture of the differences between projects and programs and the management consequences of these differences. From the wide range of information on project and programme management here a selection is made to clarify the differences.

Project
The whole idea of a project is so simple when it is boiled down yet, it is at the same time so broad and so all encompassing that it can be easy to become overwhelmed in the process of breaking down exactly what a project in fact is. To put it somewhat simply, a project refers specially to any short-term and or temporary task engagement or endeavour in which a particular and unique outcome. often in the form of a specific product and or service is generated or created. This is usually done via the utilization or a predetermined project management team and run by a designated project management team leader. It also involves the utilization of a number of specific and particular supplemental concepts and utilizations including project staff, project scheduling, project calendars, project life cycles, etc. In general, a project has a fixed time and a fixed goal and multiple projects may run at the same time

Program
The concept of program refers specifically to the series, listing, or group of those similarly structured and or otherwise interrelated projects that when the decision is made to coordinate the management of all them in a coordinated way will garner benefits and improved ability to maintain control as opposed to if the management of each of these took place on a project by project basis. Some tangible examples of instances in which it is beneficial to group management of certain projects within the overall scope is when it comes to organization and maximum efficiency in regards to staffing. It is far more efficient to distribute staff across a number of independent projects yet within one umbrella program than to attempt to coordinate staffing across all projects independently. It also helps to better utilize office resources and other supply materials. Specific enumerated program elements may consist of not only large scope work-related items, but also in regards to elements outside of scope of the discrete projects that make up the program.

Difference between project and program management:
Project management is the act of creating plans and managing resources in order to accomplish a project. A project is a scheduled undertaking for the purpose of creating a product or service or an improved situation. Program management, on the other hand, is the act of creating and managing multiple projects, most of the projects are usually related to one another. Project management is usually short-lived with specific time constraints while program management is more an ongoing process in order to achieve the goals and objectives. The job of a project manager usually involves working on finite projects or objectives. The program manager works more often with strategy.
A project management team works to identify the triple constraint of time, scope and cost of a project. Then, they plan and report on the delivery of the project. While the project is being accomplished the triple constraint is reviewed. When the project is closed, the project management team will review and report on the accomplishment of the project. A program management team works to identify the mission, projects to be accomplish

)]TJ0.0001etTc -sh

ussitu

Annex 9. How to organize the capturing of implicit knowledge

To capture implicit knowledge a different methodology

Annex 10. Lessons Learnt on Multi-stakeholder Dialogues in Ghana

The description below is based on interviews in Ghana with relevant internal and external stakeholders and the results are validated afterwards by the country coordinator and the Ghana VPA coordinator.

a- The organization of the process

The real dialogue between stakeholders took place in the VPA steering committee that since 2006

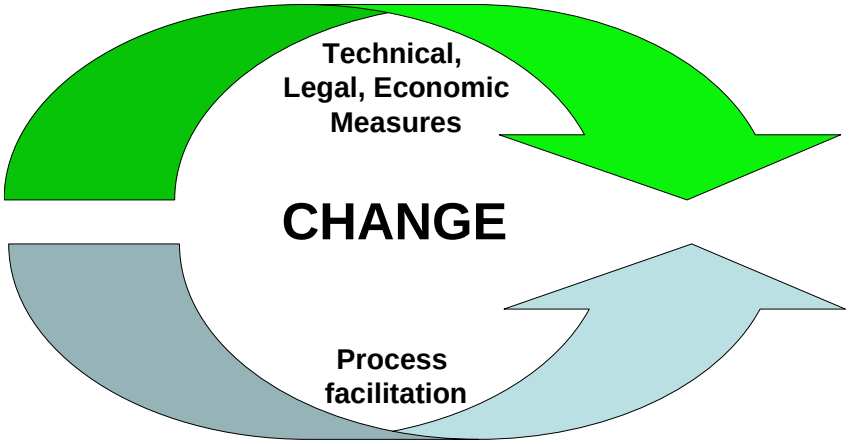

b- Lessons learnt from the process

How does a multi-stakeholder dialogue relate to the policy process? In a democratic open society one always needs a form of multi-stakeholder dialogue for major policy change affecting a whole sector of society. There are many different forms, ranging from one- or two-way information campaigns to joint policy planning and formulation exercises. A well tailored and managed stakeholder process always helps, but no dialogue can take over role of the government. In a policy process the technical, legal and economic decisions are taken by the government. These decisions are so to say the different parts of the engine of the policy decision making. The multi-stakeholder process provides the oil that makes that engine work.f8603Mohmanm the process of eneeneenee5aged stakl-0z0.0002/TToj6(g a)]T1f kl-

government. It changed the Roadmap for the VPA and ToR for the consultations: IUCN became observer and civil society got a seat and later a second one on the steering committee. The government started to change its attitude towards civil society and its contributions and vice versa.

c. Milestones and tipping point in the Ghana VPA Multi Stakeholder Dialogue

In interviews with some of the key stakeholders the highlights of stakeholder consultation process of the Ghana VPA process were identified. With the colour red are the kick off and tipping point in the

Policy focus Actors	2005 FLEGT	2006 Negotiations 1	2007 Negotiations 2	2008 Negotiations 3	2009 VPA
		representation widened beyond Forest watch constituencies.	Committees.		gap between government and civil society
Civil Society	Awareness campaigns. Perceive government as their enemy.	Separate awareness raising, action research and capacity building activities Agenda setting for key issues	Expression of frustration with process in tripartite meeting meets with sympathy of EC. Civil society communiqué	Constructive approach in feedback to reports. Participation as observers in negotiation team. Consensus with stakeholders.	High degree of professionalism established Areas identified where they can work with government
Traditional Authorities			IUCN information meetings on FLEG and VPA. Communiqué National House of Chiefs	Constructive approach in feedback to reports. Consensus with stakeholders.	Awareness of the external drivers of establish

Practical Lessons learnt on MSD in Ghana

Interviews with key stakeholders in Ghana brought to light a wealth of very practical lessons learnt that had been so far mostly 'implicit' knowledge. The practical lessons can be clustered on learning about the process, the stakeholders or partners in the dialogue and the role of IUCN.

The process	The partners	The role of the IUCN
The issue is highly political at all levels with high stakes of members of elite groups, who are not directly engaged in the MSD The objective – consensus – and the rules of the game have to be clear from the start Often the attitude of the government is not very receptive for a participatory approach Consensus building is not a logical decision making process, mutual learning is key Ensure adequate time frame and resources The process has various phases: networking; relationship building; information sharing; joint research; formulation of positions (communiqués); consensus building, negotiations. Relations building is time consuming Define role of IUCN in process and in implementation of VPA Mix of formal and informal interventions and meetings; much behind the scenes work Make a communication strategy to inform and engage partners in the process and support their		

		be prepared to take the blame

Annex 12. Video proposal on lessons learnt for Ghana

Bringing the voices to the table
Lessons learned of the VPA MSD in Ghana
First ideas for a 6 minute video

Target audience
IUCN colleagues
Forestry community world wide
European Commission, Bilateral and Multilateral donors

Objectives
Show the added value of multi-stakeholder dialogue in forest governance, the lessons learned in Ghana and the role IUCN can play. For example choose from the following learning points:

What makes participation meaningful? The tipping point is the VPA MSD process was the tripartite meeting, organized by IUCN with EC after the second negotiation round in Ghana in 2007 when civil society brought to the attention of the EC that the consultation process as started since 2005 was far from satisfactory. The EC delegation in response gave a strong signal to its counterparts that for them the VPA must be based on serious consultations and support from national stakeholders. This external 'pressure' triggered the change in the government's attitude; it changed the Roadmap for the VPA and ToR for the consultations: IUCN became observer and civil society got a seat and later a second one on the steering committee. The government started to change its attitude towards civil society and its contributions and vice versa. Mutual recognition and respect became the basis for more meaningful interaction and participation in the process.

Who sits at the table? The second lesson learned is that representatives of all stakeholders should be engaged in a meaningful way and that the way to do so is to actively engage them in the selection of their representatives in the VPA process. In Ghana in the beginning the government selected the representation of civil society that did not really work. Similarly not all stakeholders were engaged: not the communities, who have an interest in positive change nor members of the elite, who have high stakes in business as usual with regard to illegal logging. This indicates that there are still challenges in Ghana to create the conditions for the implementation of the VPA and for improved governance.

What is the character and structure of a multi-stakeholder dialogue? The third lesson is that a successful MSD is not a logical, rational and purely science-based process of decision making, but a process of involvement of stakeholders in government decision making based on mutual learning, recognizing the different interests and perspectives. Its value is not in fast decision making, but in creating involvement needed to improve policies in such a way that a basis for the support for their implementation is created. In Ghana the tripartite dialogue took place in the VPA steering committee and was formally facilitated by the VPA coordinator. IUCN took a mediating role in the discussions. IUCN did not facilitate the FLEG or VPA process. The multi-stakeholder dialogue in the VPA steering committee was based on input from separate consultations. IUCN played a key role in facilitating these consultations. The formal VPA decisions were taken in the negotiation process between government and the EC. Private sector and civil society had an observer status during those negotiations.

What does facilitation of MSD really mean? A fourth lesson is that facilitating an MSD is not the same as facilitating round tables with different stakeholder groups. Most of the work is behind the scene translating positions of groups in the language of other groups to create better understanding and clarifying interests. Sometimes translation has to be done literally, e.g. for the communities. Access to information is key condition to participate. IUCN played a key role in making knowledge flow effectively between key players, including the EC. Facilitation also includes strengthening of capacities of stakeholder groups. This should not be based on training needs assessments, but on articulating

the demand for new knowledge and skills needed for the next step in

potential benefits of empowering stakeholders in forest management, needs to be better explained and understood at the local levels so that its ultimate relevance to livelihood development and natural resource management is appreciated, perhaps through the use of case studies where improved governance results in demonstrated

		doubtful both they were late and did not really address key issues in perceptions, and misconceptions of primary audiences.	
	Intensify and accelerate targeted capacity building efforts in line with the detailed LFAs for each country component	Capacity building efforts have been intensified but their linkage to the	
